TRANSFORMING CUSTOMER JOURNEYS
Playbook

Journey Team Guide

Incubation

This playbook contains all the pieces and parts that make up our approach to transforming customer journeys. This is a living document and the latest version can be found on TCJ's Confluence site.

Last updated in May 2019

CIMB

How this module fits into overall TCJ Playbook

Transformation Design

Overall TCJ strategy
- 5-year roadmap
- Economics

Cross-journey elements
- Journey Team org blueprint and agile way of working
- Journey Team Model Office

Technology Enablement

Tech
- Target architecture
- DevOps
- Tech Execution Plan

Journey N

Retail CASA Journey

Commercial Lending Journey

Planning
- Understanding of business
- Map of sub-journeys
- As-is diagnostic of sub-journeys
- Assessment of potential impact
- Prioritization
- To-be journeys
- Delivery roadmap

Incubation
- Zero-based design
- Finalized product roadmap
- Backlog development
- OKRs and targets
- Squad onboarding

Waves
- MVP
- Test and learn
- Roll-out plan (Biz and Tech)

Transformation Management

TCJ organization and governance
- **Organization** of TCJ (e.g., Structure
- **Governance** within TCJ and **interactions and dependencies with the bank** (e.g., Decision making processes, decision making bodies)
- **Program management and value assurance** (e.g., PMO processes, value/performance management, dashboards)

Talent
- Recruiting targets and pipeline
- Onboarding
- Capability building
- Retention, career progression and management

Culture and change management

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

What this module covers

What are the outputs for each journey, and how should each journey operationalize itself?

- **Recap: Phases that each Journey Team undergoes**
- B1. Aligning the target strategy with customer vision
- B2. Defining delivery roadmap
- B3. Onboarding the team (i.e. Sprint 0)
- Translating this into a sprint plan

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

The journey transformation is delivered over three phases: Planning, Incubation and Waves

Detailed in this playbook

	2 months	2 months	4 waves x 3 months each	
Journey Phases	**A. Planning**	**B. Incubation**	**C. Waves**	
			Build and Pilot	Roll in and scale
Activity	▪ Initial analysis based on internal and external sources of insight ▪ Process diagnostic ▪ Revenue and cost baselining ▪ Identify and detailing of key interventions ▪ Refine bottom-up impact estimates ▪ Planning and road-mapping	▪ Build collective understanding of the current journey from customers perspective ▪ 'Zero based design' based on informed leadership choice ▪ Identify and validate the levers for change ▪ Business case definition backed with empirical data ▪ Planning and road-mapping	▪ Build the 'minimum viable solution' (tech or non-tech) ▪ Deploy, test and learn and iterate with customers ▪ Prepare to scale	▪ Roll in volume and people into the Lab ▪ New features and product improvements developed in agile way and released regularly ▪ IT industrialisation
Outcome	▪ Initial blueprint for prioritized journeys: – As-is journey, pain points/ opportunities – KPI definition & potential impact assessment – High-level implementation plan/ investments ▪ Final product roadmap with overall plan by waves ▪ Harmonized portfolio of initiatives (between TCJ and BAU) ▪ Target IT architecture ▪ High-level technology buildout plan	▪ High level target architecture and high level operations model ▪ Target state re-design of journey including principles and customer vision ▪ Roadmap of change ▪ Validation of hypothesis through customer insight / research ▪ The zero-based approach covers product, policy, and processes	▪ Evidence of new leadership behaviours / ways of working ▪ Validated learning on baseline benefits, feasibility and customer benefits	▪ Functioning journey with supporting technology ops model ▪ Ops model for moving from E2E to BAU ▪ Metrics and tracking ▪ Aligned leadership purpose

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

The Journey Planning Phase consists of 7 main elements

Key inputs

A Understanding of the business

1. **External lens:** Market trends, regulations
2. **Customer lens:** Customer segments, product offering, customer experience
3. **Internal lens:** Business financials, organization, technology, existing initiatives

Key outputs from transformation design

B Map of sub-journeys

1. Define customer segment and process
2. Define sub-journeys

C As-is diagnostic of sub-journeys

1. Map out as-is process and pain points for each sub-journey
2. Map out as-is tech architecture and deep-dive into systems

D Assessment of potential impact

1. Develop model to compile baseline
2. Model potential revenue uplift and cost reduction
3. Define metrics for Objective and Key Results

E Prioritization

1. Prioritize sub-journeys based on four criteria

F To-be journeys

1. Create to-be journey and key interventions
2. Create to-be architecture for prioritized sub-journey
3. Assess feasibility

G Delivery roadmap

1. Define final product roadmap with overall plan by waves
2. Define technology implementation roadmap
3. Align on harmonized portfolio of initiatives between TCJ and BAU

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

B. The Incubation phase translates the knowledge gained in the understanding phase to an implementation plan

Key workstreams	B1. Aligning the target strategy with customer vision	B2. Defining the delivery roadmap	B3. Onboarding the team, implementation and evaluation
Activities	▪ Workshops to define target customer experience journeys ▪ Interviews with experts to refine based on Zero Based Design ▪ Working sessions to generate target policies and IT architecture blueprint	▪ Rapid co-creation and ideation by the whole team (incl. product and ops) ▪ Test with experts ▪ Complete deliverable templates ▪ Iterate with stakeholder / experts ▪ Detail “front runner”	▪ Identify full Lab team, defining the hiring plan ▪ Workshops and communication to embed mind-sets required for success ▪ Secure required enablers ▪ Perform risk assessment ▪ Syndicate deliverables with stakeholders ▪ Seek governance approval
Deliverables	▪ Storyboards for customer proposition vision ▪ Target product description ▪ Target customer journey maps ▪ Design briefs ▪ Blueprint of future operational / org design ▪ Target IT architecture ▪ Target policies (incl. conduct/credit risk)	▪ Product roadmap incl. MVP, sub-journeys ▪ IT Development timeline, IT critical path, dependencies ▪ Operational and org trans-formation road-map (incl. KPI) ▪ Business case document ▪ Resource request ▪ List of risks and mitigations	▪ Business case document ▪ Quantitative estimates for baseline and target operational and financial KPIs ▪ Resource request ▪ Core team members onboarded and co- located ▪ Full role and headcount requirements, hiring plan ▪ Location, resources, testing environments available ▪ List of risks and mitigations

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Table of contents

What are the outputs for each journey, and how should each journey operationalize itself?

- Recap: Phases that each Journey Team undergoes
- **B1. Aligning the target strategy with customer vision**
- B2. Defining delivery roadmap
- B3. Onboarding the team (i.e. Sprint 0)
- Translating this into a sprint plan

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time

Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Staff the concept team - Team should have the necessary skills and domain knowledge to ideate towards defining mvp scope.

Preparation

- Identify skills needed for concept ideation and prototype validation
- Concept Sprint teams usually include facilitator / lead Designer, researchers, domain experts, prototype/developer etc. These roles will be 100% dedicated for this sprint
- Identify number of team members needed with each skill set
- Engage appropriate SMEs outside of team

Activities

- Discuss roles, team availability, and skill sets needed with staffing coordinator
- Understand constraints of identified skills and availability of team members when staffing different roles

Outcome

- Named team members with start dates are confirmed
- All core team members are dedicated and available for Concept Sprint

Best practices

- Teams are cross functional with required skills to develop concepts
- Has one dedicated Product Owner, Facilitator / Scrum Master, Design and Technology Lead
- Open space with whiteboards and wall space for posters, stickie boards etc

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Staff the concept team - The team: Concept focused

The cross functional Concept Team

- Fully dedicated team for two-week concept sprint : A design thinking led ideation and prototype validation process
- Intensive, collaborative working sessions including customer testing of prototypes, results in ‘seed’ of backlog for Sprint 0
- Empowered by a mandate to validate possible solutions to identified needs and pain points
- Staffed with 6-7 team members with relevant Design, subject matter, technical and market knowledge as necessary
- Led by an expert in facilitation and design thinking tools, often design and product staff

Key roles	Responsibilities
Facilitator 100%	Drives vision and strategy for the concept, ensuring the necessary business value and viability of solutions in line with the needs of the business
Design Lead 100%	Champion customer experience, helping the team create holistic experiences as well as visuals and drives customer and user testing. As needed may use: ▪ **Design Researcher** – Specialized designer who uses qualitative and quantitative methods to understand users, their context, and their needs ▪ **Experience Designer** – Translates user needs into solutions, in particular thinking about the product experience beyond just the application, screens, or digital concept ▪ **Visual Designer** – (if applicable) develop code, help with prototyping and testing designs with customers, bringing challenges to Tech Lead
Tech Lead 100%	Leads technical vision, thinking ahead and being innovative about solutions, while considering viability of solutions and available talent
Functional Support 20%-100%	Provide support for concept team to execute on mandate (e.g., understanding legalities, system or process complexity, specific customer or market insights, etc)

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Approach for the concept sprint: The Zero-Based Design process applies blue-sky thinking to re-imagine an ideal client experience

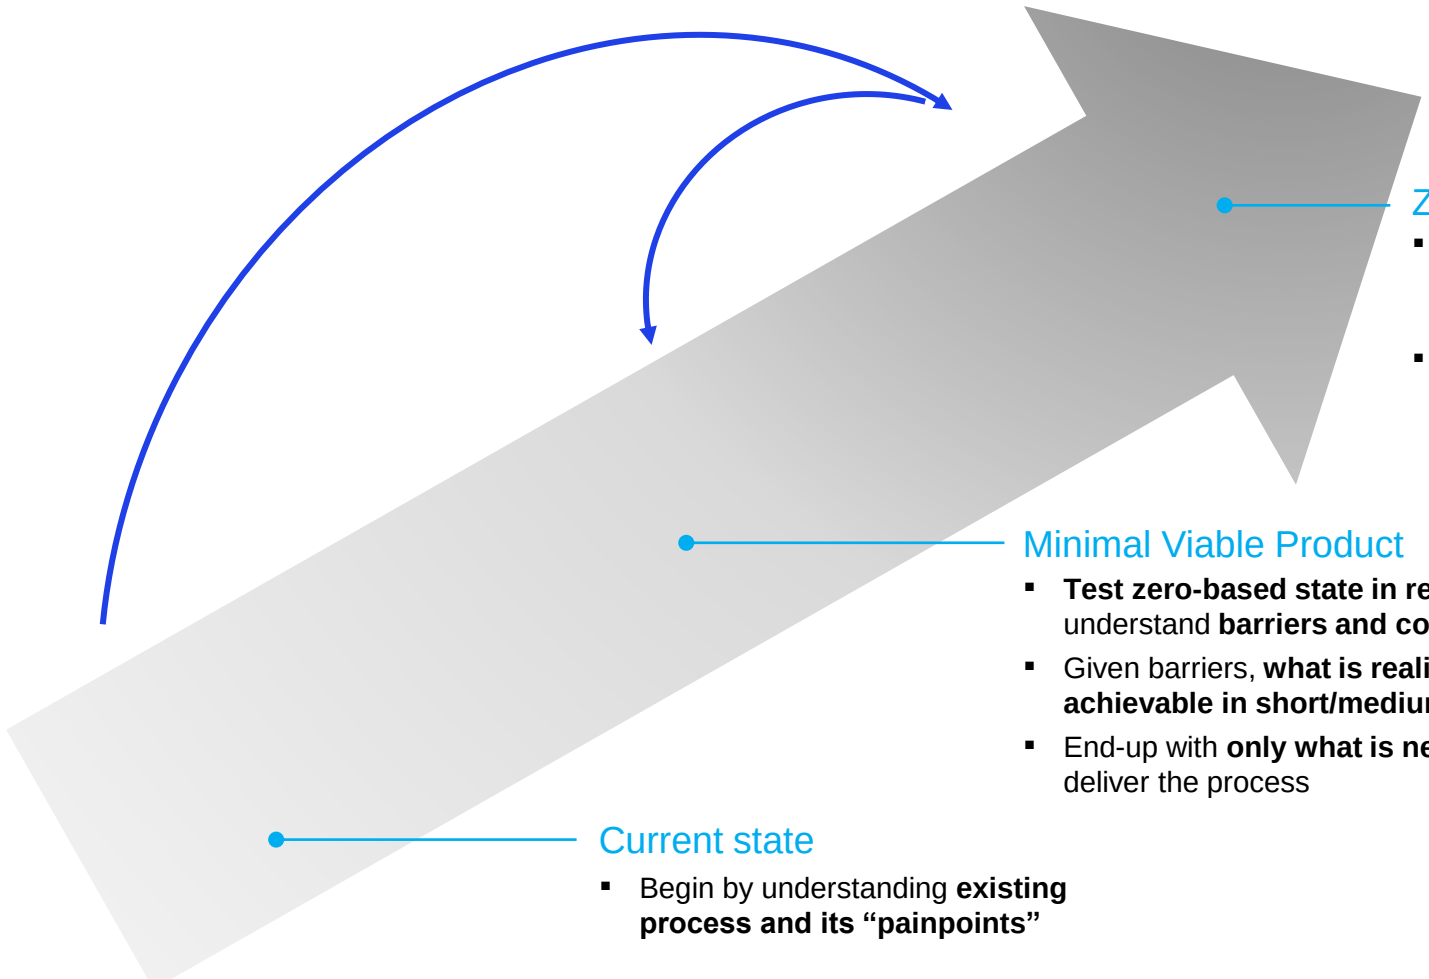

Zero-Based Design

- Starts with defining an **optimal "clean slate" vision**
- **E.g.,** our best people sit in a closed room designing **"What do we really need to deliver this"**

Minimal Viable Product

- **Test zero-based state in real-world and** understand **barriers and constraints**
- Given barriers, **what is realistically achievable in short/medium** period of time?
- End-up with **only what is necessary** to deliver the process

Current state

- Begin by understanding **existing process and its "painpoints"**

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

The Zero-Based Design process starts by understanding the current process and then re-imagining the ideal journey

	Details	Prep required	Responsible	Timing
Pre-work	1a **Understand the current state** ▪ Map the current process to understand: – Critical components of process – KPIs (e.g. volumes, turnover, acceptance rates)	▪ Walkthroughs of current processes ▪ SME interviews ▪ Key product data gathered	▪ Journey Team and Navigator	~ 1 week
	1b **Create template personas** ▪ Create personas to inspire ideal client journey (based on research data from marketing team and insights from contextual interviews) ▪ Leave blanks on personas to complete with broader team during ZBD	▪ Gather market/ segmentation data ▪ Hold contextual interviews	▪ Design	~ 1 week
Zero-Based Design	2 **Zero-Based Design workshop** ▪ Fill out template personas to inspire ideal client journey (prepped in advance) ▪ Complete empathy map to understand customer pain-points ▪ Ideate on features and map an ideal customer journey	▪ Template personas ▪ Understanding of current state process	▪ Journey Team and Design	1 day
Post-work	3 **Create initial sketches** ▪ Create initial hand-drawn concepts ▪ Refine ongoing design based on – Strategic business decisions – Design solution improvements – Tech development input	▪ Outputs from ZBD workshop	▪ Design, PO	2 days

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

1b. Create template personas

Personas are detailed profiles of user archetypes.
A persona embodies a variety of insights from research and analysis. They help to thread user-centered thinking throughout the design process.

These fictional profiles represents realistic and distinctive:

- User context
- Needs
- Pains
- Value and motivations

How to create personas

1. Gather research findings and group by theme
2. Identify patterns among the different user groups
3. Create persona representations using names, photos, icons, and quotes
   - Do they share similar characteristics?
   - Do they behave similarly?
   - Do they experience similar challenges?

4. Think carefully about how the personas behave and what pain points they go through in relation to the problem statement

5. Focus on the persona who is the highest priority, where solving their pain points would have the most impact. You will likely have many personas who will use your digital solution, but for MVP, focus on the highest impact persona(s)

6. Share persona(s) with other stakeholders

Why using persona?

- It inspires ideation
- It creates concrete memory versus abstraction
- It validate design decisions based on user needs, not personal preferences
- It provides reasoning for prioritization

Name

"Quote

"

Background

Age
Status
Occupation

VALUE

MOTIVATION

PAINS

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Persona examples

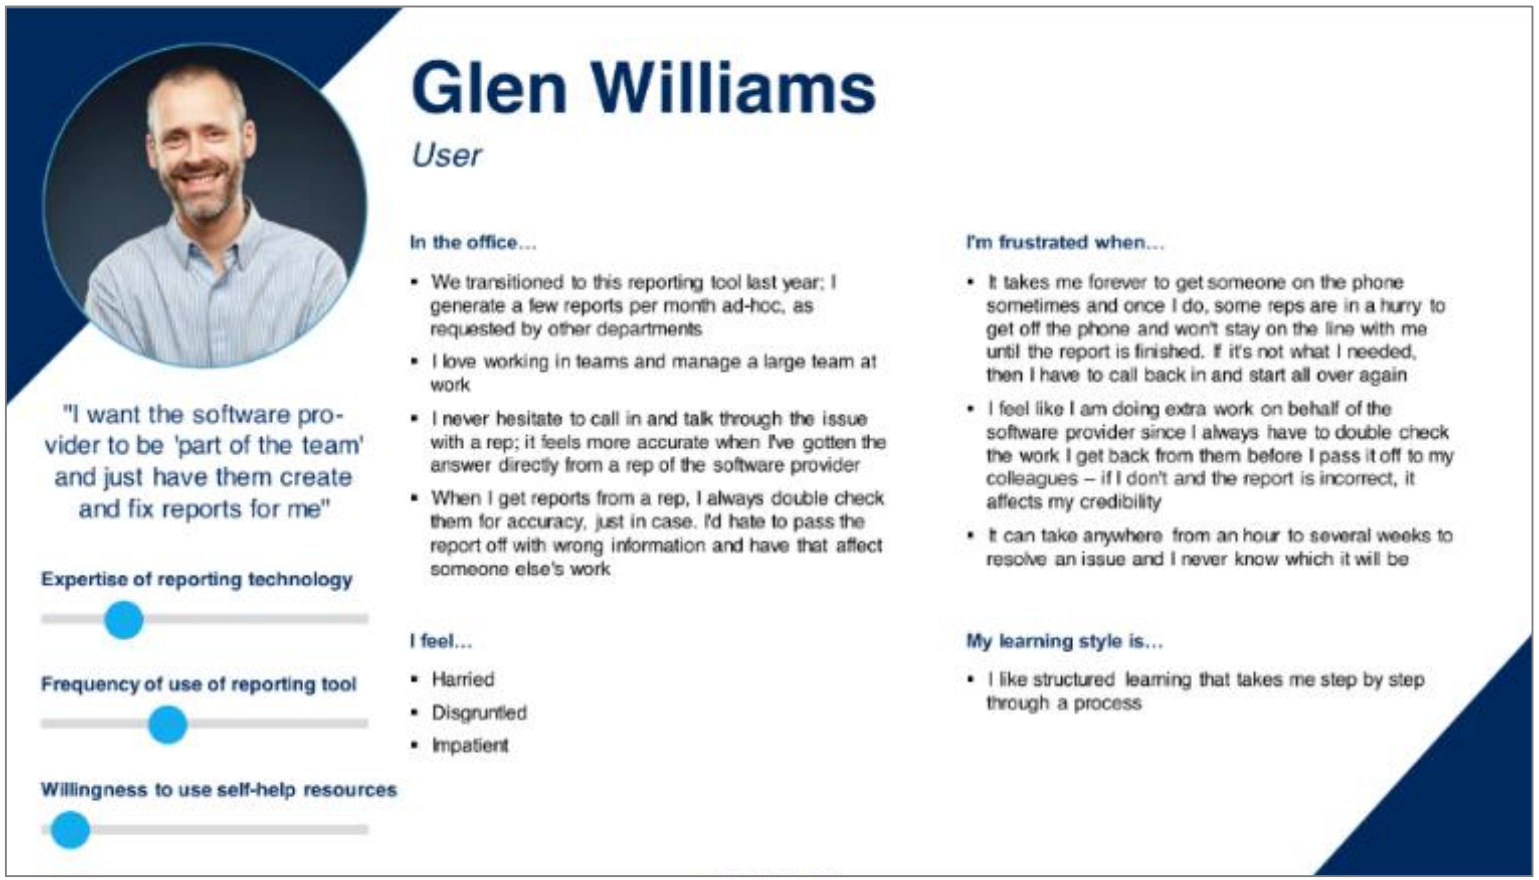

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Create journey map

Journey mapping narrates persona(s) interaction with a product/service. It focuses key events, pains and opportunities from each persona's unique perspective. It highlights which customer and issues your team is solving for

Why using journey mapping?

- It provides a holistic view of quantitative and qualitative data
- It forces emphasis on customer experience
- It create a shared language around current customer experience
- It helps to identify opportunity areas and pain points (ideal state journey)

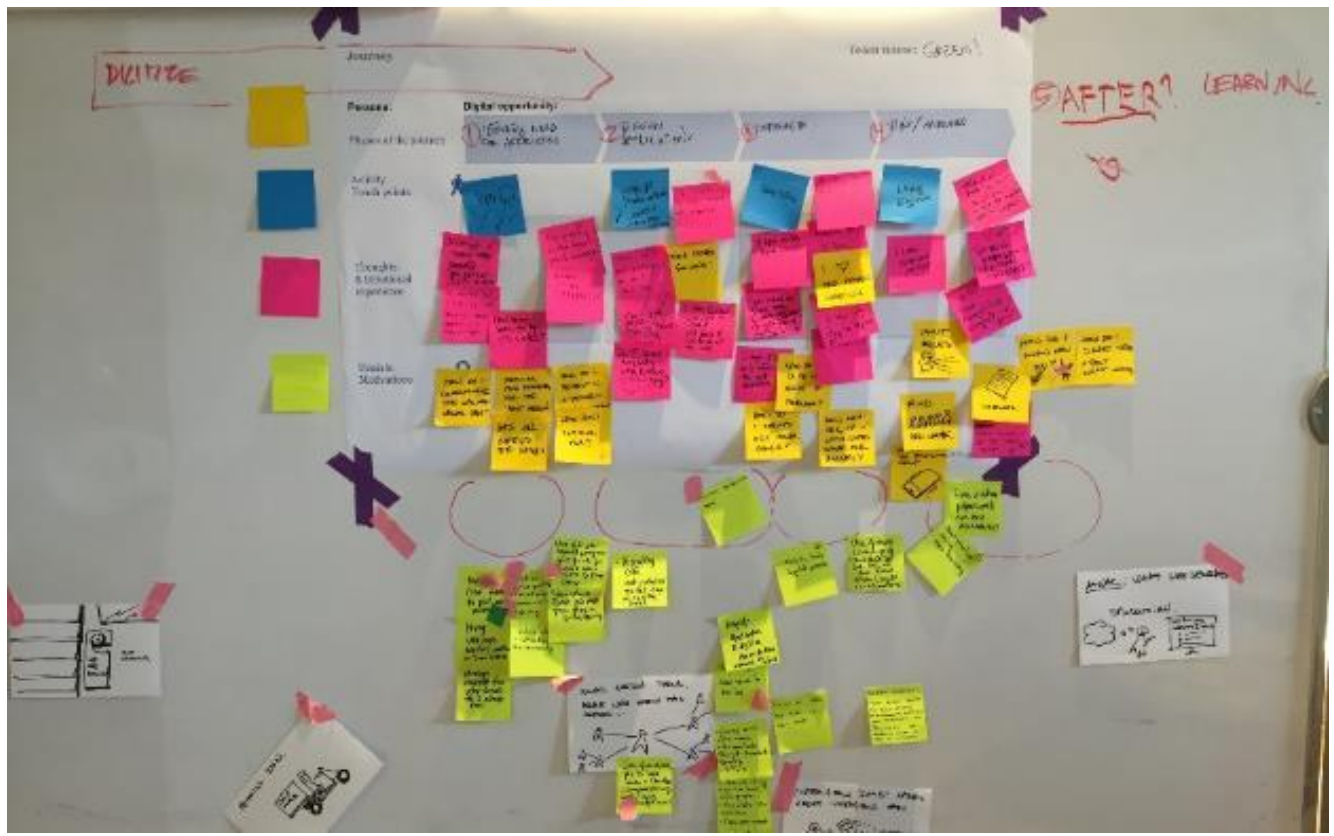

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Journey map template

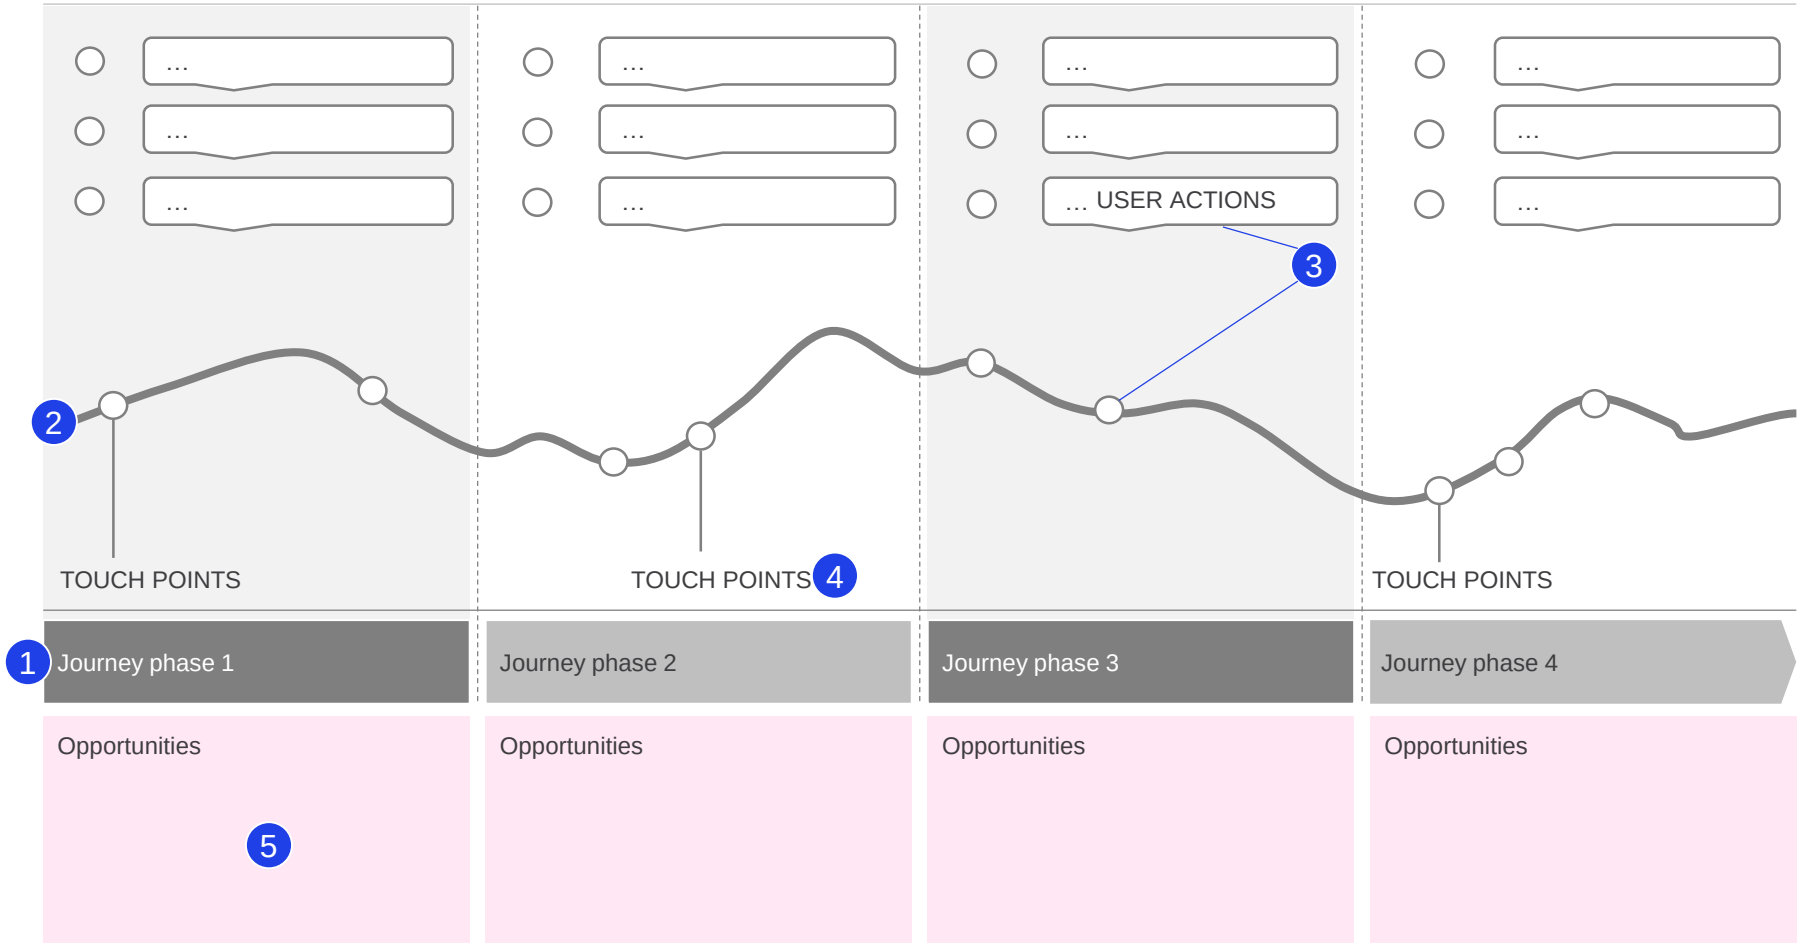

How to build a journey map

1. Journey phases

Identify the phases of the persona's journey - keep it simple and try to limit to key phases.

2. Emotional Experience

Captures the emotional lows and highs during a customer's interaction with a product/service. It usually highlights pain points and opportunity areas

3. User actions

Capture actions and steps users take to achieve their goal using the product/service

4. Touch points

Identify **activity touchpoints** the persona encounters (e.g., speaks to a person, visits a website, etc.) and write it in the touchpoint section.

5. Opportunity areas

Potential places to alter the course of a customer journey based on identifies high/low emotional experience throughout the journey

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Journey map example

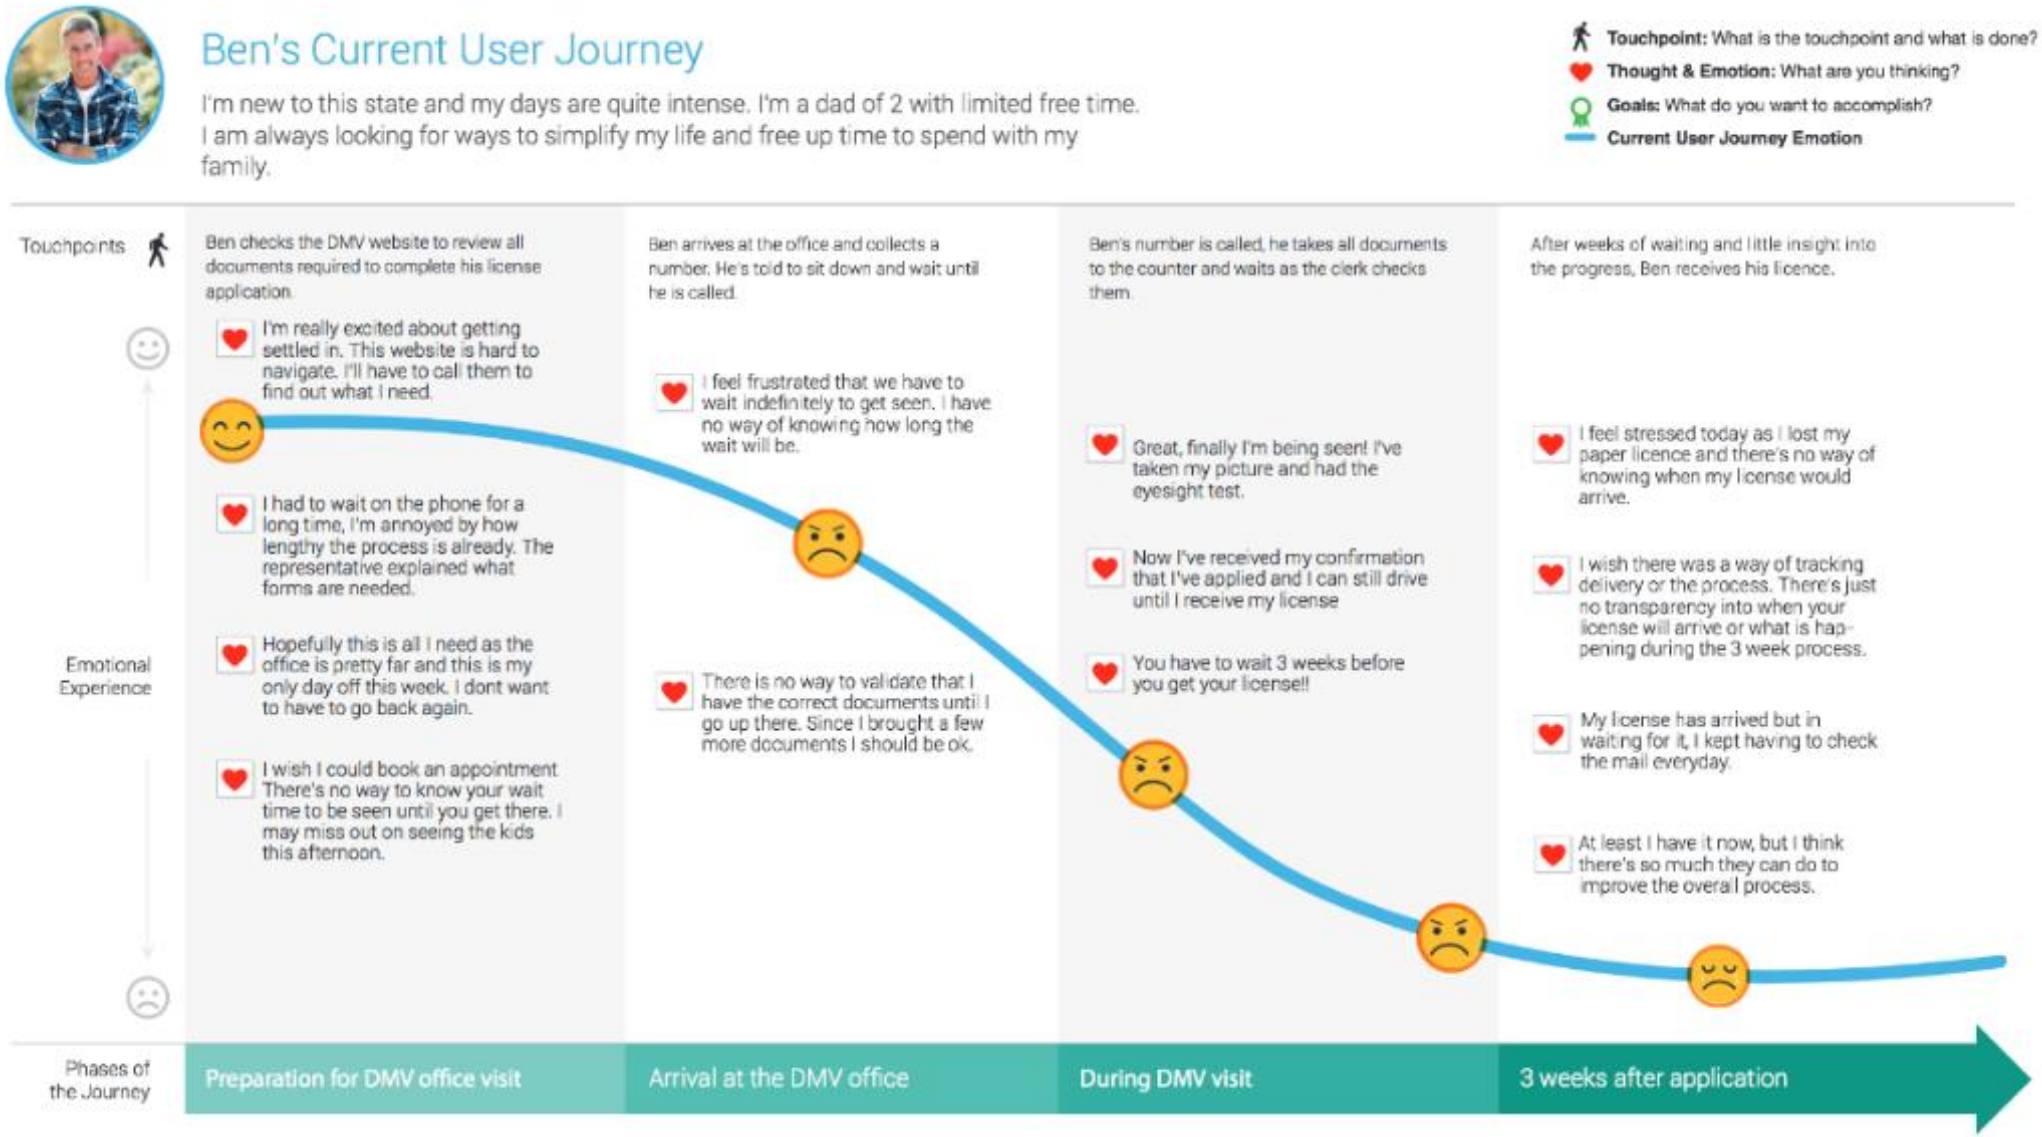

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Brainstorm ideas to solve customer pain points

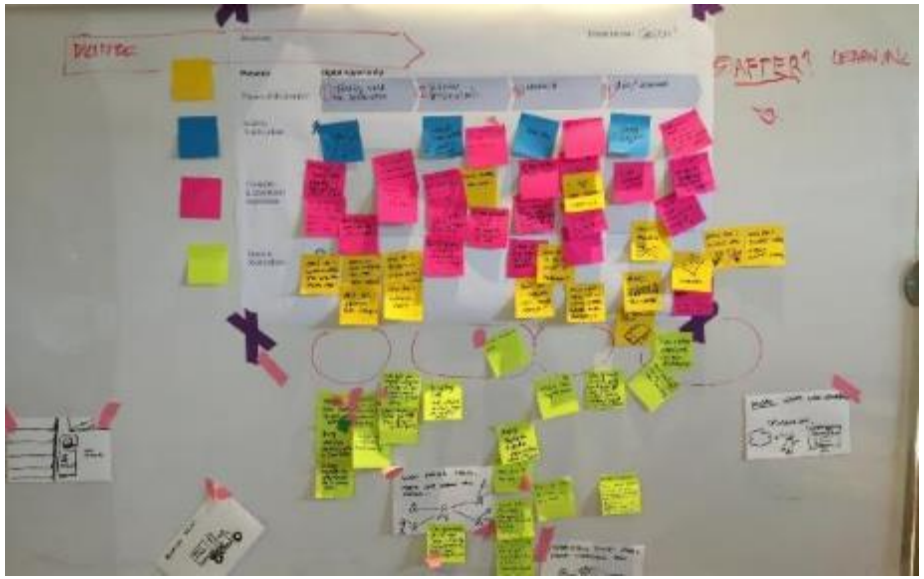

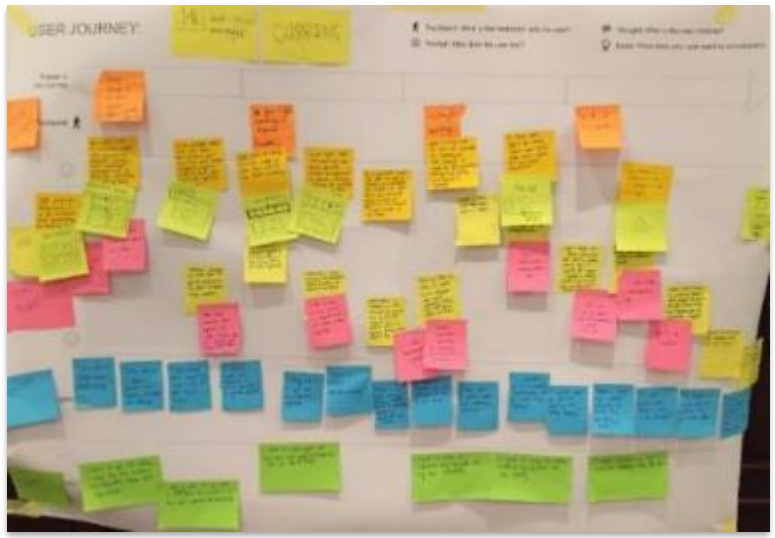

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Sketch and prioritize concepts

Step 1: Lightning ideation

Individually write or sketch concepts that solve the journey pain points

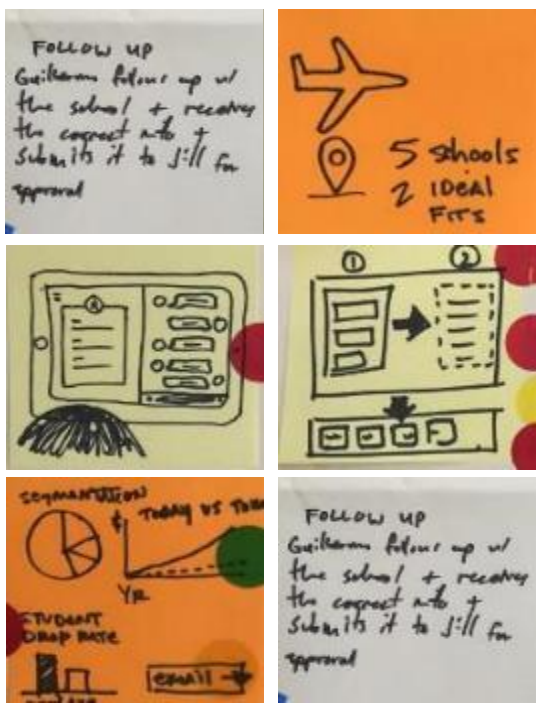

Step 2: Select Idea

One by one share the concepts with your team and select the most impactful to highlight

Step 3: Screen sequence

Create a storyline and sketched wireframes from one or more of the selected concepts

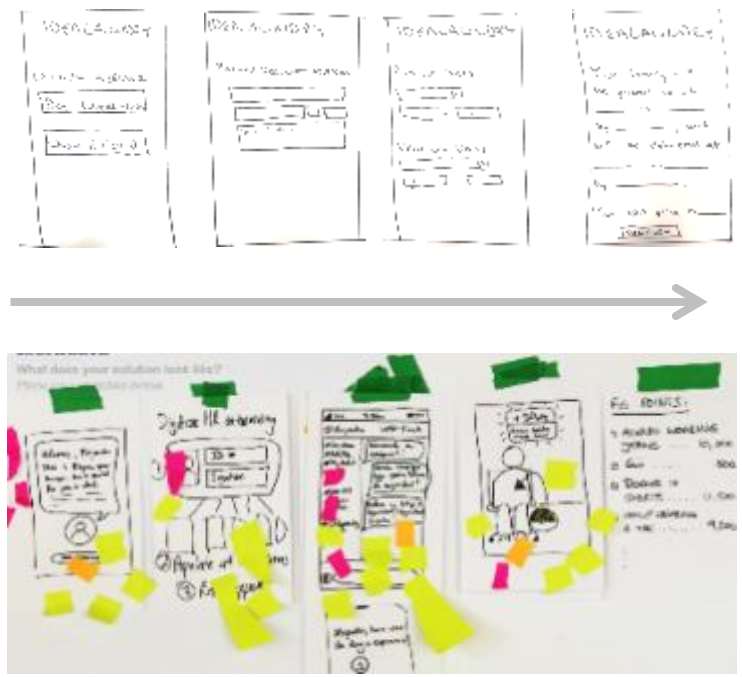

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Capture selected concepts for prototyping

Solution name

Painpoints:

What specific pain points does your solution solving for?

Benefits:

How does your solution benefit your persona?

Description

What are the key features of your solution?

Illustration:

What does your solution look like?

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Concept sketch examples

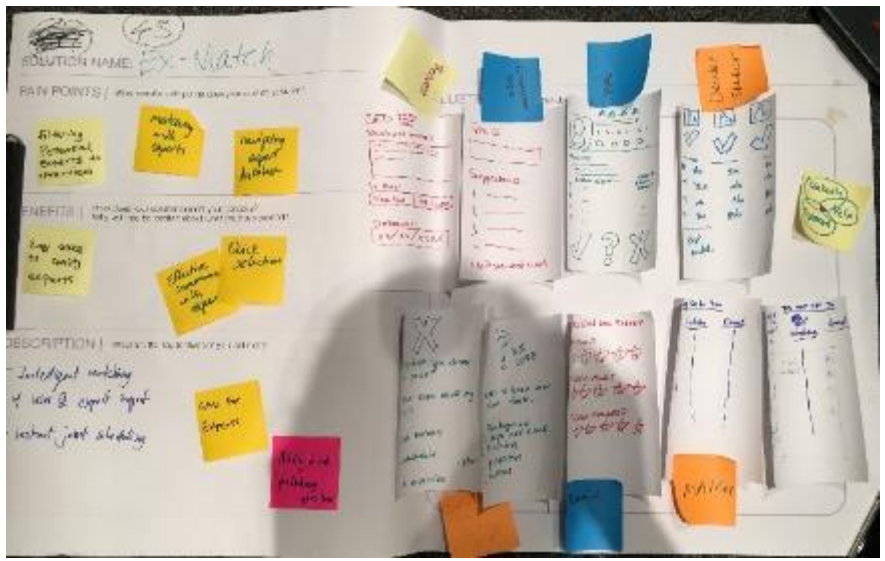



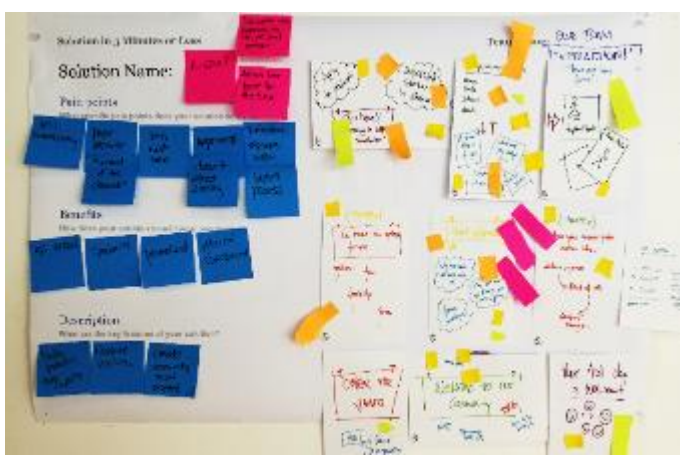

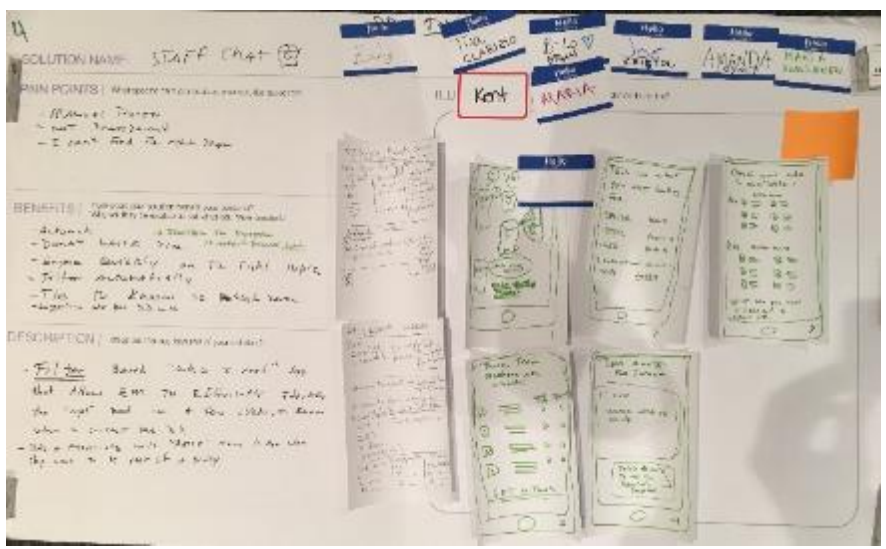

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Prototype and test with users to validate concepts (1/2)

Goal here is to test the desirability of selected concepts with the users. Paper prototype/low fidelity prototypes (i.e. wireframes) allow fast iteration of the design/flow

Sketch low fidelity screens

- Team members will draw low fidelity screens using pens and papers that highlight the improved experience based on the aligned ideas
- Team members will sketch a high impact user-story with a clear user flow
- The story will need to include an action that connects one screen to another

Digitize paper prototype

- Use application such as Pop to digitize the screens based on the actions that connect the screens into a digital prototype
- Click through the prototype to streamline the flow (fix usability)

Test prototype with users

- Prototypes can vary widely in their fidelity, ranging from low fidelity paper prototypes to high fidelity prototypes that incorporate the final visual design aesthetic.
- Prototypes are instrumental during validation and usability testing, providing an experience that feels
“real” to the user

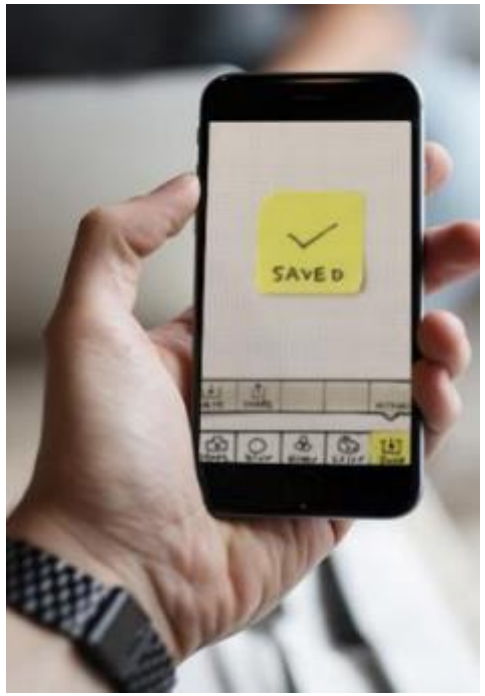



Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Prototype and test with users to validate concepts (2/2)

Design wireframes

- Wireframes provide “blueprints” for design and development, defining the way users experience and interact with the product
- They show the relative positioning of features and how they sit together, and also the hierarchy of information
- When sequenced together, they illustrate how users flow through the product and complete the tasks they need to

Develop visual design

- As concept sketches mature into functional wireframes, the next step is to apply visual design
- Visual design adds the emotive and branding layer of how we perceive and relate to products. It utilizes color, typography, imagery and layout to bring the product to life

Build experiential prototypes

- Prototypes can vary widely in their fidelity, ranging from low fidelity paper prototypes to high fidelity prototypes that incorporate the final visual design aesthetic.
- Prototypes are instrumental during validation and usability testing, providing an experience that feels “real” to the user

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

The Zero-Based Design process is a full-day interactive workshop

Goal

- The goal of the ZBD workshop is to re-design a process in a client-centric and collaborative way to create a truly distinctive experience

Example agenda

Topic	Timing
Icebreaker, introduction and agenda	09:00 – 10:00
Ideas and inspiration	10:00 – 10:30
Create client personas	10:30 – 12:30
Lunch break	*12:30 – 13:30*
Map current-state persona journey and complete empathy map	13:30 – 14:30
Ideate on an ideal customer journey	14:30 – 16:00
Sketch concepts and map scenarios	16:00 – 17:00
Daily wrap-up	17:00 – 17:30

Attendees

- Journey Team:
  - Navigator (Facilitator)
  - Product Owner
  - Design Lead (Facilitator)
  - UX designer
  - Scrum master (Facilitator)
  - Architect

- Subject matter expert:
  - Business unit
  - Anyone who is critical to the journey

The invite for the ZBD workshop outside the lab team should target individuals with open-minds, a vision for the future of the organization, and who are critical to build organizational buy-in – the group should not exceed ~20

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Setup required for Zero Based Design workshop

Tools

- 1 black Sharpie marker per person in room
- Lots of different colored post-it notes (the ~3” square kind)
- Colored sticky dots for voting
- Blank white large 3M poster sheets (as a backup if you run out of room on worksheets)
- Large poster size color, non-mounted print-outs of 1 each of your 3 personas
- 1 large blank poster size color, non-mounted print-out of the empathy map template per break-out team (usually ~3-4)
- 1 large blank poster size color, non-mounted print-out of the journey map template per break-out team (usually ~3-4)

Environment

- Need to make sure you have ample space for breakout groups inside large room or with smaller adjoining/nearby rooms
- Rooms need a projector and sound output
- Lots of wall space to hang large posters and areas to congregate in front of those posters work group breakout sessions
- Encourage participants to come dressed and thinking casually – this will be a different kind of day. Make every effort to communicate this in the setting and in your verbal and non-verbal language pre, during and after the workshop

Communication and Team

- The day begins with the entire group seated and doing ice breakers, watching and listening to the set-up
- The bulk of the day has the teams broken into small groups working together standing in front of posters
- Think carefully about team break-up on the participant side. If you have any instigators or non-creative thinkers, split them up. Likewise if you have any great innovators or design thinkers, split them up to help all the groups move forward quickly
- The goal is to have fun, inspire and get as many ideas out there as possible by engaging the participants to think differently. There are no bad ideas today. Use “and” not “but” language to extend ideas not truncate them

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Facilitation guidelines for Zero Based Design workshop

Tips and tricks for workshop facilitation

- **Journey Lead should lead the presentations** and recaps whenever possible
- Materials should be pre-syndicated with key stakeholders (Exec Sponsor)
- **The tables/group compositions should be carefully planned** (based on seniority level at the bank)
- Participants should be informed ahead of time of any necessary pre-work
  - (i) what this workshop will be about, (ii) what is their role, (iii) what we expect from them
- **The team should be thoughtful about timing and energy**
- There should be a full-time Scrum Master role (to keep the process flowing and keep track of time)
- The should be an energy meter and **energizers should occur throughout the workshops** (e.g. candies, ice-breakers, coffee breaks)

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Table of contents

What are the outputs for each journey, and how should each journey operationalize itself?

- Recap: Phases that each Journey Team undergoes
- B1. Aligning the target strategy with customer vision
- **B2. Defining delivery roadmap**
- B3. Onboarding the team (i.e. Sprint 0)
- Translating this into a sprint plan

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time

Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Components of the delivery roadmap

- **MVP design**
- Backlog build and management
- OKRs and squad metrics

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

The ZBD is scaled back to a Minimal Viable Product to be developed as the first release of the new process

Description

What is the MVP

- **The smallest thing you can build that delivers customer value** (core functionality valued the most) to a significant portion of the population that allows us to collect the most amount of information about user preferences with a minimal amount of effort

What the MVP is NOT

- Full range of features and functionalities that the product should eventually contain
- Released product that includes a range of functionalities that only partially work



Nature of MVP

- **The MVP is always "alive"** and we are always evolving based on new insights from customers and the team
- **Each sprint we are adapting the MVP based on new information** from: more in-depth technical analysis, internal/external constraints and, most importantly, customer feedback

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Activities to develop MVP

	Details	Prep required	Responsible	Timing
Pre-work	**4 Draft potential MVP scope** ▪ Gather data to understand potential scope decisions – E.g. in-branch versus online, breakdown of product types, breakdown of customer types	▪ SME interviews ▪ Additional product data gathered	▪ Navigator and PO	~ 2 days
Minimal Viable Product	**5 MVP workshop** ▪ Review full list of features from ZBD ▪ Prioritize list based on business needs, customer experience, and technical feasibility ▪ Map MVP candidate journey	▪ Initial sketches and outputs from ZBD	▪ Journey Team and Design	1 day
Post-work	**6a Iterate on MVP wireframes** ▪ Review prioritized list of features and ZBD sketches ▪ Create MVP wireframes	▪ Review set of initial sketches	▪ Design, PO	1 day + ongoing
	6b Prioritize MVP scope for the pilot ▪ Align on target pilot audience and goals for MVP first release ▪ Identify solution-areas for manual workarounds that facilitate a fast first release	▪ Review all outputs (list of prioritized features, solution architecture, sketches, etc.) ▪ Understand key product data	▪ Navigator and PO	1 day + ongoing as required

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

The MVP workshop is an interactive session to define the Minimal Viable Product at a high-level

Goal

- The goal of the MVP workshop is to prioritize features coming out of the ZBD workshop and to map a Minimal Viable Product journey; further work on scope decisions will be required as follow-up to the workshop

Example agenda

Topic	Timing
Icebreaker, introduction and agenda	09:00 – 10:00
Recap from Zero-Based Design	10:00 – 10:30
Energizer exercise	*10:30 – 10:45*
Map potential features for MVP journey	10:45 – 12:30
Lunch break	*12:30 – 13:30*
Problem-solve feasibility and prioritize features	13:30 – 15:30
Align on priority journey for MVP	15:30 – 16:30
Daily wrap-up	16:30 – 17:00

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

MVP workshop attendance: the core team and carefully selected stakeholders should attend

Work-cell team

- **Navigator** – key facilitator
- **Product Owner**
- **Analyst(s)**

Design team

- **Design Lead** – key facilitator
- **Visual / Interaction designer(s)**

Outside the lab team

- **Executive Sponsor** (other Support Committee members only if appropriate)
- **Select external** specialists (e.g. Legal or anyone who is critical to understand feasibility of the solution in more detail)

Delivery team

- **Scrum Master**
- **Architect**

The invite for the MVP workshop outside the lab team should target individuals that understand trade-offs and feasibility, can challenge existing processes, and can drive solutions – the group should not exceed ~20

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

The team defines the MVP journey at a high level during the workshop and continues to refine the scope in working sessions afterwards

	Description
During the workshop	▪ During the Workshop we will create an **MVP candidate**: – Understand the Product Owner's vision regarding the re-imagined (zero-based design) journey – Discuss and agree on full list of features on each of the steps of the new process – Prioritize these features based on value to customers (i.e. which features add the most value to customers)
After the workshop	▪ After the workshop, there is still work to be done to refine the MVP and the core-team will: – Run (high-level) analysis on the technical feasibility of each of the features (to understand if the team can develop them in 14-weeks) – Run other feasibility studies (regulatory/legal, compliance, etc.) – Create a prototype with the prioritized features that can be developed during 14 weeks – Test prioritized features with customers to understand if these really are the most valuable to them – Continuously test features with customers to repeatedly and frequently get their timely feedback

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Coming out of the MVP workshop, the team should align on the MVP journey that will be developed as the first release

EXAMPLE

Example MVP journey map

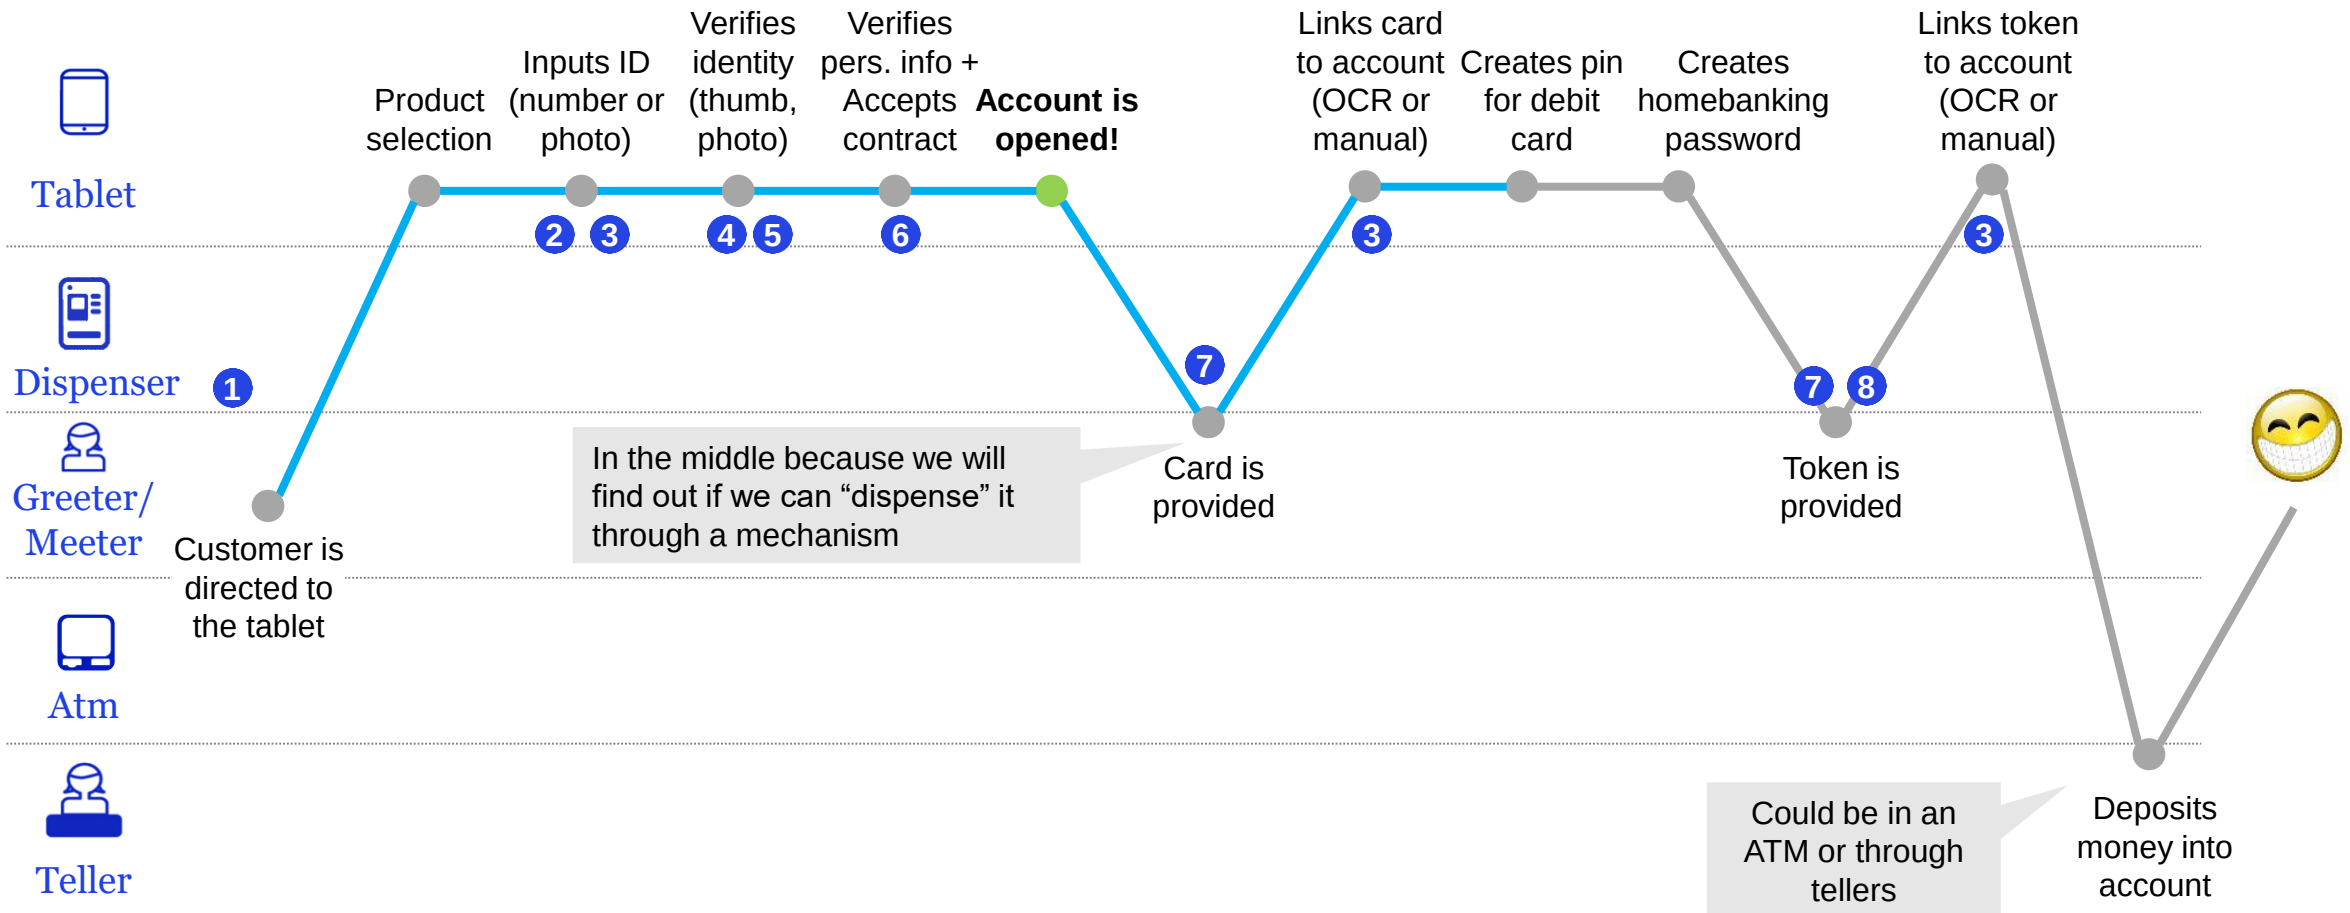

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

The team should refine the MVP scope to determine what components are feasible for development in the first release (1/2)

In scope

Example MVP scope decision

	In-branch	Self-service
Reach	▪ Although Mainstream segment (93% of clients) has a high penetration of digital technologies, they don't use those channels to interact with the bank: – 52% have access to internet, but only 7% have tokens to make operations though Homebanking – 21% have smartphones, but only 4% use the App	▪ Premium segment represents only 7% of total clients, but 65-75% of the profits ▪ High penetration of digital technologies is observed: – 91% have internet access, of which 45% have tokens – 73% have smartphones, but only 12% use the App
Rationale	⊕ Easily overcome potential roadblocks in the short term: – Physical identification of person trying to open an account may be conducted (e.g., signature, ID) – Potential legal requirements that can't be included in App can be included (e.g. signing of contract) – Debit card and token are given to the client immediately after the account is open ⊕ Customer research can be done in person, which results in richer information and insights ⊕ Branch staff can be leveraged to assist customers to open an account ⊕ Allows to target segments based on branch geography and scale branch-by-branch ⊖ Customer experience "wow" factor can be less, due to the fact that the account can't be created remotely	⊕ Better client experience due to the fact that the account can be open remotely ⊕ Easier roll-out plan once the product is launched to all customers ⊖ Given the size of the segment, savings in account opening would be very limited ⊖ Although Premium segment has a high penetration of smartphones, it is not directly translated to banking services ⊖ Longer time-to-market of initial service due to the fact that branch systems/processes can't be leveraged ⊖ Requires a custom distribution list to select clients as beta testers ⊖ Requires training a wider pool of people to respond to client questions or problems (e.g. Contact Center, IT department)

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

EXAMPLE

The team should refine the MVP scope to determine what components are feasible for development in the first release (2/2)

In scope
Out of scope

Example MVP scope decision

Client	× Account	× Currency	× Debit card	× Token	= Reach
55% new	57% Basic	65% Dollars	75% Classic	92% none	
45% existing	16% Premium	35% LC	16% Gold	8% token	
	18% Salary		9% Loyalty		
	9% Active				
100%	× 82%	× 100%	× 75%	× 100%	= 62%

For our MVP, creating a solution for all clients, accounts, currencies and offering only one debit card allows us to reduce complexity while maintaining a large eligible market size

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Translate concept into a feature map

What is a feature map?

- **Lays out Features and their constituent Epics** in a way that makes sense and is digestible
- Works just like a physical geographical map and makes the workflow and value visible
- **Plan releases in valuable slices** of functionality – to seed a Product Backlog
- Provides a way to 'eat the elephant', **highlighting priorities, dependencies, areas of complexity**

Feature map overview

- Allows the entire team to digest the big, incremental picture of scope and functionality
- A tool **to allow anyone to collaborate on the roadmap** / backlog, Identify holes and omissions
- Effectively plan and prioritize around business value delivery to users
- Usually more detailed at the top end like a typical backlog:
  - Near term contains well written User Stories
  - More granular detail (e.g. Epics / large stories) further out

Activities

- Through ideation and concept validation, you will establish "large buckets" of design – the Features or Themes
- Lay out a visual "map" to clarify scope and priority Features and their components
- Re-order the stickies to prioritize

Concept description:

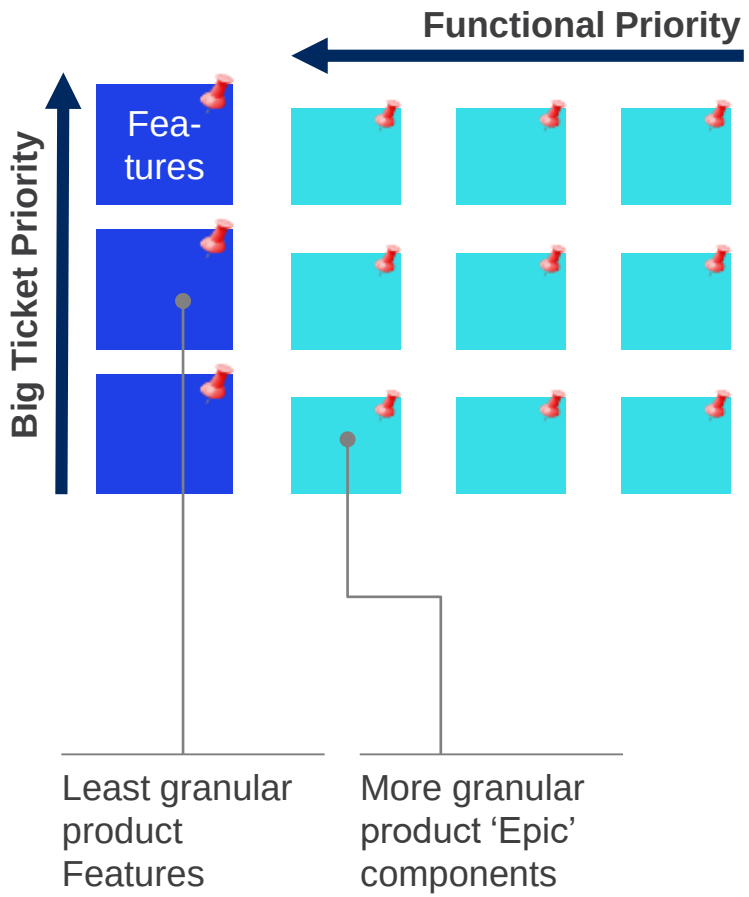

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Map the high-level MVP in the feature map

Features

- Written from the viewpoint of an **end user**
- Big chunks of work that meet **user needs**

Epics (High Level Stories)

- Major functionality that **enables user value**
- Sequenced in **decreasing level of importance** to the solution
- Can include **user-facing features** or **major technical or business-process functionality**

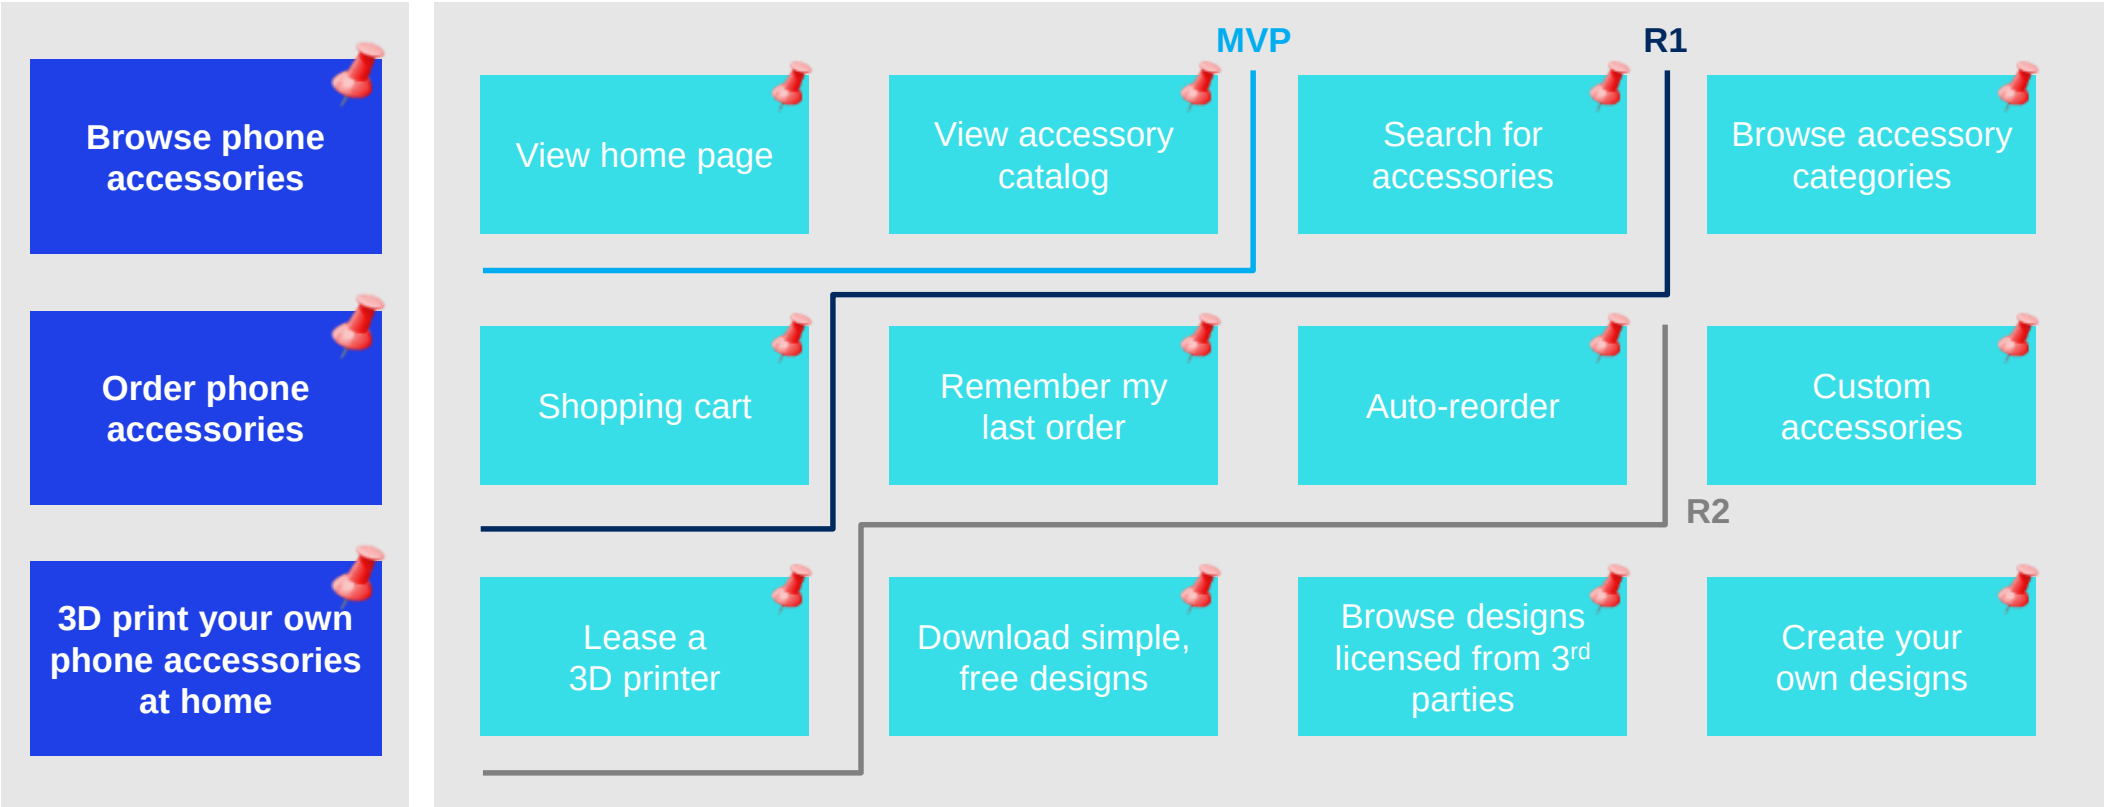

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Components of the delivery roadmap

- MVP design
- **Backlog build and management**
- OKRs and squad metrics

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

The Product Owner defines the features of the new solution by creating a backlog of user stories to develop

Product backlog

- An ordered list of items to be delivered in the future
- Contains short items (user stories) describing “what" is required and not “how" it’s done
- Is owned by the Product Owner, with contributions coming from the whole team
- Is updated, refined and re-prioritized throughout the development of the product/project in collaboration with the team

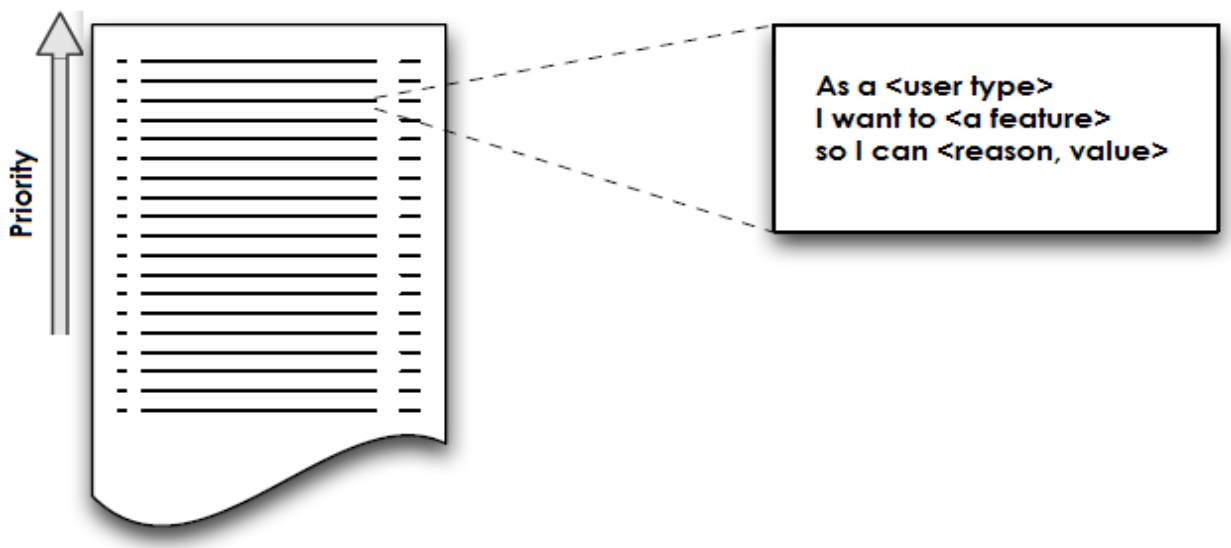

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

The product backlog constantly evolves and should be re-prioritized as the need for new features emerges

- Not all requirements are known from beginning
- New requirements can arise, some may fall out, priorities will change
- Agile: more conversation, less writing, just write what is necessary
- Product backlogs are emergent
- A living artifact which will, and should change

A product backlog is ordered (prioritized), and influenced by

- Business Value
- Risk
- Customer Satisfaction
- Cost and Cost of Delay

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

A good product backlog is detailed enough, estimated, emergent, and prioritized

Detailed enough
Estimated
Emergent
Prioritized

The iceberg metaphor

- Highest priority stories are at the top and small enough to be worked on in next sprint
- Medium priority stories are in the middle, are bigger with some details known but not all
- Large lower priority stories sit at the bottom, are large and little is known about them

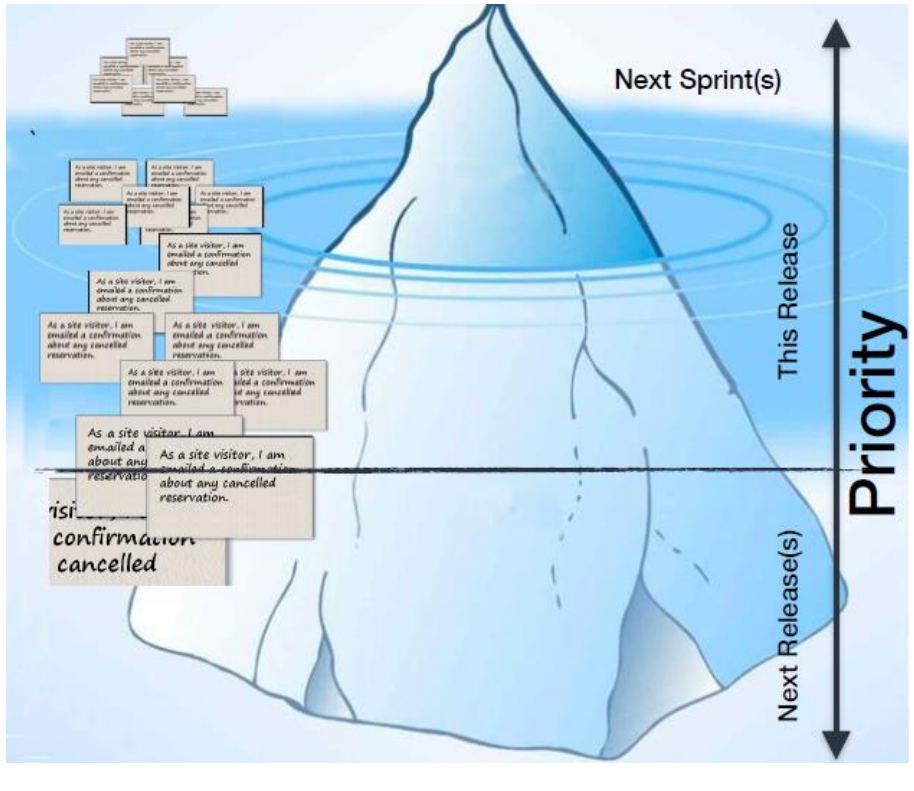

When the tip of an iceberg is removed as stories are completed, the remaining stories bounce to the top, forming a new peak. Items "under the water" are less defined, and have less focus.

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

The backlog should be regularly groomed by the PO to re-prioritize stories, add detail, and ensure the stories are ready to be worked on

Looking ahead

- Product backlog grooming is the act of looking further down the backlog and changing things such as; the priority, the acceptance criteria, splitting and sizing stories based on new information. This is an ongoing activity executed by the PO, SM, and the team collaboratively
- The Product Backlog refinement meeting usually happens 1 or 2 times per sprint, and focusses on items which are 2-3 sprints away

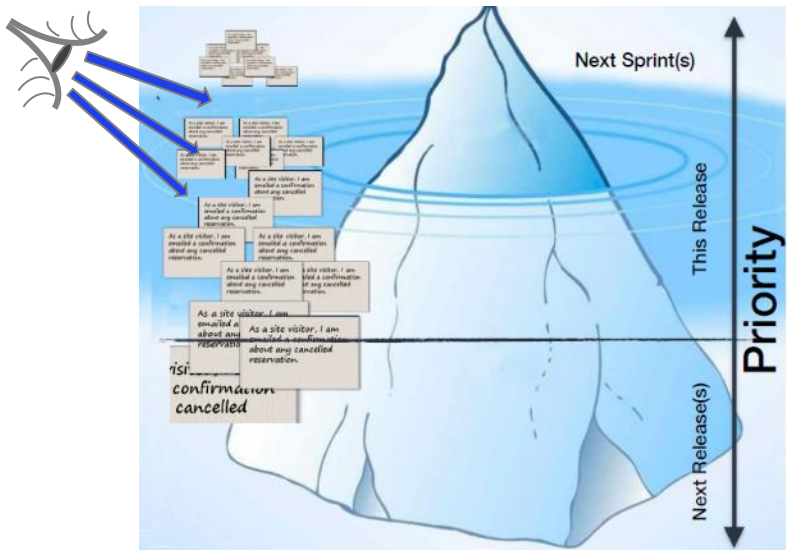

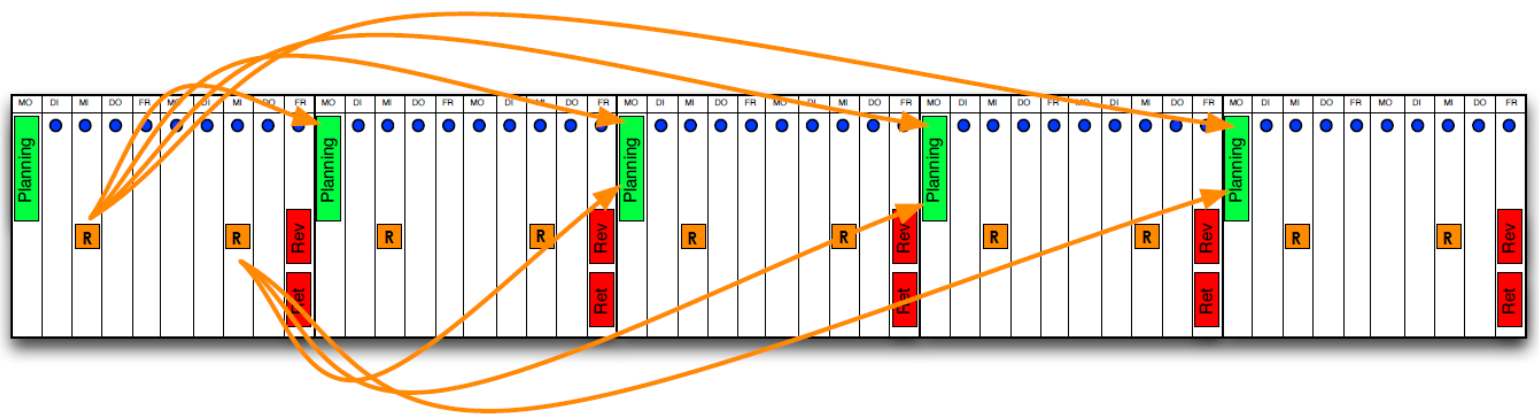

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

The product backlog is a living artifact that is constantly evolving

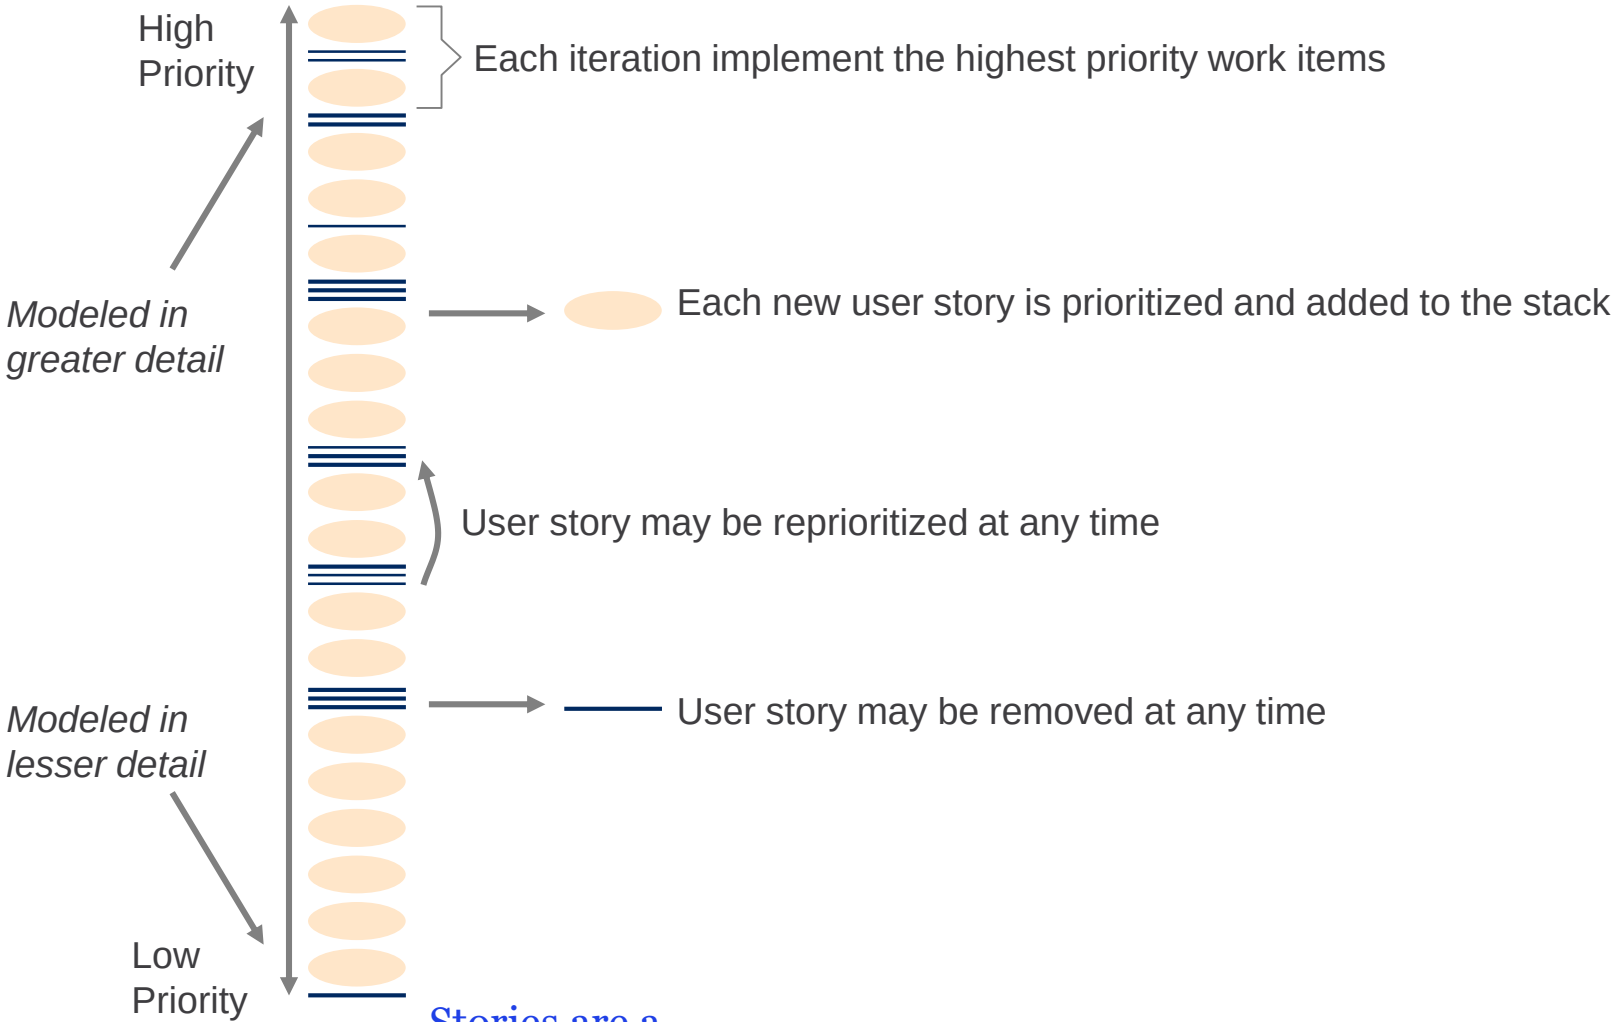

User stories

Stories are a

- User's need
- Product description
- Planning item
- Token for a conversation
- Mechanism for deferring conversation

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Contents of the backlog that are more certain should be defined in greater detail

Sprint Backlog

Sub-set of product backlog committed to delivery within the sprint

Product Backlog

Collection of epics and stories describing functionality yet to be built

More Defined

Less Defined

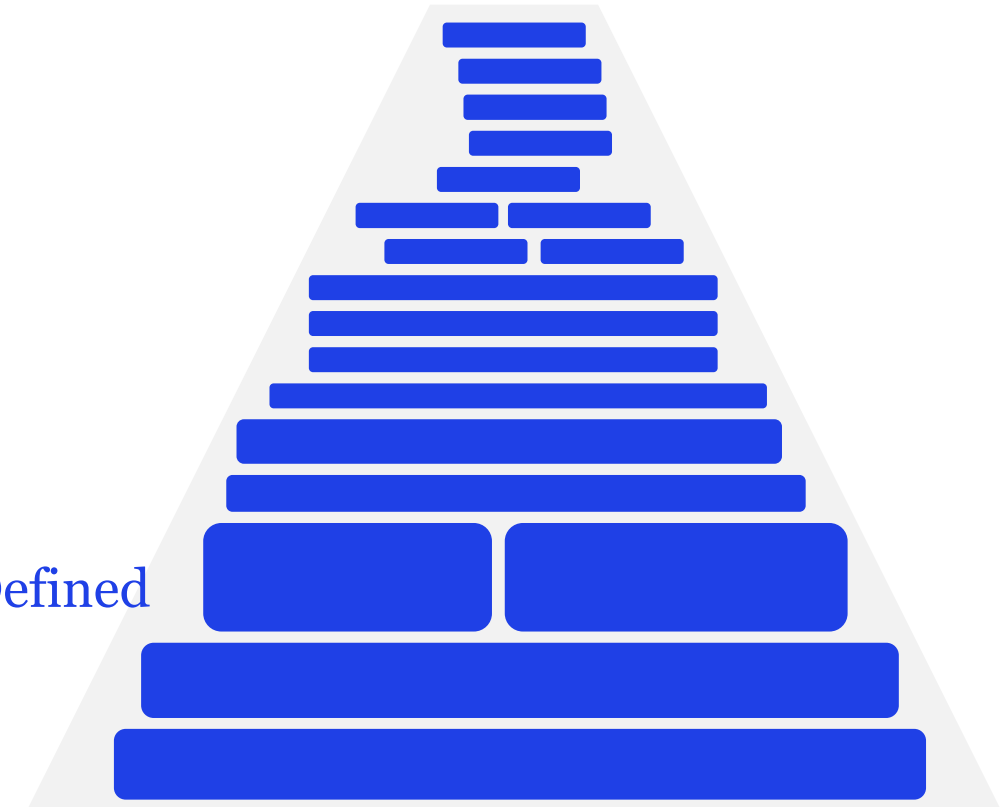

Stories

Epics

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

The PO creates the product backlog by decomposing product features into the user themes, epics, and user stories

Theme Increase website traffic

Epic Add new video section		Epic Improve login page usability		
User story	**User story**	**User story** As a user, I would like the validation on the login page to be very clear so that I can easily see when/if I make a mistake when I log in		
Task	**Task**	**Task**	**Task**	**Task**

- Laying out the **User Stories** in the Requirement Map format, helps the team:
  - Prioritize (moving Stories)
  - Identify missing pieces (adding Stories)
  - Create shared understanding of objectives (discussing, asking questions)

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Components of the delivery roadmap

- MVP design
- Backlog build and management
  - **Writing user stories**
  - Estimation
- OKRs and squad metrics

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Create backlog – What is a user story?

User story is a short and simple description, written from the user perspective

Card

User story information is lightweight. It fits onto a single index card. It's a promise to have a conversation at the appropriate time.

Confirmation

Acceptance criteria are added to the user story, to confirm the feature was implemented correctly.

Conversation

When the story is selected for a sprint, further details are finalized in conversations between the team & Product Owner. The team will write down what is agreed upon.

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

User stories should follow the INVEST mnemonic…

I Independent

Easier to Plan

E Estimable

Too Big/Too Vague?

N Negotiable

Details via Collaboration

S Sized Appropriately

Can be done in 1 week?

V Valuable

So what?

T Testable

User Acceptance Criteria

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

User stories should follow the INVEST mnemonic…

I
Independent

Independent

- Can be completed independently of other User Stories
  - avoids dependencies between stories
  - simplifies problems with estimation, prioritizing, implementation
  - ideally isolated
- Possible solutions
  - combine small stories
  - split larger stories

N
Negotiable

Negotiable

- Stories are not contracts / specifications
- Not all details are included
  - too many details create false assumptions about completeness
- Flexibility - details are communicated directly with PO through conversations
- Remember, a story is a “promise of a conversation”
- As emergent details come to light the PO and team can negotiate on adjustments to the user story or its acceptance criteria in order to deliver value in the time frame

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

User stories should follow the INVEST mnemonic…

V
Valuable

Valuable

- Value of a User Story is expressed by its functionality and use / benefit for
  - customer
  - user
  - buyer
  - sponsor, ...

E
Estimable

Estimable

- Estimations are required for planning
- Team will fail to estimate properly if
  - User Story is too big
  - technical knowledge is missing / user story is not clear
  - domain knowledge is missing

S
Sized Appropriately

Sized appropriately

- Sized correlates with uncertainty
  - big User Stories are difficult to estimate
  - and useless for planning
  - completely useless for a sprint
- Stories at the top of the backlog are small enough for the sprint
- Stories lower in the backlog are large and vague enough as needed

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

User stories should follow the INVEST mnemonic…

T

Testable

Testable

- Easy to know when the story is complete – conditions of satisfaction
- Story must have clear acceptance criteria
  - Each AC results in at least one acceptance test, but usually more
  - Tests should be automated

A user story is NOT…

- a detailed specification
- a description of "How" it should be done
- a replacement for dialog or conversation
- a fixed "contract"

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Example user story template

As a <Role>
I want <Feature>
So that <Benefit>

As a traveller, I want to reserve a hotel room So that I have a place to stay	As a vacation planner, I want to see pictures of the hotels, so that I can decide where to stay
As a user with a reservation, I want to cancel my reservation so that I can get refund	As a hotel owner, I want to see a report of all cancellation so that I can review them

Tip: Remember the role needs to be an actual end user persona, not a system or a person. Say for example: Vacationer, Hotel Owner, Travel Agent, Trip Planner or a Parent

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

User stories need to contain acceptance criteria that define the feature in greater detail

For the Product Owner

- They are a much finer grained requirements definition than the Story
- Focuses the team on how a feature will work from the customer's perspective
- It removes ambiguity from requirements
- They help form the basis of functional test cases
- They can be supported by other information like screenshots or UI wireframes, design documents, or anything that provides more detail about what should be implemented

For the Developer

- They assist the developers and testers when estimating the Story
- It forms the tests that will confirm that a feature is working and complete
- It limits the developers to adding only the functionality that the user story requires

Acceptance Criteria for a User Story are the conditions that the story must fulfill to be considered "Done". It focuses on external quality and functionality. These conditions are provided by the business and must be one of the parameters in your "Definition of Done" list

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Example acceptance criteria template

Given <some preconditions>

When <an action is performed>

Then <this will occur>

Given I am a premium member, When I cancel under 24 hours, then I incur no penalty

Given I am a site member, when I cancel my reservation, then I am emailed a confirmation

Given I am a non-premium member, When I cancel under 24 hours, then I pay 50% penalty

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

A good user story is such that one can write the whole story on a card with the acceptance criteria on the back of the card

User cancels reservation #12345

As a user with reservation
I want to cancel my reservation so that
I can get a refund

Acceptance Criteria

- Given I am a premium member, When I cancel under 24 hours, then I incur no penalty
- Given I am a non-premium member, When I cancel under 24 hours, then I pay 50% penalty
- Given I am a site member, when I cancel my reservation, then I am emailed a confirmation

Business Value: H

Effort: 8

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

User stories should articulate needs rather than define solutions

Needs-oriented stories ✓

"As a cook, I want to prepare hot food for the family, so that we can safely enjoy various fresh foods without having to spend time traveling"

"As a car-owner, I want to park somewhere safe, so that I can keep my insurance premiums low"

Solution-oriented stories ✗

"As a cook, I want a kitchen, so that I can prepare food"

"As a car-owner, I want a garage, so that I can park my car off the street"

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Basing stories around needs expands the range of potential solutions

Example needs-oriented stories

- As a car-owner, I want to park my car off the street, so that I can reduce my insurance premiums
  - Solution: Concrete platform in a gated backyard
- As a car-owner, I want to shelter my car from the rain, so that I don't have to wash it as often
  - Solution: A plastic or nylon car cover
- As a car-owner, I want to hide my car from onlookers, so that opportunists don't think of stealing or vandalizing it
  - Solution: A camouflage cover
- As a car-owner, I want to hinder thieves from driving my car away, so that I get the lowest insurance premiums
  - Solution: A strong wheel lock or alarm system
- As a car-owner, I want to securely store my tools near the car, so that it's easier to do basic maintenance
  - Solution: A mobile toolbox

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

User stories should capture features that slice from the technical front-end of the solution into the technical back-end of the solution

Good User Stories are vertical – not horizontal

- Split stories by feature, through architectural layers
- General rule - the thinner the better

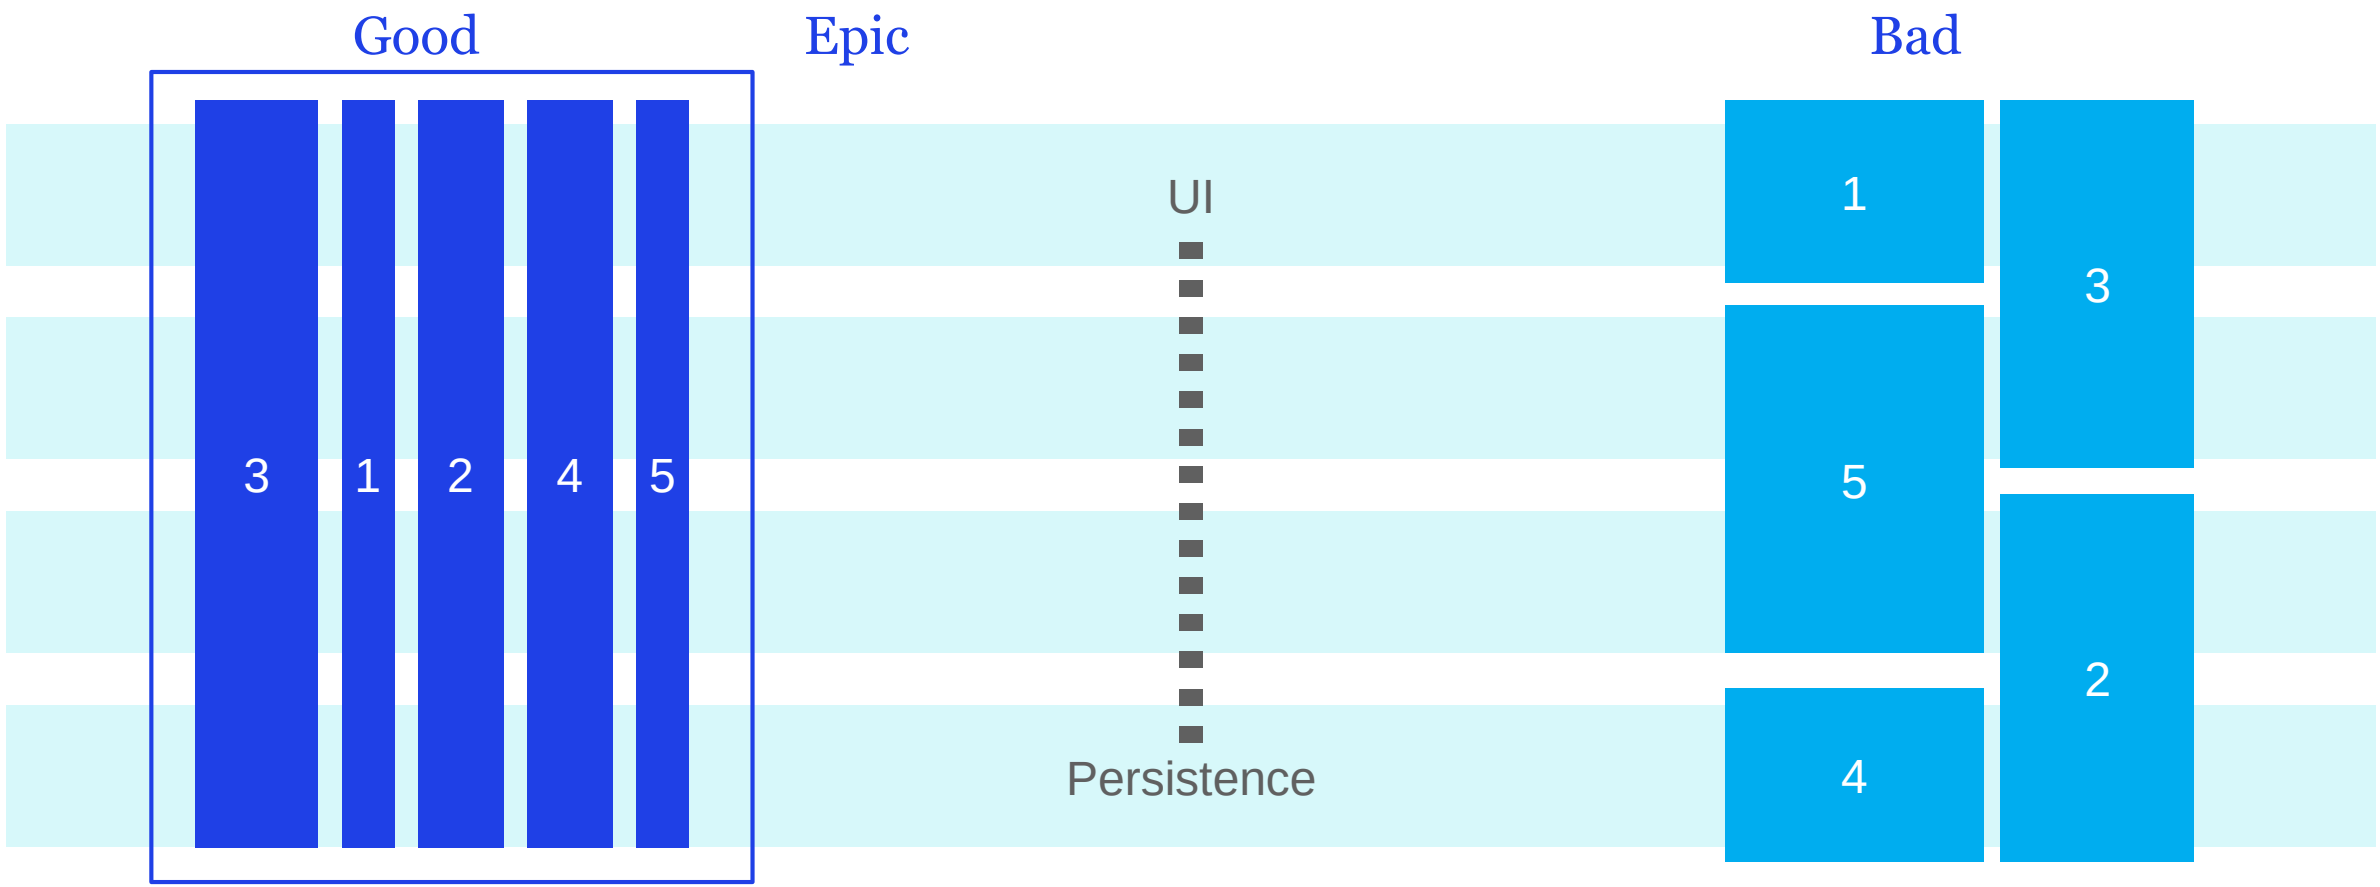

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

When stories are very high-level, they are called epics and should be split into smaller user stories for development and prioritization

EPICS

- Similar to user stories, but written from a higher perspective
- Sometimes have Acceptance Criteria
- Start with Epics to capture general product functionality
- Then split into User Stories as they rise up the backlog

Story/Epic splitting

- Can be difficult and takes practice
- Is a team effort, not just a PO task
- Often done in backlog grooming meetings & planning meetings

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Several criteria can help the PO split a user story into smaller stories

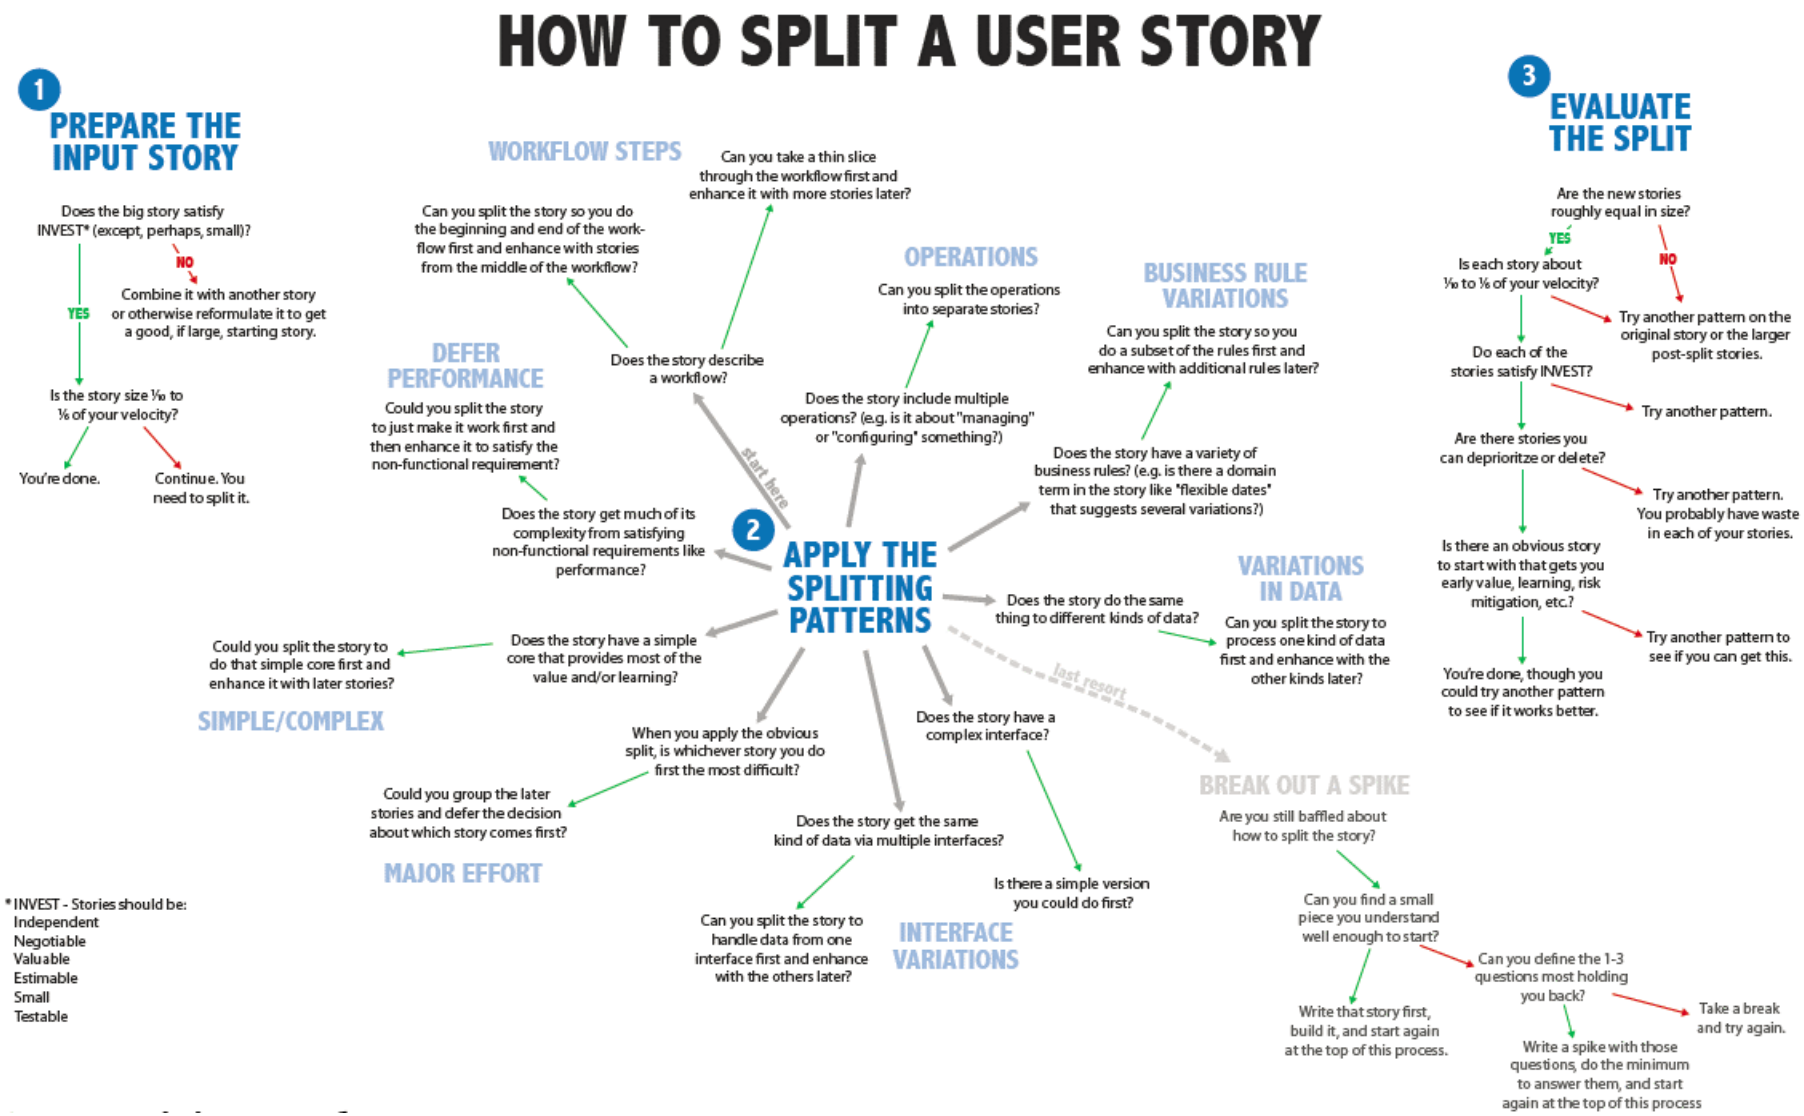

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Example user story split into smaller stories for development

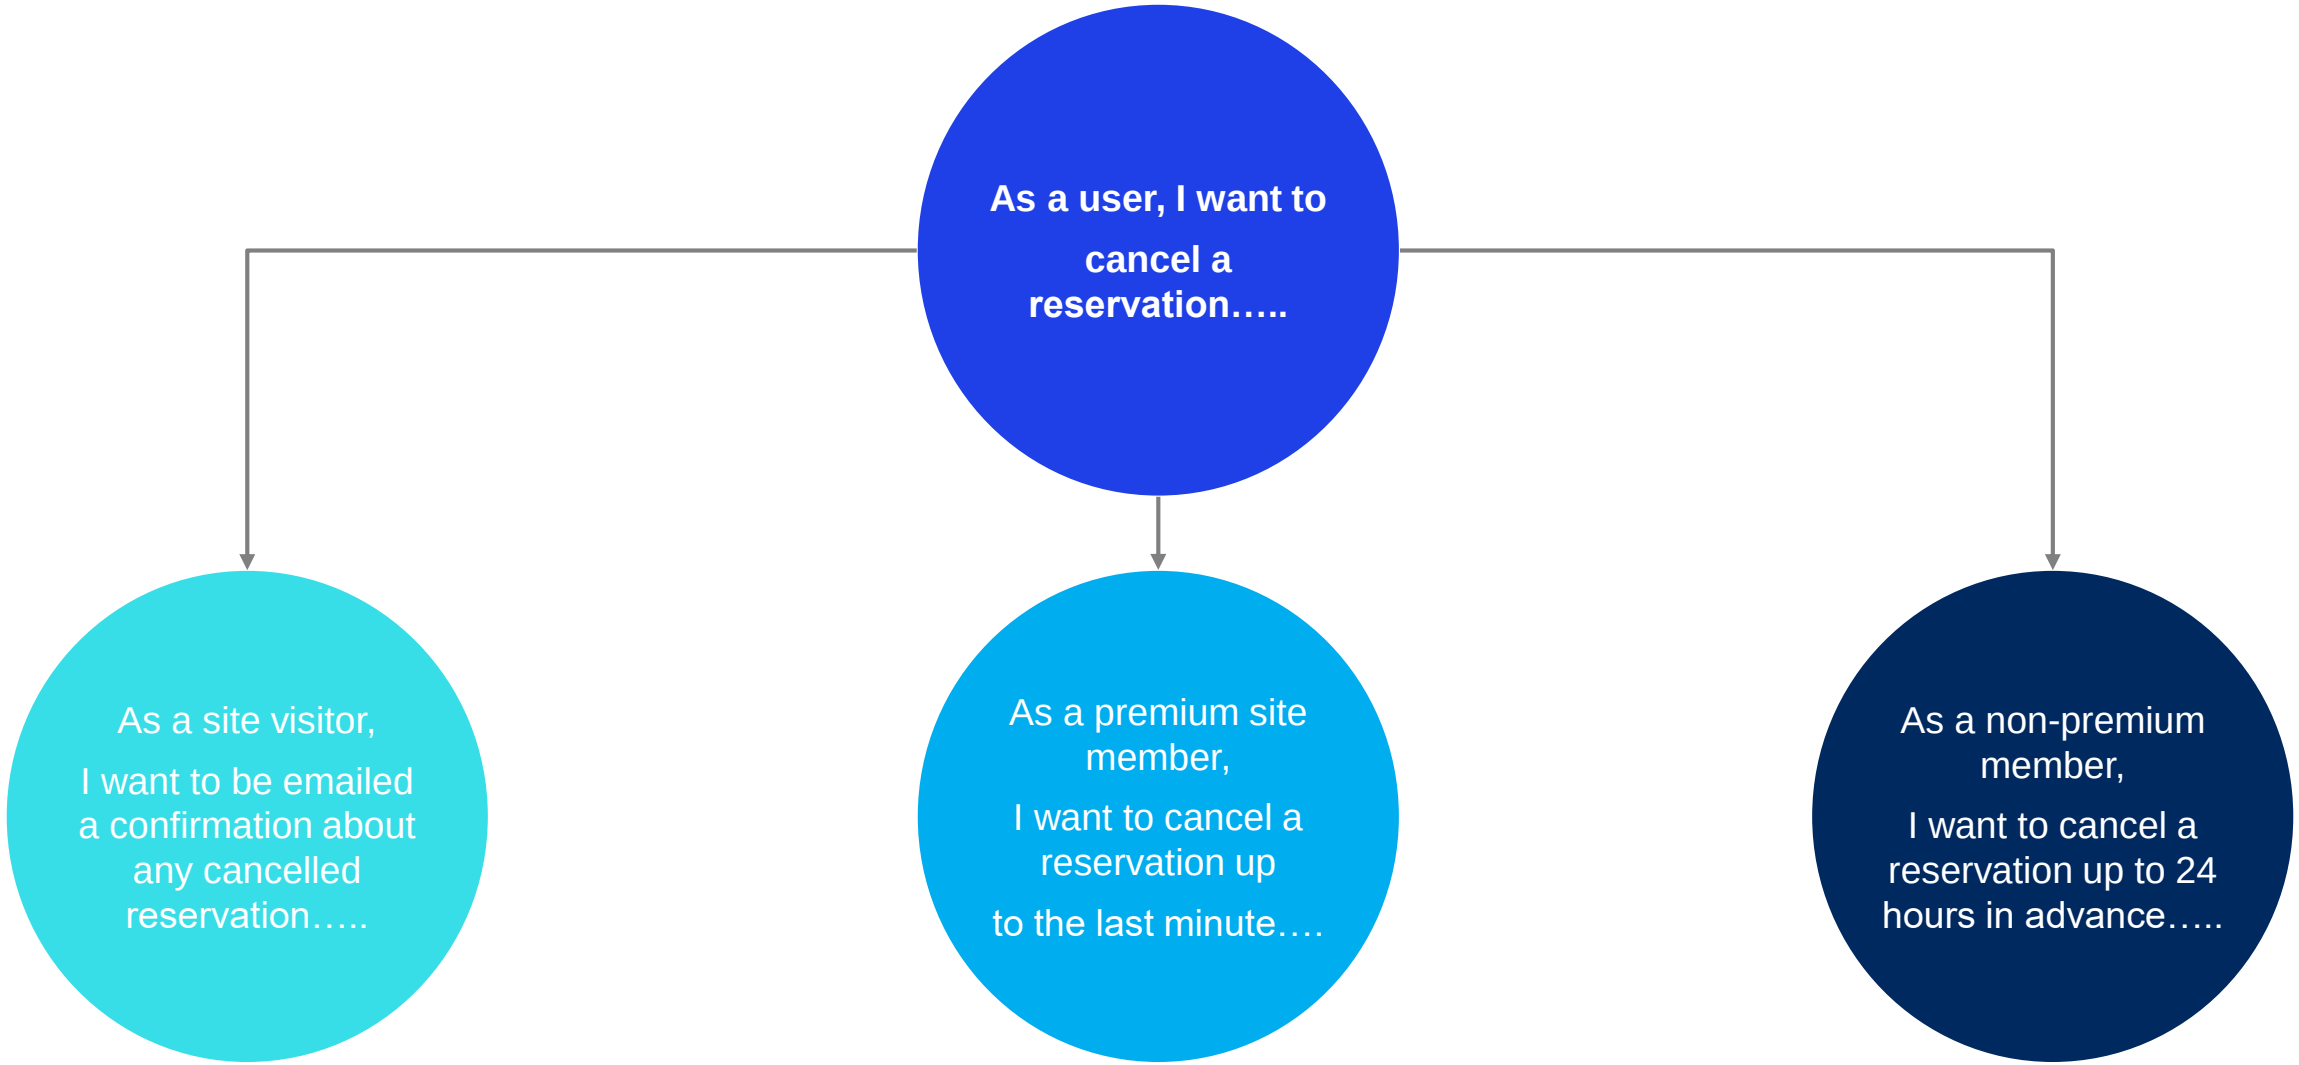

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Components of the delivery roadmap

- MVP design
- Backlog build and management
  - Writing user stories
  - **Estimation**
- OKRs and squad metrics

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Backlog estimation exercise: predict complexity and effort by grouping backlog into batches of stories

Small	Medium	Large	XL
Story	Story	Story	Story
Story 18	Story 45	Story 19	Story 10
Story 7	Story 4	Story 12	Story 2
Story 23	Story 79	Story 78	Story 37

Preparation

- Estimation involves the entire scrum team
- The team determines unit size for stories
- Considering the DoD for each story
- The team has access to full list of stories in the backlog
- Team identifies and reaches a consensus on the simplest story to be assigned a ‘small’ which will be used as a basis for calculating complexity of other stories

Ranking and grouping stories

- Deal the estimation group a small set of story cards
- Have them rank the cards into small/medium/large
- Repeat this process until the backlog is categorized into story sizes (usually XS/S/M/L/XL)
  - If required have a category for clarifications needed

Size stories

- After the stories are grouped, agree on what these sizes mean
- Choose a point system to represent each size
- Use this to estimate the total size of release

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

User stories are sized with story points that help the team understand the relative work effort required

What are story points?

- Relative size for a story that tells the team how hard the story is
- A relative term that does not directly correlate to actual hours or time
- Story sizes will be different for each team
- Not a measurement of individual productivity
- Not as effective in environments with highly standard and repeatable work
- Tracking velocity in a set time-frame

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Story points are assigned to each story in a relative way—stories that are relatively bigger receive more story points

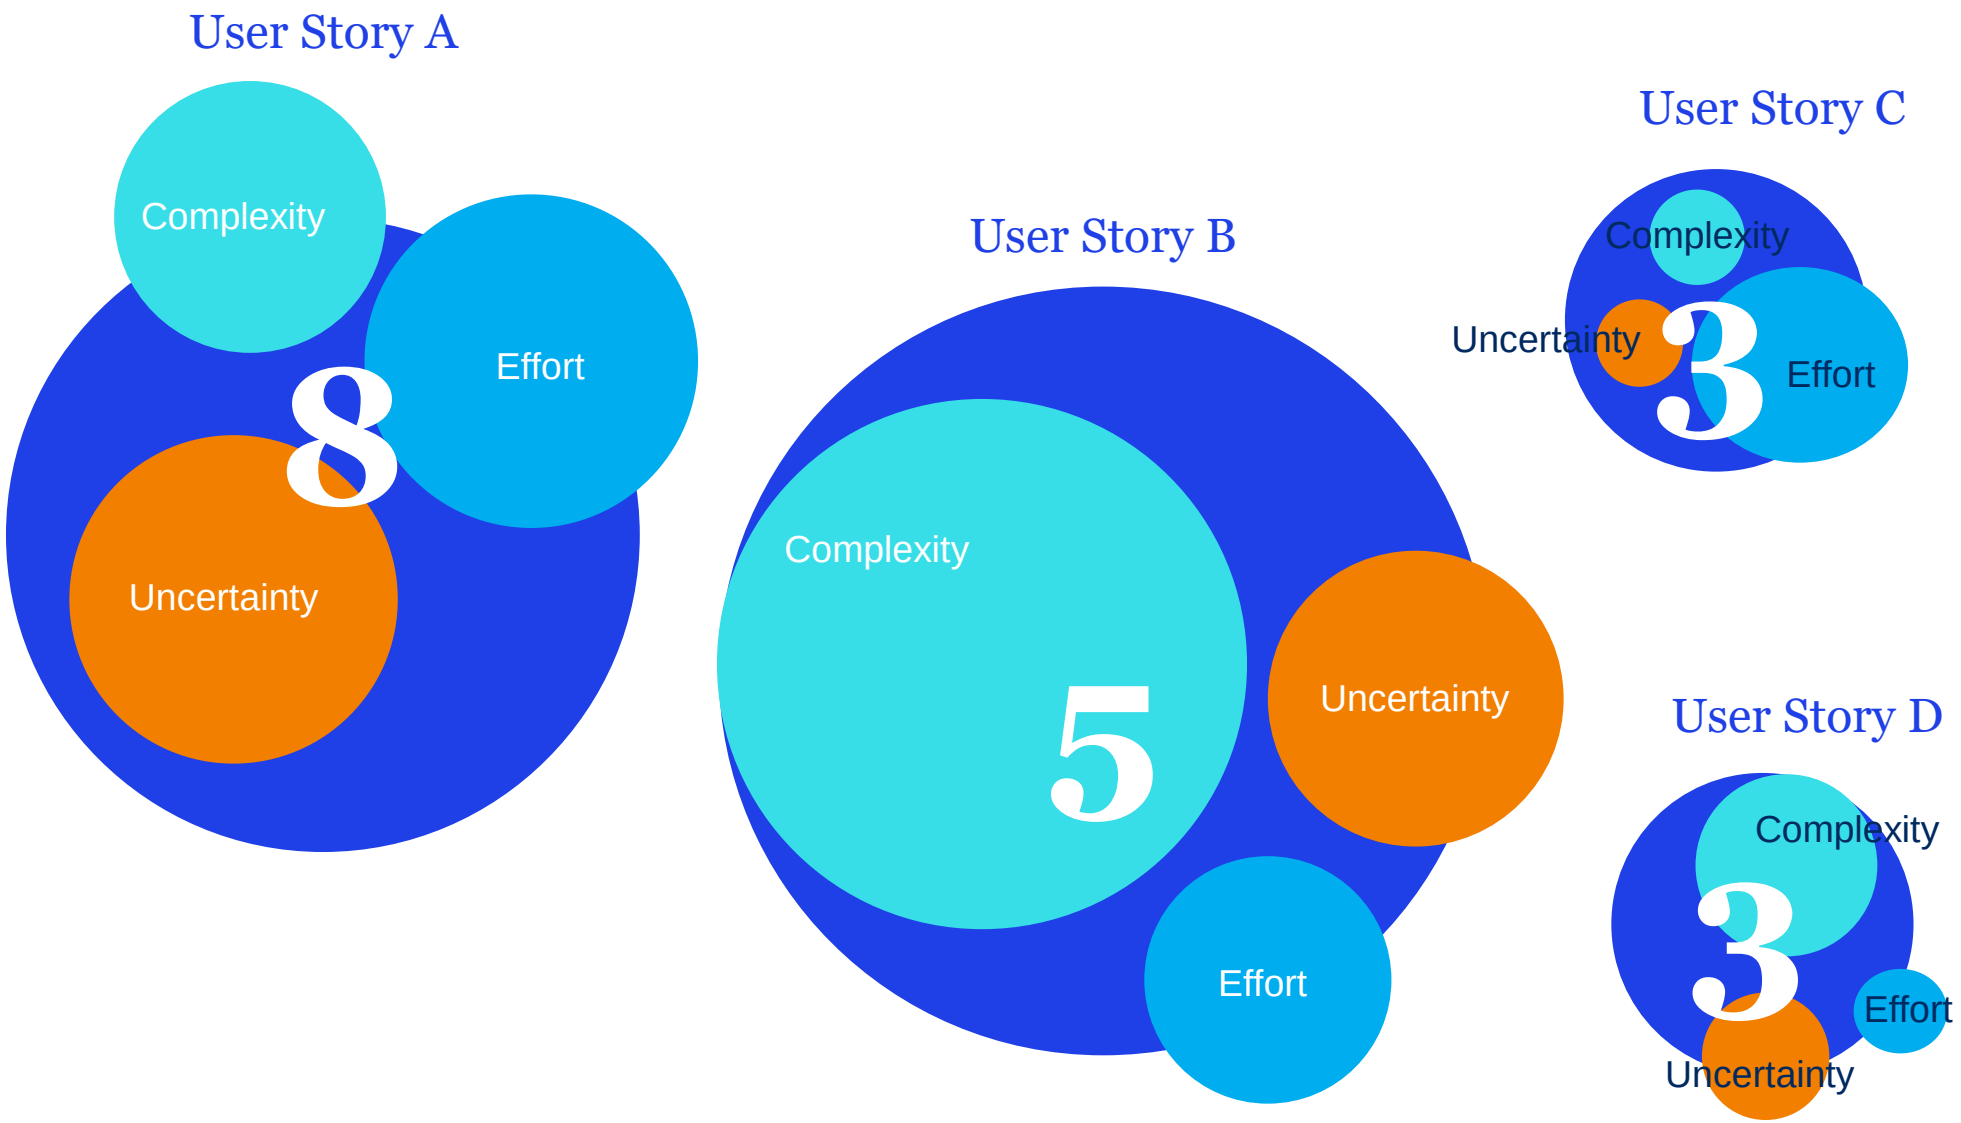

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

The backlog should be estimated with story points to get a high-level view of the work effort required

- Backlog estimation provides the development team with **an opportunity to understand the overall product functionality, and give early feedback** on the complexity of major features. It also provides the Product Owner with valuable **insight into whether the MVP scope is achievable**.
- The 4th item in the Agile manifesto states, *"Responding to change over following a plan". This is often misunderstood as meaning "Ah, we are agile now, we don't plan – why create a plan when following it is not important?"*. This is one of the agile myths which has risen since the manifesto was created in 2001.
- In fact, Agile planning is very important, but the approach is slightly different to that of planning techniques used in traditional software development.
- Planning is an activity - a plan is an artefact. **In agile, the focus is more on the activity, not the artefact.** Agile planning is continuous throughout the lifecycle of the product/project and is expected to change and be refined constantly. They are designed to be easily changed and also reflect the uncertainty and complexity that exists in the development of a software product. Agile planning is not an activity executed at the start of a product or project, and any deviation from which is regarded as unfavorable.

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

To size the backlog, the team assigns a relative T-shirt size to each of the stories

T-shirt sizes for stories

SM story = 1 point

MED story = 3 points

LG story = 8 points

X-L story = 13 points

Sizing of the backlog

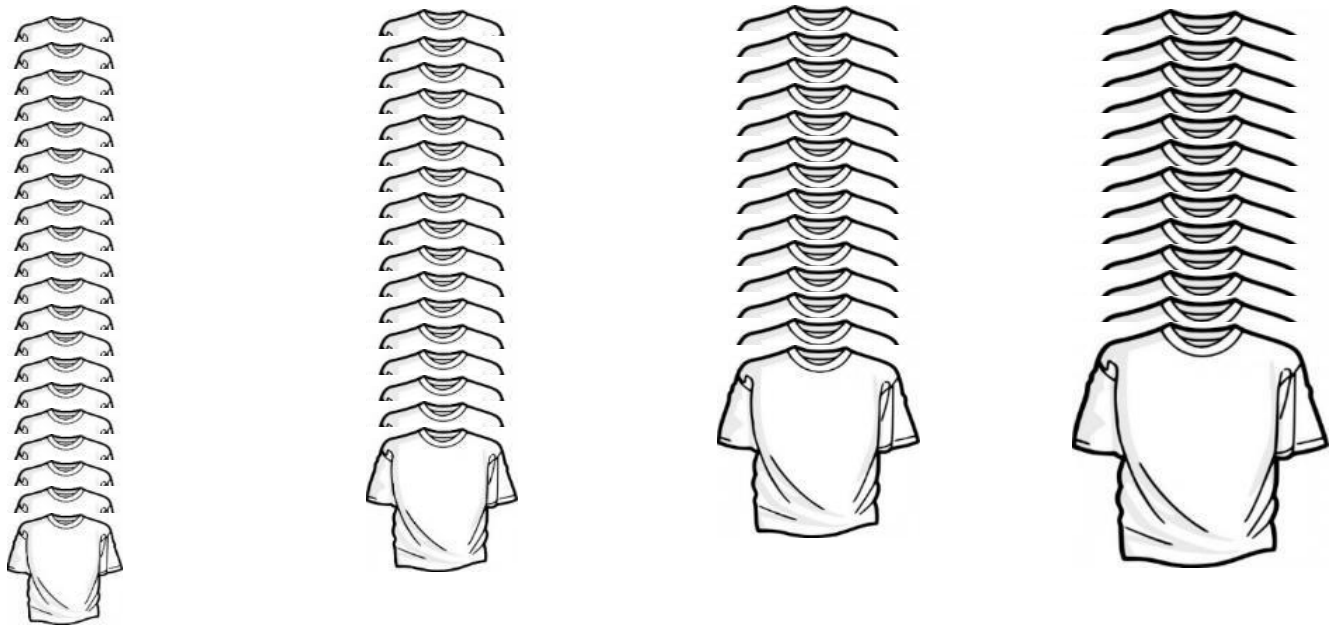

20 SM X 1 pts + 17 MED X 3 pts + 14 LG X 8 pts + 13 X-L X 13 pts

Backlog = 352 pts

SM, MED and LG stories should be achievable within a single sprint XL stories are epics – they are too big to complete within a sprint, and must be broken down into multiple stories before the team can work on them

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

User stories should not be re-estimated unless their scope changes significantly

Situation

- Typically the backlog is **estimated somewhere near the start** of the project
- At this point the team is new and has the least knowledge of the complexity and implementation details of each piece of functionality
- As the team completes sprints and continues to learn and improve, **their knowledge continuously increases – this can lead the team to want to re-estimate** certain stories where the estimates are 'out of date'
- However, if the team re-estimates stories during sprint planning, they are effectively estimating the current sprint's stories with a much greater level of knowledge than they had when estimating the whole backlog
- This means the current sprint's **re-estimated stories are no longer sized relative to the rest of the backlog, which can skew velocity and release progress tracking**

Resolution

- When a team reaches this point, rather than re-estimate stories during sprint planning, there are two viable options:
  - **Run a session with the team to re-estimate all stories in the backlog (not recommended unless there are serious discrepancies in the backlog**, since this takes time away from the team's development activities)
  - **Accept that we probably have inaccuracies in all our existing estimations, and acknowledge that our velocity will gradually take that into account over time (recommended)**
- Further reading: https://dzone.com/articles/dont-estimate-stories-sprint

An exception to this rule is when the scope of a story has significantly changed – in this case it makes sense for the team to re-estimate, since the bulk of the story is new functionality

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Estimates are necessary to…

- Allow **us to predict** when a Sprint goal will be met, and therefore when a substantial increment of value will be delivered
- Help our stakeholders **plan ahead**. They are part of the value we provide.
- Help us **de-risk scope** of uncertain size and complexity
- Estimated **work can be traded in and out** of scope for other work of similar size. Without estimates you lose the ability to trade
- Gain **a better understanding** of what is needed to develop the solution. The very process of estimation adds value. When we estimate we discuss requirements in more detail.

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Due to the inherent 'Cone of Uncertainty' in software estimation, the estimates for the backlog are indicative rather than precise

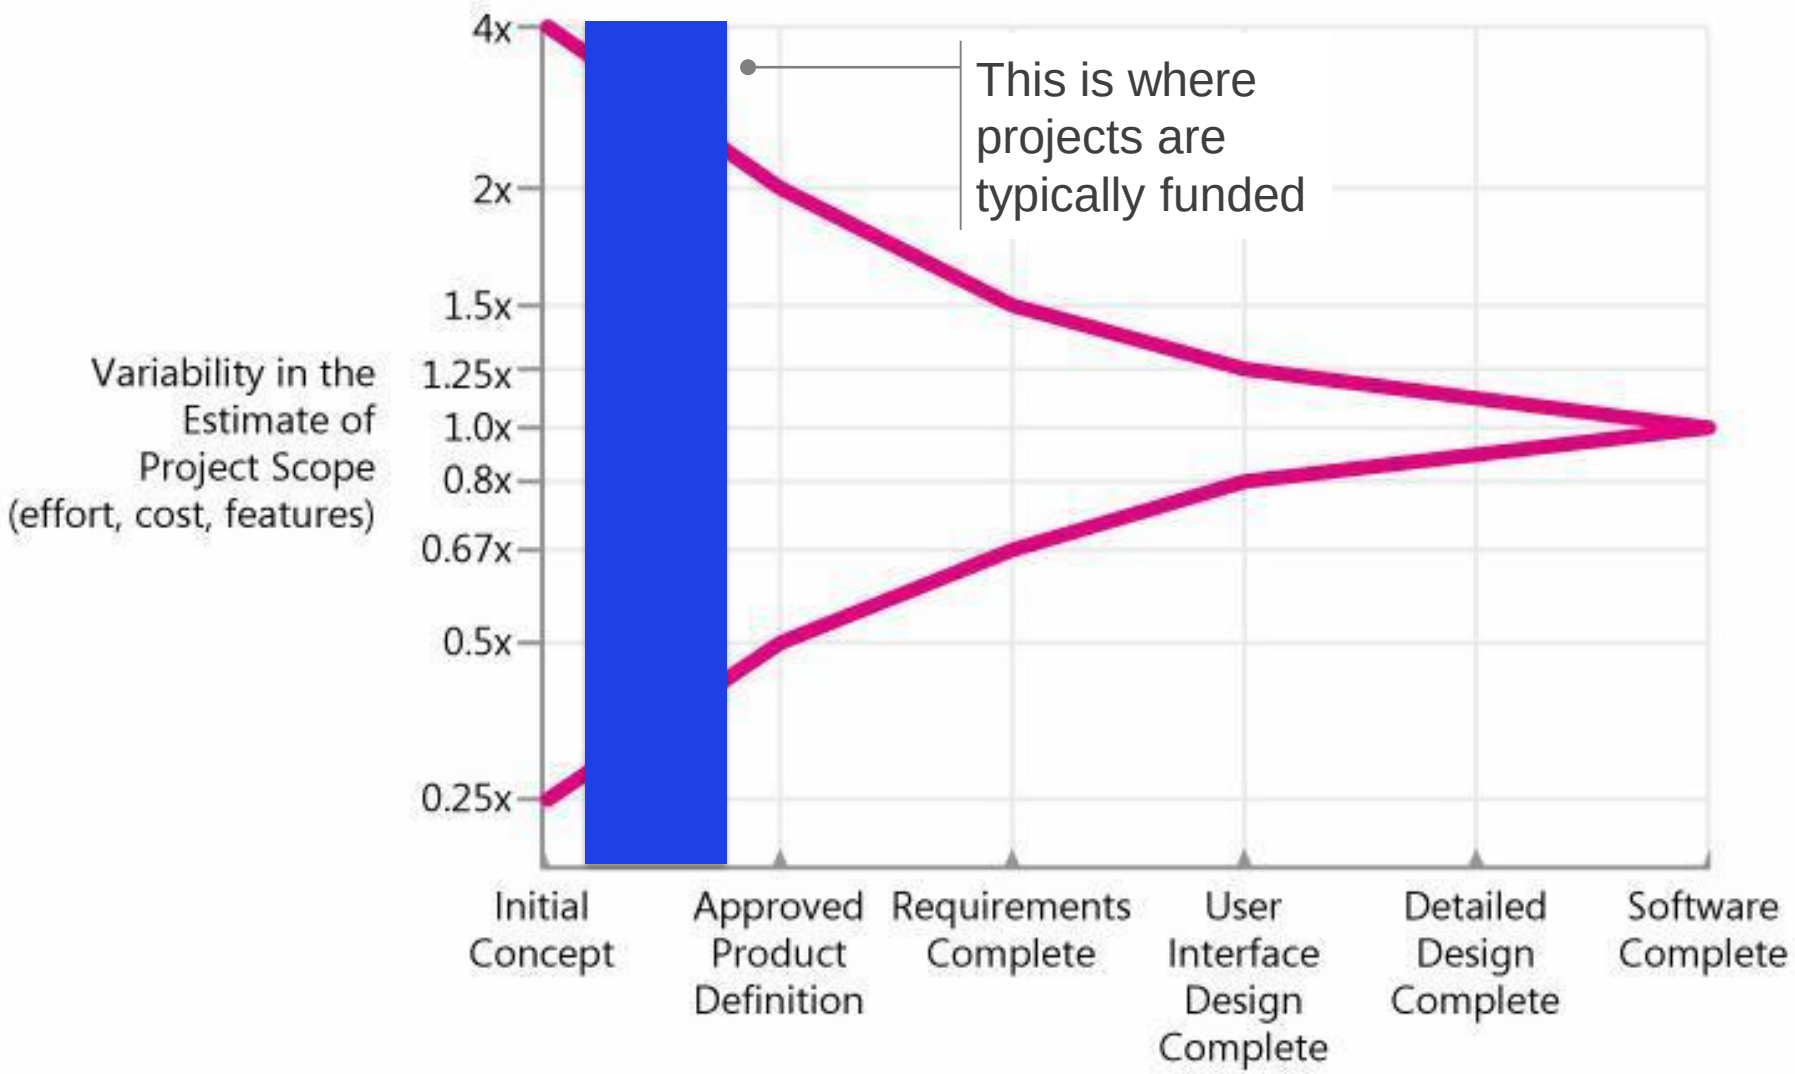

SOURCE: http://www.agilenutshell.com/cone_of_uncertainty

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

It is crucial that the team manages stakeholder expectations around backlog estimates

Estimates become commitments

- Many organisations confuse estimates with commitments
- Every estimate has a level of probability associated with it
- If an estimate states that X will be done by June 30th, this carries a level of probability as to whether it will be achieved (or not)
- Regardless of the probability, an estimate like this is passed around the organisation and becomes a commitment!
- However, if an estimate is a range, if conveys more explicitly there is probability associated with it.
- An range *is* a probability, a commitment cannot be made to a probability!
- Commitments are made to dates, estimates are made to ranges

Communicating forecasts

- Avoid estimates becoming commitments
- **Communicate with a range, not with a fixed point** (date or position in a backlog)
- But update the forecasts regularly after each iteration, and the range will converge as more knowledge is gained

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Components of the delivery roadmap

- **MVP design**
- Backlog build and management
- OKRs and squad metrics

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

The Journey Team should set key success metrics for the MVP to be incorporated in the business case

EXAMPLE

	Metric	Target
Reach	▪ **Migration rate for new process:** – Number of accounts opened through digital solution in-branch – % of accounts opened in-branch through digital solution (per branch level)	▪ **35% of total accounts opened in pilot branches will use our digital solution** – Assume 50% migration from customers ("low adoption" segments will have a 20% migration rate and "high adoption" segments will have an 80% migration rate) – Assumes that ~70% of account types are eligible (payroll account and Gold debit cards are out of scope for our MVP)
UX	▪ **Ease of use of digital solution:** – In-branch: % of accounts opened with minimal support from the greeter	▪ **40% of digital openings completed independently** – Assume "low adoption" segments will have a 0% completion rate with minimal assistance and "high adoption" segments will have an 70% completion rate with minimal assistance
	▪ **Satisfaction with account opening experience:** – % of satisfied users of digital solution (captured through question at end of process)	▪ **70% of clients satisfied with the process** – Current baseline for customer satisfaction with branch experience while opening a savings account is ~60% (top two boxes) and ~5% (bottom 2 boxes)
	▪ **Time for process:** – Average time the account opening process takes (traditional versus digital)	▪ **10 min or less to open an account** (depends on user testing results) – Current baseline is ~25 minutes including wait and service time

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Besides the key success metrics, the Journey Team will also track additional metrics

EXAMPLE

✓ Act upon Tracking ✗ Not tracking

	Metrics to track	MVP	Steady-state[1]
UX	▪ **Ease of use of digital solution:**		
	– In-branch: % of assisted account openings through digital solution	✓	✓
	– In-branch: % of drop-off rate per step of the process	✓	✓
	– Outsi		
	▪ **Satisfacti**		
	– % of s		
	– Satisf questi		
	▪ **Time for p**		
	– Avera		
	– Avera		
Customer behaviour	▪ **Product fit**		
	– % acc		
	▪ **Usage of**		
	– % of c		
Reliability	▪ **Outage tin**		
	– % time		
	▪ **Errors:**		
	– # of sy		
	▪ **Inventory:**		
	– # of in		

✓ Act upon Tracking ✗ Not tracking

	Metrics to track	MVP	Steady-state[1]
Reach	▪ **Adoption rate for new process:**		
	– Number of accounts opened through digital solution in-branch	✓	✓
	– Number of accounts opened through digital solution outside-branch	✗	✓
	– % of accounts opened in-branch through digital solution (per branch level)	✓	✓
Cost	▪ **Cost breakdown:**		
	– Breakdown of digital solution cost per account (vs traditional process)	Tracking	✓
Revenue	▪ **Total revenue generated per branch:**		
	– Number of products sold per AdVS per branch	Tracking	✓
	– Total revenues generated per AdVS per branch	Tracking	✓
	▪ **Cross sell rates of products associated to savings accounts:**		
	– % of accounts opened with insurance	✗	✓
	– % of accounts opened with debit cards	✗	✓
	▪ **Additional revenues from new digital solution:**		
	– Mix of product sales generated from digital solution	✗	✓
	– Increase in number of new accounts opened	✗	✓

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Refine Journey Team business case with Business Unit

	Details	Prep required	Teams involved	Example outputs
Align on approach	▪ **Align with stakeholders and teams on the source of value of the digital solution** – E.g. lift in customer experience, cost savings from reduced staffing, increased sales	▪ MVP scope defined	▪ Journey Team (owner) ▪ Support Committee ▪ Other teams (e.g. decision-makers from Finance, Capacity Planning, Branch)	
Gather data	▪ **Make data requests to teams to gather all required inputs** – E.g. breakdown of product types, information on capacity, revenue data	▪ Approach defined	▪ Journey Team (owner) ▪ Other teams (e.g. SMEs from Product, Capacity Planning, Branch)	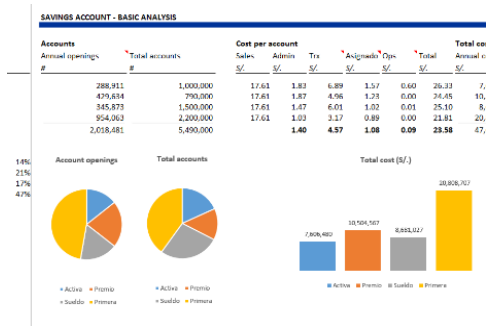
Validate findings & iterate	▪ **Conduct analysis, validate findings, and iterate as required** – E.g. create assumptions around migration rates; run numbers on potential reductions in staffing or lift in sales or delta in customer satisfaction	▪ Data gathered ▪ Approach and assumptions defined	▪ Journey Team (owner) ▪ Support Committee ▪ Other teams (e.g. decision-makers from Finance, Capacity Planning, Branch)	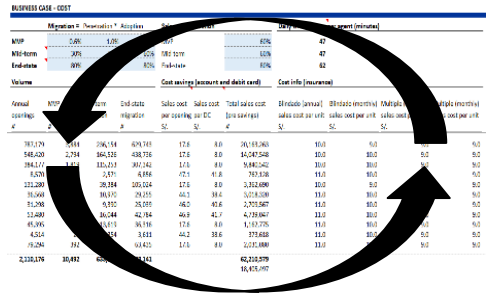

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Table of contents

What are the outputs for each journey, and how should each journey operationalize itself?

- Recap: Phases that each Journey Team undergoes
- B1. Aligning the target strategy with customer vision
- B2. Defining delivery roadmap
- **B3. Onboarding the team (i.e. Sprint 0)**
- Translating this into a sprint plan

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time

Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Components of onboarding (1/2)

Objective

Pre-Requisites

Deliverables

Mobilize the team: Ensure a common understanding of the process to be leveraged for the release
Owner: Scrum Master
Participants: Team, Product Owners

- Team staffed with all required skills needed
- Agile capabilities available to provide overview
- Entire team available for Sprint 0 including SME's and niche skills

Roles and Responsibilities: Scrum collapses roles and responsibilities to drive shared ownership, responsibility and quality in every sprint
Owner: Scrum Master
Participants: Team and Product Owner

- Introduction/training sessions for all participants
- Well defined roles to support the team
- Enough individuals with or working on acquiring required skill set

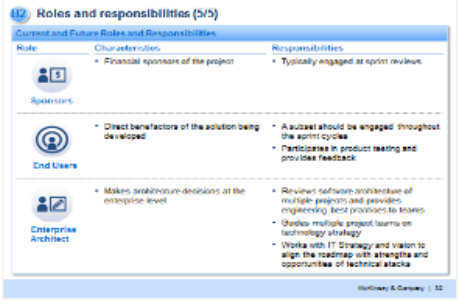

Establish team cadence and working norms: Agreement on how the team will work together and sprint cadence
Owner: Scrum Master
Participants: Team and Product Owner

- Team has shared space
- Team and leadership agree to follow agile principles
- Team collectively define working agreements

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Components of onboarding (2/2)

Objective

Pre-Requisites

Deliverables

Release Planning: Gain alignment between Stakeholders, Product Owner(s), and the team on what can be accomplished in the release and craft an initial release plan. Includes story point estimation of the backlog.
Owner: Scrum Master
Participants: Product Owner and Team

- Single product backlog with prioritized user stories and acceptance criteria

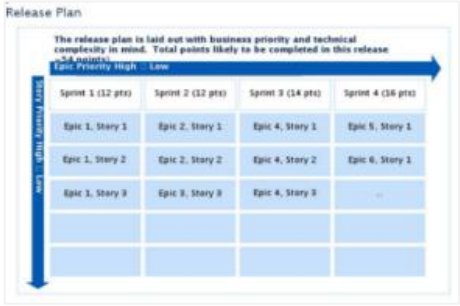

Environment set up: Have everything in place for the team to start development including environments and tools for every team member. One of the environment should be same as Production
Owner: Scrum Master
Participants: Team

- Introduction/training sessions for all participants
- Well defined roles to support the team
- Enough individuals with or working on acquiring required skill set

Working environ-ments and set up for the team to start developing following development best practices

Sprint 1 Planning:
Team creates sprint goal with the Product Owner and assess stories they can commit to base on definition of done and engineering best practices
Owner: Product Owner
Participants: Scrum Master and Team

- Product owner brings prioritized backlog with ready for work stories to be picked up in the sprint

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

During Sprint 0, the Delivery team has to align on several key items

Point for alignment	Description
Why are we here?	Why is the bank embarking upon this digital journey
How will we be working?	How the team will be working throughout the course of the project
Team kick-off	Meet-and-greet and team building for the full agile delivery team
Vision definition	Define the MVP scope based on the overall vision for the product
Initial product backlog	Define the initial product backlog (user stories) from the MVP
Release planning	Define a preliminary release plan based on the MVP goals and initial product backlog
Initial architecture design	Design the technical architecture based on the MVP goals
Environment setup	Set up the development environment so it is ready for Sprint 1
Agile development training	Train the team on test automation/TDD, pairing, Git & pull requests, etc.
DoD/DoR definition	Define the team's shared Definition of Done and Definition of Ready
Team norms and sprint cadence	Define team working agreements and sprint meeting cadence
Backlog estimation	Provide high-level (provisional) estimates on the stories in the product backlog

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Mobilize the team: the Delivery team should be staffed with the skills necessary to accomplish the product vision

Prep-aration

- Identify the skills needed for the product development; this includes PO team, Architect, Developers, QA, UX/UI)
- **Identify number of team members needed with each skill set. Keeping in mind engineering aspirations** (e.g., automated testing skills)

Activities

- Discuss team availability and skill sets needed with staffing managers
- Understand & identify skill constraints of team members
- For a distributed team, create a virtual team to enable collaboration and dedicate team focus within each location

Outcome

- Named team members with start dates confirmed
- **All team members are dedicated and available for Sprint 0**

Good Practices

- Teams are cross functional with required skills to develop and demonstrate completed stories at sprint end
- Has exactly one defined and dedicated PO, SM and Solution Architect
- **Co-located (within location) in an open space setting and create ability to talk to each other without scheduling meetings or leaving their desks**
- **Identify SM in each location to help syndicate the whole team**

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Roles and responsibilities: the Delivery team should be onboarded to ensure clear understanding of roles and responsibilities

Prep-aration

- Identify other leaders and stakeholders that will be involved in the process and engage them in the process
- Leverage the Agile Coach to help facilitate the sessions

Activities

- **Conduct session with the whole team to review and understand roles within Scrum and interactions with extended team**
- **Review the team composition, working model, and who will be fulfilling each role**
- Educate all team members and stake-holders (including leadership) about their roles and what will be required of them

Outcome

- Team members and stakeholders understand Scrum roles and have a sense of collective responsibility
- Team is established as self-organizing and is free from any command-and-control management

Good Practices

- Ensure the whole team attends the session (including distributed team members)
- **Find ways to engage the people who are remote throughout the session (e.g., video links, face card of speaking person and keeping track of speaker)**

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Roles and responsibilities: coaching plans should be set-up for key members of the team (SM, SA, PO)

Example coaching plan for Solution Architect

	Goal	Action items
Domain Expertise	▪ Balance architectural knowledge with hands-on development and coaching	▪ Work on coding tasks ▪ Pair on coding/reviews with other team members
Agile Expertise	▪ Learn how to effectively apply agile practices at the team level ▪ Embrace new ideas and be open to evolutionary architectural design	▪ Promote ‘agile discipline’ within the team (e.g. automated test coverage, peer reviews, refactoring, helping people meet DoD) ▪ Partner with PO and SM to understand the backlog and ensure technical requirements are covered
Individual skills	▪ Embrace collaborative way of working within and outside the team ▪ Become a trusted thought partner for other team members	▪ Spend time with people to understand strengths and coaching needs ▪ Influence the team as a knowledgeable peer (not a ‘boss giving orders’)
Mindset & behaviors	▪ Promote continuous improvement and learning within the team	▪ Encourage the team to spend time on learning and self-improvement ▪ Identify ways to improve the development process

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Roles and responsibilities: check-list

- Product Owner (PO) and proxies clearly understand their role and responsibilities, how to execute their responsibilities on the team, and how to drive the direction for the release
- Scrum Master (SM) clearly understands their role, responsibilities, and expectations; SM has capabilities to execute responsibilities and work closely with the Scrum team
- Scrum Team is cross-functional and includes all the required skills to design, develop and test completed stories at the end of each sprint; team has a defined PO team and a defined SM

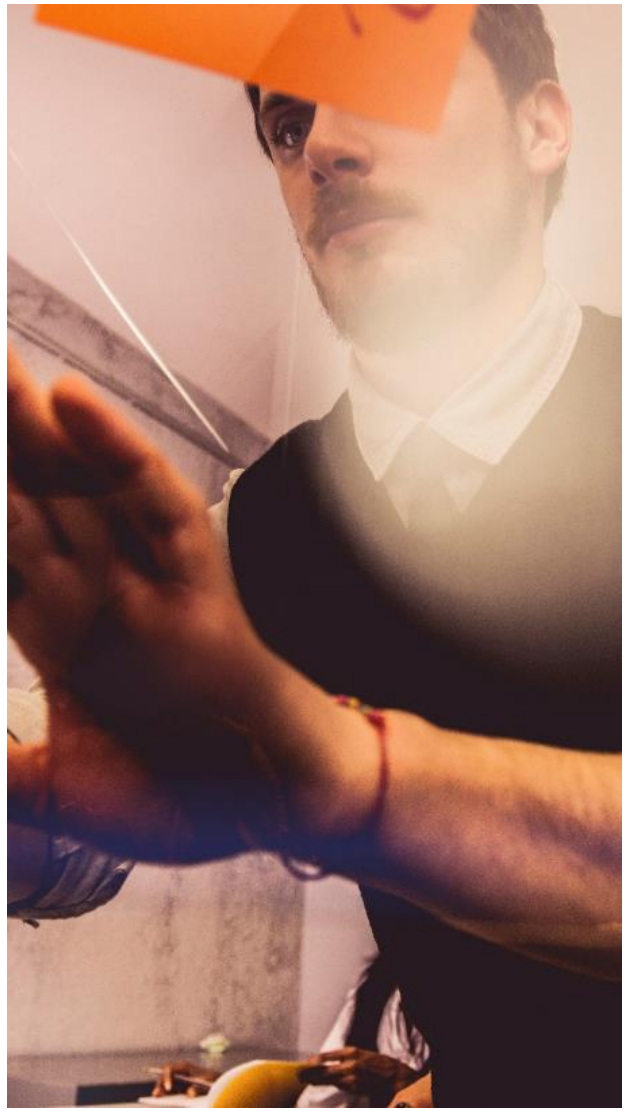

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Establish team cadence and norms: the team should create a shared ‘definition of done’ to ensure quality and completeness

- A **definition of done** ensure that the working software produced at the end of the sprint is of high quality and potentially shippable
- Teams typically start with a simple definition of done and slowly evolve as they have a stable sustained velocity

A user story is “done” in an iteration when (NOT an exhaustive list)…..

- Build created and deployed into truck
- Unit test coverage is 90%
- Code reviewed and tested by dev
- Approved by Product Owner
- All acceptance criteria are met
- Required documents updated
- No defects in the backlog are high or critical
- Performance accepted and signed off
- Regression testing complete
- Etc.

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Establish team cadence and norms: the team should create a shared ‘definition of ready’ to ensure stories are ready to be worked on

- **Definition of ready** ensures that everyone knows when work is ready to be taken into a sprint, or when all necessary conditions are right for a team to start a sprint

Some examples for reference (NOT an exhaustive list):

- Story defined and written
- Acceptance criteria clearly defined
- Dependencies identified
- Story sized by the development team
- Performance criteria identified
- Team has a good idea on how to demo the story

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Release planning: the team should create a release plan during Sprint 0

Preparation

- **Business vision and scope exist and have been validated by Product owner team and syndicated with leadership**
- Core team members have been identified and staffed; full team attends release planning session
- Product owner has a backlog with prioritized list of stories and well-defined acceptance criteria

Activities

- Product Owner shares stories and acceptance criteria
- Team agrees on Definition of Done and Ready for Work
- Scrum team estimate story size
- **Team identifies stories for sprint 1 based on an assumed capacity**
- Team extrapolates the assumed velocity for the number of sprints in the release based on estimated capacity
- Team will take first 2-3 sprints to determine average velocity of team. Product Owner and team to adjust release plan each sprint based on average velocity.
- While sizing stories team identifies assumptions, risks and potential solutions

Outcome

- Release Plan – Initial plan based on the knowledge team has today; prioritized stories slotted to sprints
- Assumptions, risks, dependencies identified

Good Practices

- Utilize affinity sizing or Poker planning to size stories.
- Relative sizing techniques levels the field for all team members and holds them equally accountable
- **For new teams conduct a sizing exercise (fruit salad) to help them understand the estimation concepts**
- **Poker planning tool for distributed teams:** http://www.planningpoker.com/
- **Planning poker cards created for local team**

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Release planning – Use story points to indicate complexity and effort

What are story points?

- **Team's own** relative estimate (compared to previous tasks) of the size and complexity of a task, not just duration
- **A new unit of work** different from traditional measures like hours – consistent with time – which enables performance follow-up

What are these not used for?

- Measurement of individual productivity
- Environments with highly standard and repeatable work
- Comparing productivity/progress of two different teams

Example: Product backlog

User story A – Points: 3

User story B – Points: 13

Technical Spike A – Points: 8

User story C – Points: 21

User story D – Points: 2

User story E – Points: 5

User story F – Points: 2

Technical Spike B – Points: 8

User story G – Points: 13

- We can see right away
  - Which work item cost the most
  - Total size of all the work
  - Total size of an iteration
- Ideally anything more than a 16 needs to be further broken down

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Release planning – Play planning poker, a team game that allocates points to stories and fosters team commitment and knowledge sharing

Team agrees on points system to use (e.g., Fibonacci series: 1, 2, 3, 5, 8, 13, 21)

1. A team member provides a quick overview of the user story to be sized
2. Each team member independently estimates the level of effort in story points relative to a baseline user story
3. Team votes and members with maximum/minimum scores provide rationale for score to other team members
4. Team votes again and once consensus is reached story points are assigned

- Ensure sizes are relative (e.g., if feature A is twice as difficult as feature B it should get twice as many points)
- Evaluators should consider the comprehensive effort of implementing the feature (e.g., design, development and unit testing)

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Release planning – Use expected velocity to estimate number of sprints required to deliver the product goals to assess high-level feasibility of schedule

ILLUSTRATIVE

Velocity estimation

- Velocity is **number of story points** the team completes in a sprint
- **Calculate velocity by summing** the number of story points assigned to each user story the team completes during the iteration
- Because **story point are relative measure**, it does not matter if team works on two 5 point stories or 5 two point stories
- By **summing the total story points** estimates of all desired features, we can come up with total size estimate for release
- If we know the team's velocity, **we can divide size by velocity to arrive at an estimated number of** iterations and turn this **duration into a schedule by** mapping it to a calendar
- If the team is new, use the first 2-3 sprints to determine average velocity of team. Product Owner and team to adjust release plan each sprint based on average velocity

Illustrative approach

- Present team with a stack of stories (estimates hidden)
- Add stories one-at-a-time until the team determines no more can fit
- Record the estimates for the stories the team can make
- Repeat several times, expecting to converge after several iterations

Prioritized Story List	Prioritized Story List
Story 1 - 5 points	Story 1 - 5 points
Story 2 - 3 points	Story 2 - 3 points
Story 3 - 1 points	Story 3 - 1 points
Story 4 - 2 points	Story 4 - 2 points
Story 5 - 3 points	Story 5 - 3 points

If velocity = 12, we can get these stories

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Release planning – Build and share a product roadmap for the release from previous story mapping exercise

EXAMPLE

Business value high → low

Story priority high → low

Sprint 1	Sprint 2	Sprint 3	Sprint 4
Story 1	Story 4	Story xx	Story xx
Story 2	Story 7	Story xx	Story xx
Story 3	Story xx	Story xx	…
	Story xx		
	Story xx		

- Release plan during Sprint 0 is based on an estimated velocity
- It is revised at the end of every sprint using the actual velocity of the team
- The release plan is laid out with business priority and technical complexity in mind

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Release planning – Choose relevant metrics that will inform actionable next steps for each impact area

EXAMPLE

Impact area	KPI description	Examples	Frequency of measurement
Time to market	▪ On-time delivery ▪ Speed	▪ % initiatives delivered on time ▪ Average time-to-market ▪ Average time-to-demo	▪ Monthly ▪ Monthly ▪ Monthly
Progress towards release	▪ Release burn-up	▪ Story points completed to date compared to total release	▪ Weekly
Quality	▪ Delivery ▪ Accuracy	▪ Overall defect rate ▪ % of user story / requirement growth by initiative	▪ Weekly ▪ Weekly
Maturity org. skillset	▪ Agile adoption ▪ Team velocity	▪ % Agile teams ▪ Variance in team velocity	▪ Monthly ▪ Weekly

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Table of contents

What are the outputs for each journey, and how should each journey operationalize itself?

- Recap: Phases that each Journey Team undergoes
- B1. Aligning the target strategy with customer vision
- B2. Defining delivery roadmap
- B3. Onboarding the team (i.e. Sprint 0)
- **Translating this into a sprint plan**

Last Modified 11/27/2019 5:44 PM Malay Peninsula Standard Time

Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Sample Incubation sprint plan for Commercial Lending Journey Team

PRELIMINARY

Key outcomes	Sprint deliverables 1 (Wk 9-10: 29 Apr -12 May)	2 (Wk 11-12:13-26 May)	3 (Wk 13-14:27 May- 9 June)	4 (Wk 15-16:10-23 June)
A Design	▪ Collision workshop completed as initial impetus for ideas ▪ Initial customer interviews completed ▪ Initial planning for Design System completed"	▪ Digitized personas, as-is and current journeys ▪ Preliminary scribbles and wireframes ▪ First round of customer / RM testing completed (~4 customers, 4 RMs) ▪ First version of clickable prototype created (in InVision)	▪ Updated clickable prototype (InVision) after iterations ▪ Learnings from testing sessions summarized ▪ Multiple rounds of customer / RM testing completed (add'l 8 customers, 8 RMs) ▪ UI / Visual Designs on key screens ▪ Design System - initial components created ▪ Additional workshop / gallery walk completed	▪ High fidelity clickable prototype (InVision) ready ▪ Customer and RM testing in incubation completed ▪ Learnings from testing sessions summarized ▪ Visual designs of key screens completed ▪ Design support on User Stories ▪ Additional components integrated into Design System
B1 Technology - RM-assisted Web app	▪ Set of tools to be used for the RM-assisted journey finalized (WCMS, Leads Interaction, Leads Management) ▪ Procurement of tools initiated ▪ Architecture finalized and approval process w/ IT EAS initiated ▪ Draft APIs required for RM-assisted Web App	▪ Master Customer Data solution for corporate customers (by IT) creation initiated -- (dependent upon first set of screens designed) ▪ APIs required for RM-assisted Web app updated ▪ API development by IT initiated ▪ Set up of JIRA and Confluence complete	▪ On-boarding of Developers and Tech Leads completed (w/ Laptops and VPN connectivity) ▪ Seed micro-service creation kick-started and devops setup completed ▪ Seed front-end app created and devops setup completed ▪ Initial Backlog and Product specification created	▪ Handover documentation completed work ▪ Backlog prepared for both incubation setups ▪ All software and infrastructure procured ▪ IT dependencies resolved and planned for ▪ DevOps setup completed ▪ Budget approved for all Capex for Commercial Lending journey interventions
B2 Technology - Automation and workflow streamlining on BCS	▪ Assessment of options for OCR, NLP and RPA tools completed[1] ▪ Software tools to be used for OCR/NLP/RPA finalized ▪ Procurement of tools initiated ▪ Developer and Tech Lead resourcing for OCR/NLP/RPA tools initiated ▪ Complete architecture of OCR/NLP/RPA setup (including interfaces for manual validation, or Documentum etc.) defined and approval w/ IT EAS sought	▪ Set up of JIRA and Confluence complete[2]	▪ On-boarding of Developers and Tech Leads completed (w/ Laptops and VPN connectivity) ▪ Prototype for end-to-end automation and workflow streamlining for at 1 document completed ▪ Initial Backlog and Product specification created	
C Business elements	▪ Alignment of business team on plan for Incubation phase ▪ Locking in resources required from business ▪ Alignment of revenue and cost baseline and growth model with business team ▪ Preliminary alignment of metrics of evaluation	▪ Onboarding of members from Business completed ▪ Initial roadmap of testing ▪ Preliminary design of Model office construct ▪ Preliminary view of KPIs of MO members	▪ Preliminary approvals for 'roll-in' of critical functions in MO ▪ Preliminary view of Wave 1 test plan ▪ Alignment on the MO construct with Business ▪ Preliminary view on the measurement dashboards for MO ▪ KPIs for MO members finalized	▪ Model Office construct signed off ▪ Test plan finalized, and aligned with technology release plan ▪ Hypothesis of the MO scale plan aligned ▪ Impact estimation finalized ▪ Initial 'to-be' process maps for MO operations created
Tech enablement	▪ DevOps tools and Infrastructure Setup ▪ Sourcing strategy & options ▪ Vendor onboarding ▪ Backlog creation for infra setup	▪ Build mgmt. system created ▪ Backlog creation for Commercial journey initiated		

1 Dependency: at least 5 of each type of prioritized Document to be scanned and corresponding BCS fields to be automated
2 Dependency: prioritized set of documents for Automation journey

Last Modified 11/27/2019 5:44 PM Malay Peninsul
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time
