TRANSFORMING CUSTOMER JOURNEYS
Playbook

Talent

Recruiting pipeline

This playbook contains all the pieces and parts that make up our approach to transforming customer journeys. This is a living document and the latest version can be found on TCJ's Confluence site.

Last updated in May 2019

CIMB

How this module fits into overall TCJ Playbook

Recap: Roadmap of Journey Teams

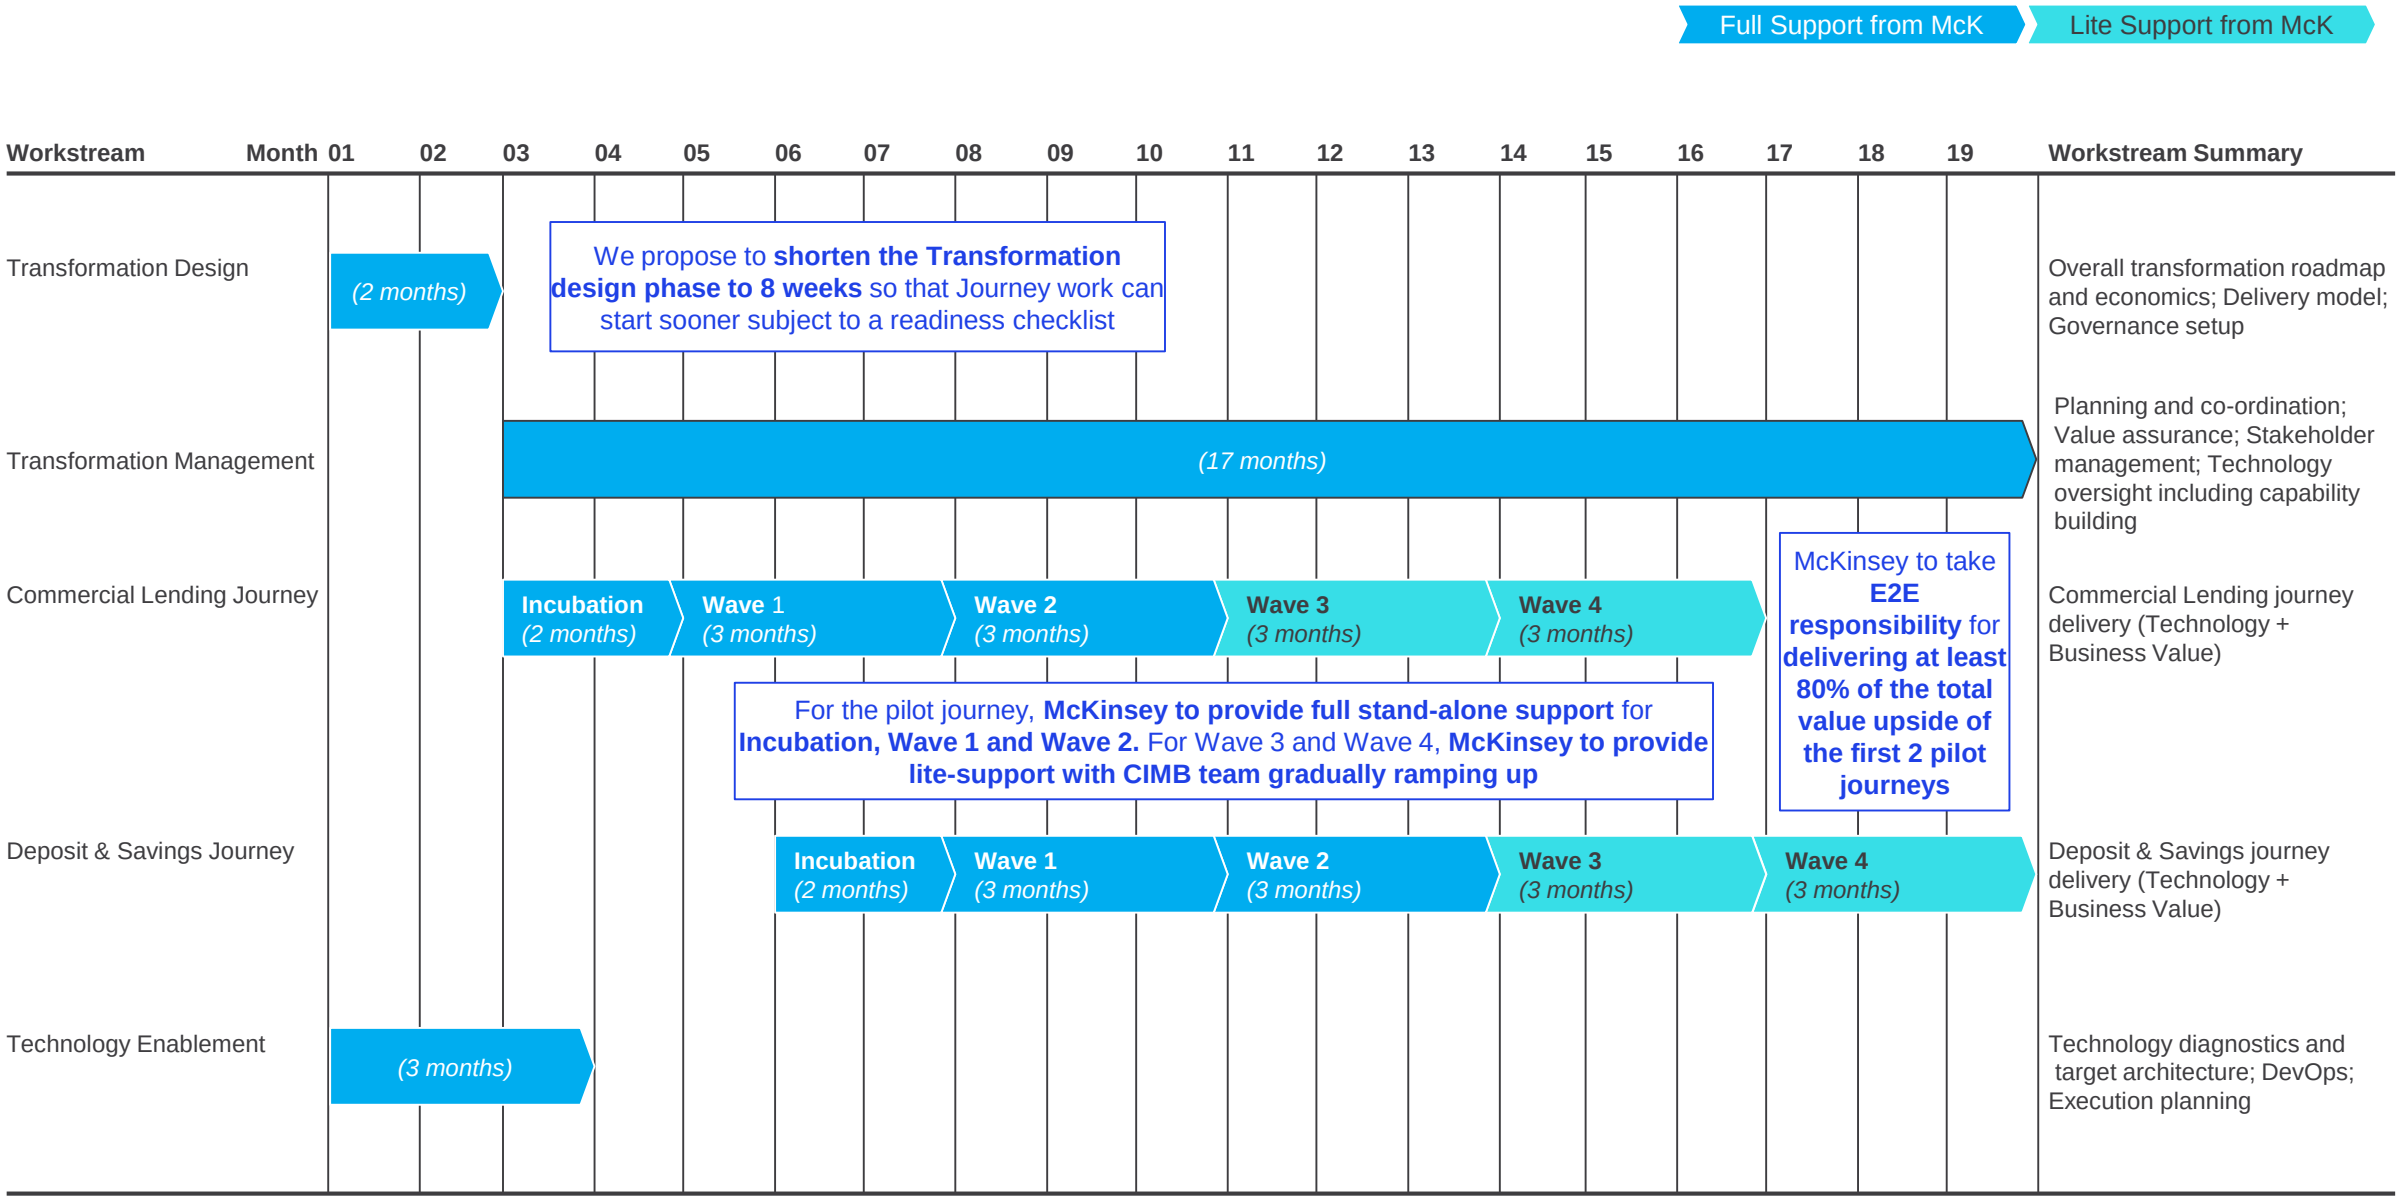

Table of Contents

How does TCJ manage the resource requirements for its Journey Teams?

- **Resource plan for each Journey Team**
- Managing the recruiting pipeline

Resource plan for Commercial Journey Team – Incubate phase

UPDATED AS OF 8-APR-2019

			Timing	M3-4			M5-7			
Org	**Source**	**Workstream**	**Resource Plan**	**Incubate**			**Wave 1**			**Date of joining**
				Requirement	Filled	Vacancy	Requirement	Filled	Vacancy	
Commercial Journey - Non-tech	CIMB TCJ (100%)	Transformation Management	Journey Lead	1	1	-	1	1	-	1-May
			Navigator	1	1	-	1	1	-	15-Apr
			Product owner	-	1	-	1	1	-	15-Apr
			Scrum Master	-	1	-	-	1	-	1-Apr
			Business Analyst	-		-	1	-	1	
		Operations	Operations Lead	-	-	-	0.5	-	0.5	
			Operations team	-		-	2.0	-	2.0	
			Subtotal (Business Team)	2.0	4.0	-	6.5	4.0	3.5	
	CIMB Business Subject Experts (30-50%)	Subject Matter Experts	Business Credit Risk	0.5	-	0.5	2.0	-	2.0	
			iCIMB Operations	0.5	-	0.5	0.5	-	0.5	
			Sales	0.5	-	0.5	0.5	-	0.5	
			Product Function	0.5	-	0.5	1	-	1	
			Legal and Compliance	0.5	-	0.5				
			Finance Function	0.5	-	0.5	0.5	-	0.5	
			Subtotal (SME Team)	3.0	-	3.0	4.5	-	4.5	
Commercial Journey - Technology	CIMB Tech	Technology	Enterprise Solution architect	0.5	-	0.5	1	-	1	
			IT PMO	1	1	-	1	1	-	1-Jun
			Dev Ops engineers	-		-	1	-	1	
			QAs	-		-	1	-	1	
		Design	Designers	-	2.0	-	-	2.0	-	
			Subtotal (TCJ Tech Team)	1.5	3.0	0.5	4.0	3.0	3.0	
	McKinsey Tech	Technology	Agile coach	1		1				
			Experience Design Lead	1		1				
			UI designer	1		1				
			Enterprise architect	1		1				
			Tech lead	1		1				
	Infosys Tech	Technology	Scrum master	1		1				
			Front end TL 1	1		1				
			Back end TL 2	1		1				
			DevOps / SRE	1		1				
			QA Lead	1		1				
			FE Dev	3.0		3.0				
			BE Dev	3.0		3.0				
			QA	1		1				
			Subtotal (McK/Infosys Tech Team)	16.0	-	16.0				
Journey Team - Total			**Grand Total (TCJ Journey Team)**	**22.5**	**7.0**	**19.5**				
TCJ Central	CIMB TCJ	Program Management and Value Assurance	Programme Director (lead)	1	1	-				
			Value Assurance	-	-	-				
			Finance PMO	2.0	-	2.0				
		Technology Delivery	Head of Tech Solution Delivery (lead)	1	1	-				
			Infra manager	-	-	-				
			Head Solution Architecture	-	-	-				
			Head Dev Ops	-	-	-				
		Design	Head of Design (lead)	-	1	-				1-Jul
TCJ Central Team - Total			**Grand Total (TCJ Central Team)**	**4.0**	**3.0**	**2.0**	**4.0**	**-**	**4.0**	

Updated file maintained on Box

https://mckinsey.box.com/s/3b5erj95d27dc9ypqox9gsxks4389d2f

Table of Contents

How does TCJ manage the resource requirements for its Journey Teams?

- Resource plan for each Journey Team
- **Managing the recruiting pipeline**

Process for managing recruiting pipeline

Step:	Plan	Sourcing	Screening	Onboard	Performance mgmt
	▪ TCJ Central Team HR prepares resource planning outlook for next 6 months (headcount, type of role) ▪ Journey Lead and Chapter Lead to refresh resource plan[1] (if any) ▪ TCJ Central Program Management to approve, based on resource budget ▪ Prepare role descriptions to use during sourcing (standard repository available, update if required)	▪ Trigger request with respective CIMB bodies – HR for new hires – Business for secondees – IT for secondees ▪ Trigger budgeting discussions with	▪ New hires: Screened profiles are interviewed by Journey Lead and Chapter Lead ▪ Secondees: During request discussions with Business and IT, review candidate profiles to ensure: – Meets competency level required – Has authority and can be accountable for decisions required by role	▪ New TCJ member undergoes defined onboarding process, led by Chapter Lead	▪ TCJ member selects career track and undergoes respective: – Capability building – Evaluations cycle ▪ <Detailed in separate playbook>
Frequency	▪ Monthly	▪ Monthly	▪ Continuous (based on latest sourcing pipeline)	▪ Continuous	▪ Continuous
Person-in-charge	▪ Led by TCJ Central HR ▪ Supported by Journey Lead and Chapter Lead	▪ Led by TCJ Central HR	▪ Coordinated by TCJ Central HR ▪ Supported by Journey Lead and Chapter Lead	▪ Chapter Lead	▪ Continuous

E2E pipeline is tracked by TCJ Central Team

1 Based on previous sprint retrospective and upcoming backlog
SOURCE: Team analysis

Track performance of hiring process, to identify and address any areas of underpeformance

Recruiting-related metrics (typically sourced via ATS)

Metrics	Objective
Application Completion Rate (%)	▪ Measure the success of job application platform and process. ▪ Provides actionable insights into the external momentum for various digital roles
Candidate Call Back Rate (%)	▪ Measure the success of recruiting efforts
Candidates per Hire	▪ Measure the effectiveness of recruitment efforts. Demonstrates internal momentum/ enthusiasm for bridging the digital skill gap
Cost per Hire ($)	▪ Measure the total spend associated with recruiting to fill an open position
Sourcing Channel Effectiveness	▪ Measures how much each of your sourcing channels (e.g., job boards, recruitment ads, sourcing tools, professional social networks, etc.) are contributing to pool of potential candidates
Fill Rate (%)	▪ Measure the total jobs filled divided by the number by the total jobs open
Time to Hire	▪ Measure the amount of time it takes to hire a candidate for a role. ▪ Provides insights into interview process efficiencies to ensure rapid hiring decisions
Job acceptance rate	▪ Provides line of sight into the ability to attract top digital talent ▪ If unsatisfactory, HR and digital leads should align on key reasons, e.g., growth opportunity, compensation etc. and address them, e.g., additional funds, new career path etc.

BACKUP

The initial phase will last 3 months, and will setup the program

Workstream	Resource Plan	M1	M2	M3	Comments
Transformation Office	Leadership	1.5	1.5	1.5	Accountable leadership
	Experts	2	2	2	Global experts from similar transformation
	Project Manager	1	1	-	PMO for setting up transformation
	Consultant	2	2	-	Consultant to support programsetup
	Solutions and Research	3	3	-	
	McKinsey – Subtotal (Transformation Office)	**9.5**	**9.5**	**3.5**	
Technology Enablement	Leadership	0.5	0.5	0.5	Technology Leadership from MDL
	Architect / Sr. Tech Lead	2	2	2	Senior Architect, and DevOps Lead
	Consultant	1	1	1	Consultant to support Tech Enablement Phase
	McKinsey – Subtotal (Tech Enablement)	**3.5**	**3.5**	**3.5**	
	McKinsey – Total (Phase 1)	**13**	**13**	**7**	

1 Consistent leadership team in place

Transformation Management (by TCJ Central Team)

Transformation Office	Resource	Month 1-3	Month 4-6	Month 6 onwards	Comments
Program Management	Program Managers	1	2	3-5	Coordinate across journeys, and organizational priorities
Value Assurance	Finance Team	1	2	3-5	Sizing of baseline and benefit calculations
Capability Build Function	Business roles industrialization	-	1	3-5	Acquire and develop top talent to take over McKinsey, coordinate with vendors – Business and Operations Roles
	Technology roles industrialization	-	1	3-5	Acquire & develop top talent to take over McKinsey, coordinate with vendors – Tech Roles
Technology industrialization / co-ordination	Solution Architect (Central IT)	1	1	3-5	Align journey architects with Central IT Architecture, and Technology Priorities
	IT PMO	1	1	2-3	Co-ordinate with Central IT teams priorities, roadmap and execution
	CIMB Total	**4**	**8**	**17-28**	

SOURCE: Proposal clarification document (2018)

CIMB Commercial Lending journey team by Waves

		M3-4	M5-7	M8-10	M11-13	M14-16	
Workstream	Resource Plan	**I**	**W1**	**W2**	**W3**	**W4**	**Comments**
Transformation Management	Journey Lead	1	1	1	1	1	Develop vision, goals, features and business value for lab
	Finance + PMO	2	1	1	1	1	Helps with building the business case, drawing down funding and keeping track of costs per Journey
	Navigator	1	1	1	2	2	Ensures overall alignment with key business stakeholders; takes over from McK team after wave 3-4
Product	Product owner	0	1	1	1	1	Develop vision, goals, features and business value for feature teams
	Business Analyst	0	0	2	2	2	Define the target end state of the service and write the epics associated to it
Delivery Management	Delivery Lead	1	1	1	1	1	Ensures lab is delivering at pace, de-bottlenecks any blockers and ensures timely escalation
	Scrum Master	0	0	1	1	1	IT PO to write epics and stories with the product owner to feed UX and engineers
Design	Lead Designer	0	0	1	1	1	Design target user experience and provide voice of customer research
	Designers	0	0	2	2	2	Lead the execution of designs
Data & Analytics	Data Analyst	0	1	1	2	2	Manage the data requirements, and Analytics for a better User Experience
Operations	Operations Lead	0.5	0.5	0.5	0.5	0.5	Work with different operations team for solution launch
	Operations team	0	2	3	7	7	Day to day operations
Marketing	Marketing Lead	0.5	0.5	0.5	0.5	0.5	Work with different marketing team for marketing launch
	Marketing team	0	1	2	2	2	Day to day marketing operations
Communications	Communications Lead	0	0.5	0.5	0.5	0.5	Communication strategy
	Comms / Copywriters	0	1	1	2	2	Copywriting
	Subtotal (Business Team)	**6**	**11.5**	**19.5**	**26.5**	**26.5**	
Technology	Solution architect	0.5	1	1	1	1	Provide the perspective of technical feasibility and define the technical roadmap
	Tech Lead	0	1	1	1	1	Work with solution architect to shape technical end-state for programme, coach developers
	Dev Ops engineers	0	1	1	2	2	Build DevOps pipeline, and manage infrastructure. Support developers in deployments
	FE Developers	0	0	3	6	6	Create high quality working software that delivers the release vision – Application Build
	BE Developers	0	0	3	6	6	Create high quality working software that delivers the release vision – Microservices
	Qas	0	1	2	4	4	Lead the execution the testing strategy for the release
	Subtotal (Tech Team)	**0.5**	**4**	**11**	**20**	**20**	
Subject Matter Experts	Business Credit Team	0.5	2	2	2	2	SME for Credit Risk
	iCIMB Operations	0.5	0.5	0.5	0.5	0.5	SME for Operational Risk
	Sales Manager	0.5	0.5	0.5	0.5	0.5	SME for Sales Process, etc.
	Product Function	0.5	1	1	0.5	0.5	SME for Product Construct, Pricing, Terms etc.
	Legal & Compliance Function	0.5	0.5	0.5	0.5	0.5	SME for Legal and Compliance (Bank & Group)
	Finance Function	0.5	0.5	0.5	0.5	0.5	SME for Finance
	Subtotal (SMEs)	**3**	**4.5**	**4.5**	**4**	**4**	
	Grand Total (Journey Team)	**9.5**	**20**	**35**	**50.5**	**50.5**	

SOURCE: Proposal clarification document (2018); updated based on team discussion

CIMB Deposit & Savings journey team by Waves

Workstream	Resource Plan	I	W1	W2	W3	W4	Comments
Transformation Management	Journey Lead	1	1	1	1	1	Develop vision, goals, features and business value for lab
	Finance + PMO	2	1	1	1	1	Helps with building the business case, drawing down funding and keeping track of costs per Journey
	Navigator	1	1	1	2	2	Ensures overall alignment with key business stakeholders; takes over from McK team after wave 3-4
Product	Product owner	0	1	1	1	1	Develop vision, goals, features and business value for feature teams
	Business Analyst	0	0	2	2	2	Define the target end state of the service and write the epics associated to it
Delivery Management	Delivery Lead	1	1	1	1	1	Ensures lab is delivering at pace, de-bottlenecks any blockers and ensures timely escalation
	Scrum Master	0	0	1	1	1	IT PO to write epics and stories with the product owner to feed UX and engineers
Design	Lead Designer	0	0	1	1	1	Design target user experience and provide voice of customer research
	Designers	0	0	2	2	2	Lead the execution of designs
Data & Analytics	Data Analyst	0	1	1	2	2	Manage the data requirements, and Analytics for a better User Experience
Operations	Operations Lead	0.5	0.5	0.5	0.5	0.5	Work with different operations team for solution launch
	Operations team	0	2	2	4	4	Day to day operations
Marketing	Marketing Lead	0.5	0.5	0.5	0.5	0.5	Work with different marketing team for marketing launch
	Marketing team	0	1	2	3	3	Day to day marketing operations
Communications	Communications Lead	0	0.5	0.5	0.5	0.5	Communication strategy
	Comms / Copywriters	0	1	1	2	2	Copywriting
	Subtotal (Business Team)	**6**	**11.5**	**18.5**	**24.5**	**24.5**	
Technology	Solution architect	0.5	1	1	1	1	Provide the perspective of technical feasibility and define the technical roadmap
	Tech Lead	0	1	1	1	1	Work with solution architect to shape technical end-state for programme, coach developers
	Dev Ops engineers	0	1	1	2	2	Build DevOps pipeline, and manage infrastructure. Support developers in deployments
	FE Developers	0	0	2	4	4	Create high quality working software that delivers the release vision – Application Build
	BE Developers	0	0	2	4	4	Create high quality working software that delivers the release vision – Microservices
	Qas	0	1	1	3	3	Lead the execution the testing strategy for the release
	Subtotal (Tech Team)	**0.5**	**4**	**8**	**15**	**15**	
Subject Matter Experts	Credit Risk Function	0	0	0	0	0	SME for Credit Risk
	Legal & Compliance Function	0.5	0.5	0.5	0.5	0.5	SME for Legal and Compliance (Bank & Group)
	Finance Function	0.5	0.5	0.5	0.5	0.5	SME for Finance
	Operational Risk (if relevant)	0.5	0.5	1	1	1	SME for Operational Risk
	Product Function	0.5	1	1	1	1	SME for Product Construct, Pricing, Terms etc.
	Subtotal (SMEs)	**2**	**2.5**	**3**	**3**	**3**	
	Grand Total (Journey Team)	**8.5**	**18**	**29.5**	**42.5**	**42.5**	

McKinsey support with an integrated team peaking at ~50 FTE

Workstream	Resource Plan	M3	M4	M5	M6	M7	M8	M9	M10	M11	M12	M13	M14	M15	M16	M17	M18	M19	Comments
Journey Teams (McKinsey)	Leadership[1]	1.5	1.5	1.5	1.5	1.5	1.5	1.5	1.5	1.5	1.5	1.5	1.5	1.5	1.5	1.5	1.5	1.5	Leadership oversight & value assurance
	Journey Leads	1	1	1	2	2	2	2	2	2	2	2	2	2	2	2	2	2	1 Journey Lead per Journey
	Experts	3	3	3	4	4	4	4	4	4	4	4	3	3	3	2	2	2	Global experts for each Journey, Transformation, Capability building
	Project Manager	1	1	1	2	2	2	2	2	2	2	2	2	2	2	1	1	1	1 PM per Journey
	Consultant	3	3	3	5	5	5	5	5	4	4	4	3	3	3	2	2	2	Consultant support per Journey
	Architect / Sr. Tech Lead	1	1	1	2	2	2	2	2	1.5	1.5	1.5	0.5	0.5	0.5	0.5	0.5	0.5	2 Senior Technologists across 2 Journeys
	Design Leadership	1	1	1	1.5	1.5	1.5	1.5	1.5	1	1	1	1	1	1	0.5	0.5	0.5	1 Design Lead per Journey Squad
	Designers	2	2	2	4	4	4	4	4	2	2	2	0	0	0	0	0	0	2x Designers per Journey Squad
	Agile Coach	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1 Agile Coach across 2 Journey Squads
	PO	1	1	1	2	2	2	2	2	2	2	2	2	2	2	1	1	1	1 PO per Journey
	Solutions and Research	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	Research and Solutions from similar global programs
	Agile Coach	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1 Agile Coach across Journeys
	McKinsey – Subtotal (Journeys)	**19.5**	**19.5**	**19.5**	**29**	**29**	**29**	**29**	**29**	**25**	**25**	**25**	**20**	**20**	**20**	**15.5**	**15.5**	**15.5**	
Sapient Team (Journeys)	Scrum Master	1	1	1	2	2	2	2	2	2	2	2	2	2	2	1	1	1	1 Scrum Master per Journey Squad
	Technical Leads	2	2	2	4	4	4	4	4	4	4	4	4	4	4	2	2	2	2x Technical Leads per Journey Squad
	Developers	0	0	6	6	6	12	12	12	9	9	9	6	6	6	3	3	3	6x developers per Journey Squad
	QA	0	0	3	3	3	6	6	6	4	4	4	2	2	2	1	1	1	3x developers per Journey Squad
	Sapient – Subtotal (Journeys)	3	3	12	15	15	24	24	24	19	19	19	14	14	14	7	7	7	
	Grand Total	**22.5**	**22.5**	**31.5**	**44**	**44**	**53**	**53**	**53**	**44**	**44**	**44**	**34**	**34**	**34**	**22.5**	**22.5**	**22.5**	

1 Consistent leadership team in place
