TRANSFORMING CUSTOMER JOURNEYS
Playbook

Journey Team Guide

Waves

This playbook contains all the pieces and parts that make up our approach to transforming customer journeys. This is a living document and the latest version can be found on TCJ's Confluence site.

Last updated in May 2019

CIMB

How this module fits into overall TCJ Playbook

Last Modified 11/27/2019 5:46 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

What this module covers

What are the outputs for each journey during Waves Phase? How should each journey operationalize itself?

- **Recap: Phases that each Journey Team undergoes**
- C1. Implementation and test
- C2. Deployment of the solution in the IT infrastructure
- C3. Roll out of solution to business

Last Modified 11/27/2019 5:46 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

The journey transformation is delivered over three phases: Understand, Incubation and Waves

Detailed in this playbook

	2 months	2 months	4 waves x 3 months each	
Journey Phases	**A. Design Phase**	**B. Incubate Phase**	**C. Waves**	
			Design and Pilot	Roll in and scale
Activity	▪ Initial analysis based on internal and external sources of insight ▪ Process diagnostic ▪ Revenue and cost baselining ▪ Identify and detailing of key interventions ▪ Refine bottom-up impact estimates ▪ Planning and road-mapping	▪ Build collective understanding of the current journey from customers perspective ▪ 'Zero based design' based on informed leadership choice ▪ Identify and validate the levers for change ▪ Business case definition backed with empirical data ▪ Planning and road-mapping	▪ Build the 'minimum viable solution' (tech or non-tech) ▪ Deploy, test and learn and iterate with customers ▪ Prepare to scale	▪ Roll in volume and people into the Lab ▪ New features and product improvements developed in agile way and released regularly ▪ IT industrialisation
Outcome	▪ Initial blueprint for prioritized journeys: – As-is journey, pain points/ opportunities – KPI definition & potential impact assessment – High-level implementation plan/ investments ▪ Final product roadmap with overall plan by waves ▪ Harmonized portfolio of initiatives (between TCJ and BAU) ▪ Target IT architecture ▪ High-level technology buildout plan	▪ High level target architecture and high level operations model ▪ Target state re-design of journey including principles and customer vision ▪ Roadmap of change ▪ Validation of hypothesis through customer insight / research ▪ The zero-based approach covers product, policy, and processes	▪ Evidence of new leadership behaviours / ways of working ▪ Validated learning on baseline benefits, feasibility and customer benefits	▪ Functioning journey with supporting technology ops model ▪ Ops model for moving from E2E to BAU ▪ Metrics and tracking ▪ Aligned leadership purpose

Last Modified 11/27/2019 5:46 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

C. The Waves will focus on implementing the solution in an Agile way, test it and roll out to the business

Key workstreams	C1. Implementation and test of the solution	C2. Deployment of the solution in the IT infrastructure	C3. Roll out the solution to the business
Activities	▪ Development of solution (code) ▪ Functional and Non-functional testing ▪ Agile Sprint ceremonies (e.g., backlog grooming)	▪ Detailed definition of required IT Infrastructure and mapping to existing infrastructure ▪ Implementation readiness activities (e.g., governance forums) ▪ Configuration of environments ▪ Build and test of environments ▪ Deployment of working code	▪ Definition plan to roll in the solution ▪ Conduction workshops with business reps ▪ Interlock with senior business stakeholders ▪ Business readiness activities (e.g., Go No-go sessions)
Deliverables	▪ Revised versions of product roadmap incl. MVP, sub-journeys ▪ Feature build plan inc. major dependencies ▪ Test plan ▪ Feedback from user groups and user testing ▪ MVPs/ working software	▪ Detailed IT Development plan, IT critical path, dependencies ▪ Implementation readiness deliverables (e.g., readiness checklist) ▪ List of risks and mitigations	▪ Business industrialisation strategy ▪ Benefits capture plan ▪ Detailed E2E plan ▪ For each segment where the solution is rolled in to: – Detailed roll in delivery plan – Training plan for operations – Business readiness – Transition/Capacity plan (if rolling into existing operation) ▪ Definition of KPIs/MI ▪ List of risks and mitigation

Last Modified 11/27/2019 5:46 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

What this module covers

What are the outputs for each journey during Waves Phase? How should each journey operationalize itself?

- Recap: Phases that each Journey Team undergoes
- **C1. Implementation and test**
- C2. Deployment of the solution in the IT infrastructure
- C3. Roll out of solution to business

Last Modified 11/27/2019 5:46 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

A clear set of activities are defined for each Journey Team across Agile build, Test & Learn and Product shaping

Process flow
Give input
Participate
Team led by Product Owner
Team led by Delivery Lead
Activity
Session

Journey Team operating model – Flow and main activities

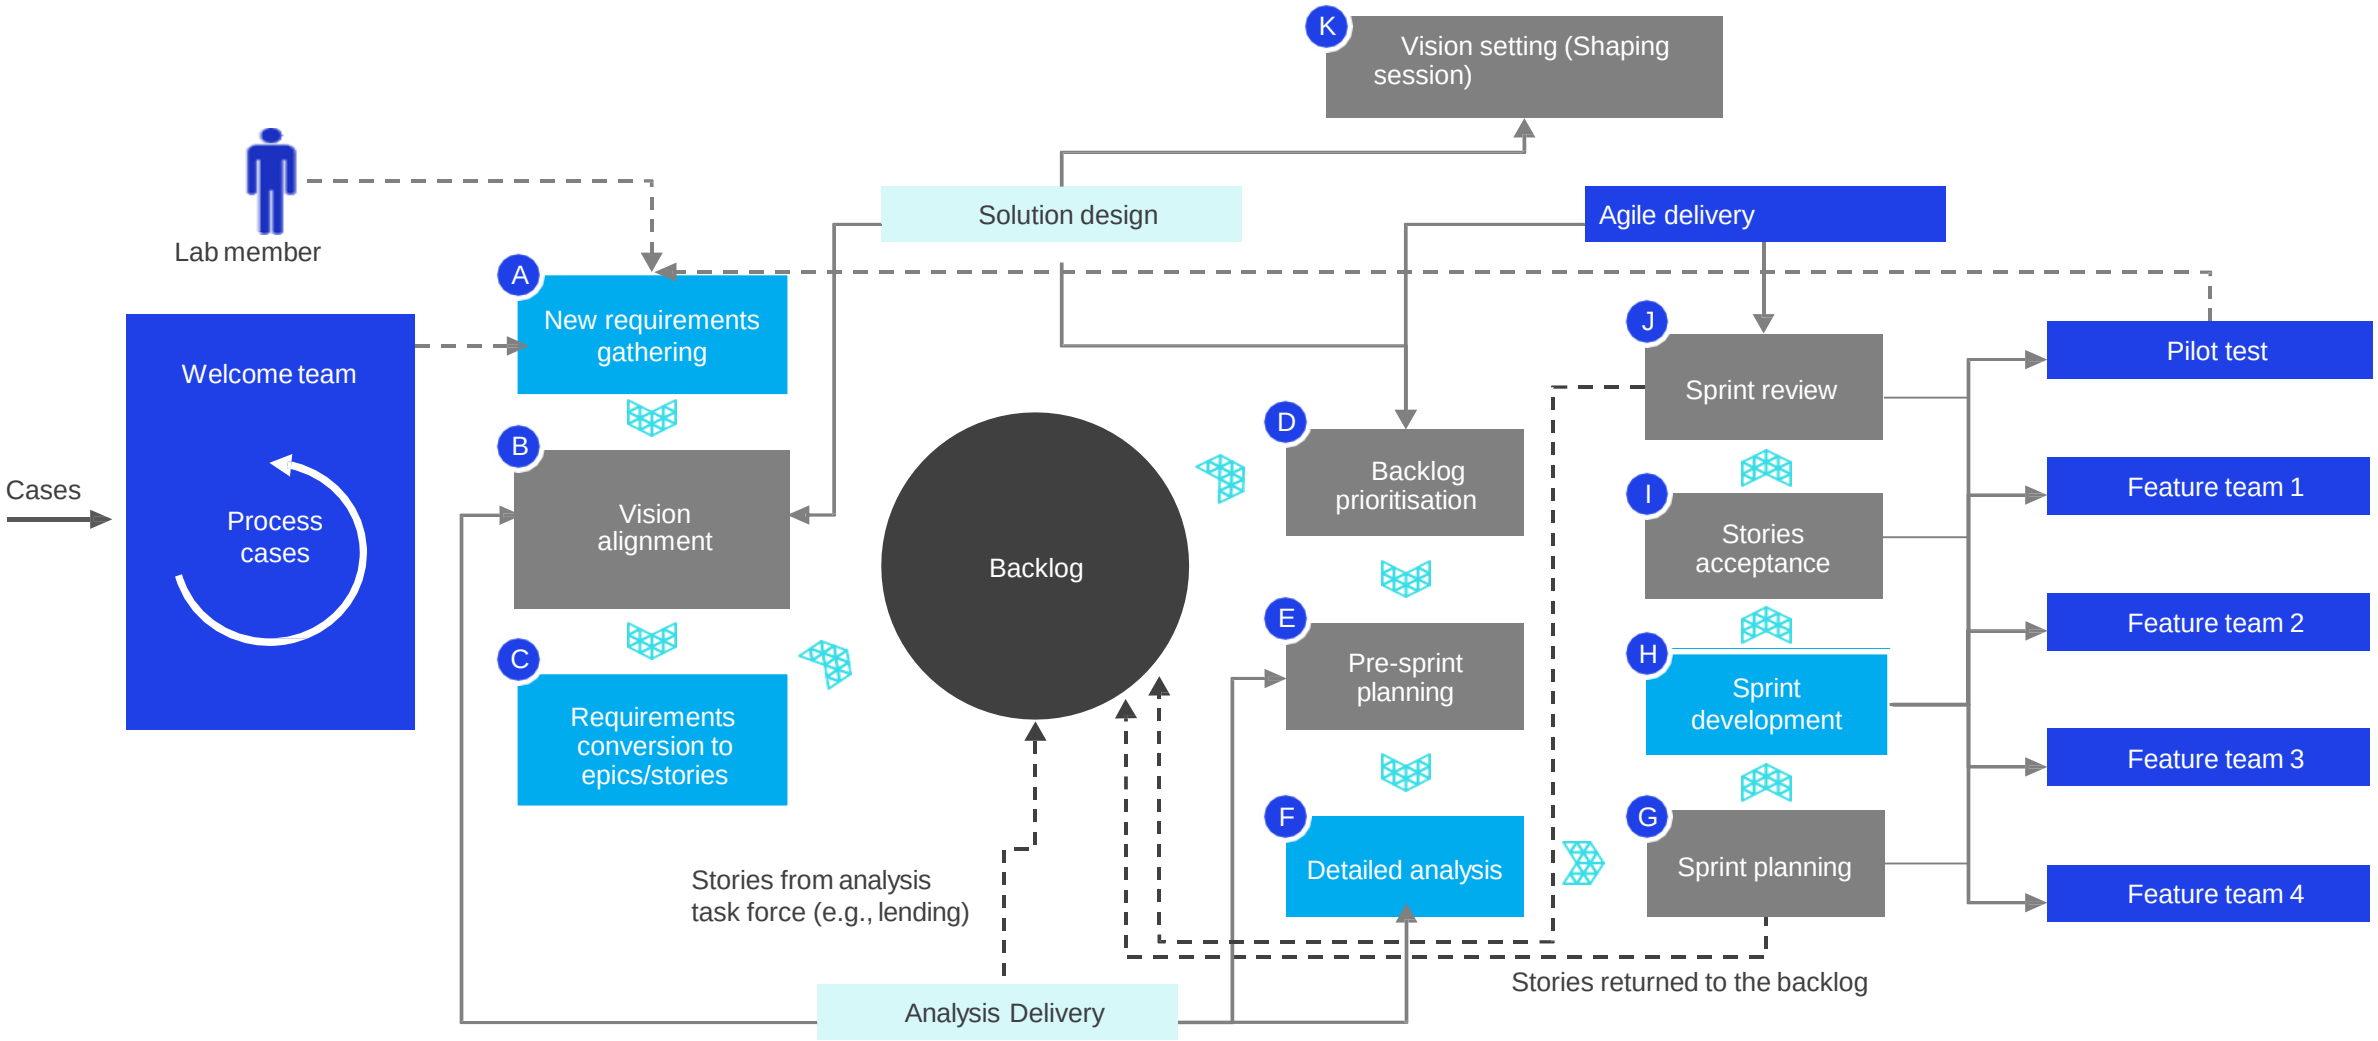

SOURCE: McKinsey

Last Modified 11/27/2019 5:46 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Detail of activities and sessions (1/11)

Epics | User Story | Improvement
Idea | Technical Task | Bugs/Investigation

Activities	Description	Participants	Frequency	Inputs	Outputs
A New requirements gathering	▪ Gather new requirements generated across the Lab ▪ Collected in Jira as new 'ideas'	▪ Welcome Team ▪ Experiments ▪ Lab member	▪ Ongoing	▪ Inputs from: – End-state vision – Welcome team feed-back (test & learn) – Experiments – Ideas from Lab members	▪ Jira new ideas (status 'Open')

Backlog Grooming Activities

Lab Innovation

Process Summary

1. Lab Members (Welcome Team, Experiments, Analysts, etc), stakeholder or other person involved identifies a potential change or improvement to target process, technology, operating model other aspects of the Lab
2. Lab Member creates new 'idea' in the Jira lab instance completing basic information
   - Summary of idea
   - Description of details and possible benefits
   - Impacted users (e.g., Welcome Team, Customer, Lab)
   - Link to any existing epics/stories (optional)
   - Additional details automatically recorded (reporter, created date, initial status

SOURCE: McKinsey

Last Modified 11/27/2019 5:46 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Detail of activities and sessions (2/11)

Epics | User Story | Improvement | Idea | Technical Task | Bugs/Investigation

Activities	Description	Participants	Frequency	Inputs	Outputs
B Vision alignment	▪ Evaluate ideas and asses in fit with the vision and end state	▪ PO (chair) ▪ Backlog owner ▪ Senior analyst ▪ IT arch. lead ▪ CX lead ▪ Bus. arch. Lead	▪ Fortnightly	▪ New ideas – Jira filter: 'Open Ideas'	▪ Reviewed and prioritised list of ideas – Status – Assignee – Wave Delivery – Wave Priority

Backlog Grooming Activities

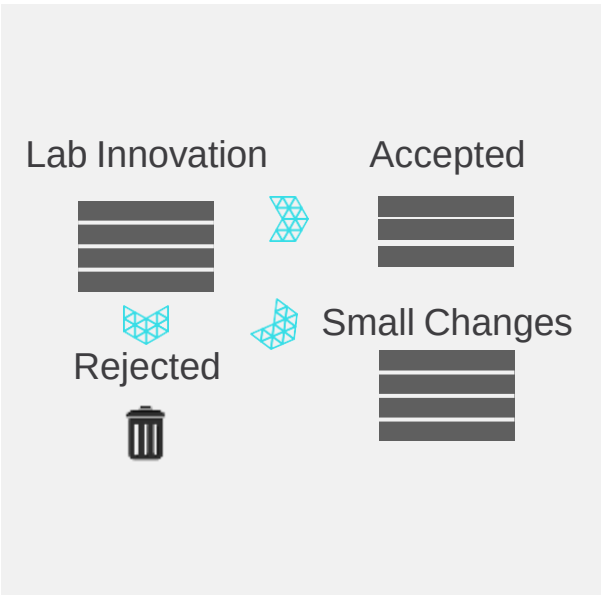

Process Summary

Preparation

1. PO regularly grooms of open ideas in Jira ("Idea backlog") making any obvious decisions
2. Lead Analyst regularly reviews to add any relevant information to ideas

Vision Alignment meeting

3. Review each open idea in Jira (filter: issue type = 'idea' and status = 'open')
4. Evaluate relevant merits and benefits of suggested ideas to decide next action
   - Accepted – idea has sufficient merit to be considered for development (progressed onto backlog). Target wave, priority and other information captured
   - Small Change – low-effort improvements to existing feature
   - Rejected – idea lacks sufficient merit to be taken forwards at this time
   - Clarification – further details are required before evaluation. Updated before next meeting

SOURCE: McKinsey

Last Modified 11/27/2019 5:46 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Detail of activities and sessions (3/11)

Epics | User Story | Improvement | Idea | Technical Task | Bugs/Investigation

Activities	Description	Participants	Frequency	Inputs	Outputs
C Requirements conversion to epics/stories	▪ Convert ideas into to epics/stories. Include: – Delivery T-shirt sizing – Required analysis – Estimation of the benefits	▪ Senior analyst ▪ Analysts (if required)	▪ Ongoing	▪ Accepted and prioritised ideas – Jira Filter: 'Accepted Ideas' (expand) – Jira Filter: 'Clarify Ideas' (further work)	▪ New epics and stories added into backlog linked to original idea

Backlog Grooming Activities

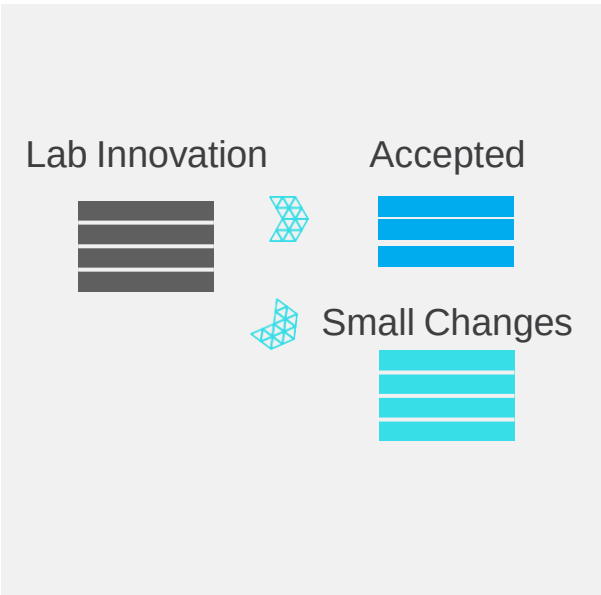

Process Summary

1. Senior Analysts reviews Accepted ideas and create user stories to be added to backlog
   - Review each accepted idea (Jira filter: issue type = 'idea' and status = 'accepted')
   - Creates relevant epic / user stories to deliver idea (linking new items to idea) adding them to backlog
   - Idea in Jira is closed
2. Senior Analysts reviews Small Changes ideas and adds change request to backlog
   - Review each small change idea (filter: issue type = 'idea' and status = 'small change')
   - Creates request to deliver change (linking new items to idea) adding them to backlog
   - Idea in Jira is closed

Last Modified 11/27/2019 5:46 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

SOURCE: McKinsey

Detail of activities and sessions (4/11)

Epics | User Story | Improvement | Idea | Technical Task | Bugs/Investigation

Activities	Description	Participants	Frequency	Inputs	Outputs
D Backlog prioritization	▪ Prioritise new Epics/stories in the existing backlog ▪ Address major dependencies (e.g. sequence, technical constraints)	▪ PO (chair) ▪ Backlog owner ▪ Scrum lead ▪ Senior Analyst ▪ IT arch. lead	▪ Fortnightly	▪ Stories recently added to backlog – Jira filter: 'New stories'	▪ Prioritised Backlog

Backlog Grooming Activities

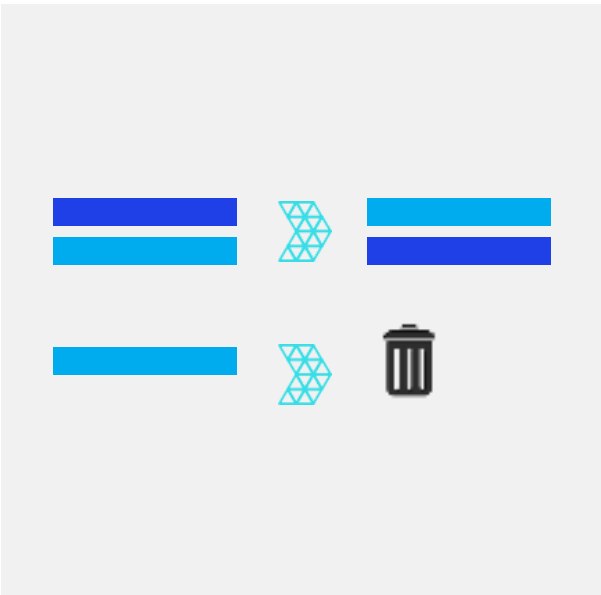

Process Summary

Backlog Prioritization meeting

1. Review each new user story / epic in Back log (Jira filter: issue type in ('idea', 'epic') and created < 14d)
   - Asses relative priority in backlog
   - Update with any relevant information from the meeting
2. Review backlog for any changes required
   - Remove any stories no longer required

SOURCE: McKinsey

Last Modified 11/27/2019 5:46 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Detail of activities and sessions (5/11)

Epics | User Story | Improvement | Idea | Technical Task | Bugs/Investigation

Activities	Description	Participants	Frequency	Inputs	Outputs
E Pre-Sprint Planning	▪ Prioritise user stories to be taken to next sprint by each team	▪ PO (chair) ▪ Backlog owner ▪ Scrum lead ▪ Senior Analyst ▪ Scrum masters	▪ Fortnightly	▪ Prioritised Backlog – Jira agile backlog	▪ Prioritised stories likely to be delivered in the next sprint

Backlog Grooming Activities

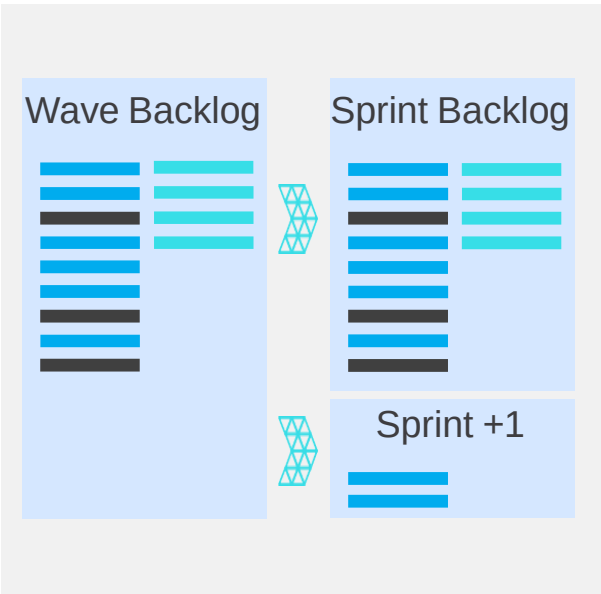

Process Summary

Preparation

1. PO reviews and prioritises backlog (Jira agile backlog)

Pre-Sprint Planning meeting

1. Review top of backlog for stories suitable to deliver
2. Assign to sprints and scrum teams for delivery
3. Identify analysis and technical task to priorities to ensure stories can be delivered

Last Modified 11/27/2019 5:46 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Detail of activities and sessions (6/11)

Epics | User Story | Improvement | Idea | Technical Task | Bugs/Investigation

Activities	Description	Participants	Frequency	Inputs	Outputs
F Detailed analysis	▪ Assign stories to analysts ▪ Further analysis required for each story ▪ Priority to the ones included in the next sprint			▪ Prioritised Backlog – Jira filter: 'Stories not analysed by Priority'	▪ Backlog (Detailed Stories)

Backlog Grooming Activities

Process Summary

1. Analysts review planned Sprints and top of backlog (Jira agile backlog)
2. Focus on analysis of highest priority stories
   - Collaborate with PO (& other experts) to expand requirements
   - Collaborate with scrum teams on technical details
   - Add details to Jira for delivery and acceptance criteria

Last Modified 11/27/2019 5:46 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Detail of activities and sessions (7/11)

Epics | User Story | Improvement | Idea | Technical Task | Bugs/Investigation

Activities	Description	Participants	Frequency	Inputs	Outputs
G Sprint planning	▪ Accordingly to the stories allocated, each team will plan and define the next sprint goals	▪ Scrum master (chair) ▪ Team ▪ Analyst/SME/PO as required	▪ Fortnightly	▪ Team target velocity ▪ Previous wave status ▪ Prioritised Backlog – Jira agile backlog	▪ Incomplete stories returned to the backlog ▪ Sprint Backlog ▪ Team goals

Backlog Grooming Activities

Sprint Backlog



Σ = Target Velocity

Process Summary

1. Calculate target velocity for Sprint (using previous sprint velocities and allowing for team availability)
2. Review each story planned for sprint (Jira Agile: Sprint backlog)
   - Confirm story is able to be taken into Sprint (sufficient understanding, able to deliver)
   - Owner presents story and answers questions from team
   - Estimate delivery effort (planning poker session); update story points
   - Add any comments into Jira relevant to delivery
3. Review relevant priority of tasks in Sprint Backlog
4. Confirm ‘sprint backlog’ by limiting stories to target velocity of Sprint
5. Start new Sprint in Jira (setting start and end dates)

SOURCE: McKinsey

Last Modified 11/27/2019 5:46 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Detail of activities and sessions (8/11)

Epics | User Story | Improvement | Idea | Technical Task | Bugs/Investigation

Activities	Description	Participants	Frequency	Inputs	Outputs
H Sprint (agile development)	▪ Development of the stories assigned to each individual team	▪ Lab	▪ Ongoing	▪ Sprint Backlog	▪ Incremental improved to Solution (e.g., working software) ▪ Updated Sprint Backlog ▪ Escalated issues

Backlog Grooming Activities

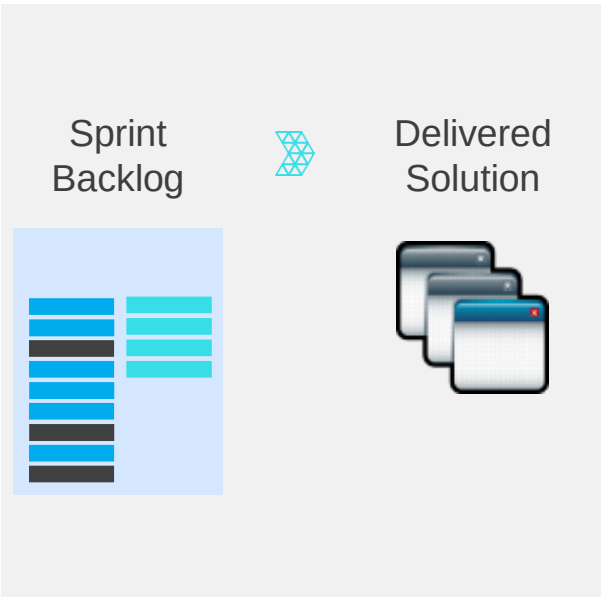

Process Summary

1. Team works on delivery of highest priority tasks in Sprint
2. Review of delivery with analyst and informal coordination with others Labs
3. Daily stand-up to coordinate scrum delivery and escalate issues
4. Scrum of scrums to coordinate Lab delivery and further escalate issues

SOURCE: McKinsey

Last Modified 11/27/2019 5:46 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Detail of activities and sessions (9/11)

Epics | User Story | Improvement | Idea | Technical Task | Bugs/Investigation

Activities	Description	Participants	Frequency	Inputs	Outputs
I Stories acceptance session	▪ Each team presents individually the stories completed so far for PO acceptance/ rejection	▪ PO (chair) ▪ Backlog owner ▪ Scrum lead ▪ Scrum teams (individually)		▪ Stories completed in the sprint	▪ Stories accepted/rejected ▪ Additional user stories, ideas, bugs based on feedback

Backlog Grooming Activities

Feedback from PO



Process Summary

1. Small meeting between PO and scrum team to review scrum team's sprint delivery, briefly discuss
   - Complete stories: also any extra taken in and highlight those to be presented
   - Blocked stories: discuss issues and what needs to be done to progress
   - Incomplete stories: those returning to the backlog for future sprints
2. Demonstrate key delivered user-stories within the solution for the PO to accept or reject
3. Capture feedback and priority (as new item in Jira) as
   - Small changes – Changes need to delivered features
   - New Ideas/Stories – New ideas or user-stories from discussion
   - Bugs – issues identify for investigation
4. Check the delivery process is working (e.g., could solution have been better delivered with more timely feedback or better quality acceptance criteria)

SOURCE: McKinsey

Last Modified 11/27/2019 5:46 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Detail of activities and sessions (10/11)

Epics | User Story | Improvement
Idea | Technical Task | Bugs/Investigation

Activities	Description	Participants	Frequency	Inputs	Outputs
J Sprint Review	▪ Lessons from sprint ▪ Planning next sprint ▪ Communication to wider lab	▪ PO (chair) ▪ Lab	▪ Fortnightly	▪ Sprint stories and goals (scrum teams)	▪ Stories returned to the backlog (not completed in the sprint)

Backlog Grooming Activities

Feedback from PO and Stakeholders

Feedback from Scrum Team

Process Summary

1. Large meeting for the entire to Lab to review progress
   - Sprint Goals – summary of stories and delivery status
   - ‘Shout out’ of major features or news on delivery (demo / slides)
2. Collect any formal/informal feedback from Lab (recorded in Jira)

SOURCE: McKinsey

Last Modified 11/27/2019 5:46 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

Detail of activities and sessions (11/11)

Epics | User Story | Improvement | Idea | Technical Task | Bugs/Investigation

Activities	Description	Participants	Frequency	Inputs	Outputs
K Vision setting (Design Forum)	▪ Setting the vision for the future waves ▪ Re-access the vision and end state for the current wave	▪ PO (chair) ▪ DL ▪ AE ▪ IT arch. lead ▪ CX lead ▪ Bus. arch. Lead ▪ Strategy team elements (1/2)		▪ Vision future waves – topics for discussion ▪ Current wave vision and end state – topics for discussion	▪ Vision future waves (WIP) ▪ Current Wave vision (updated version)

Backlog Grooming Activities

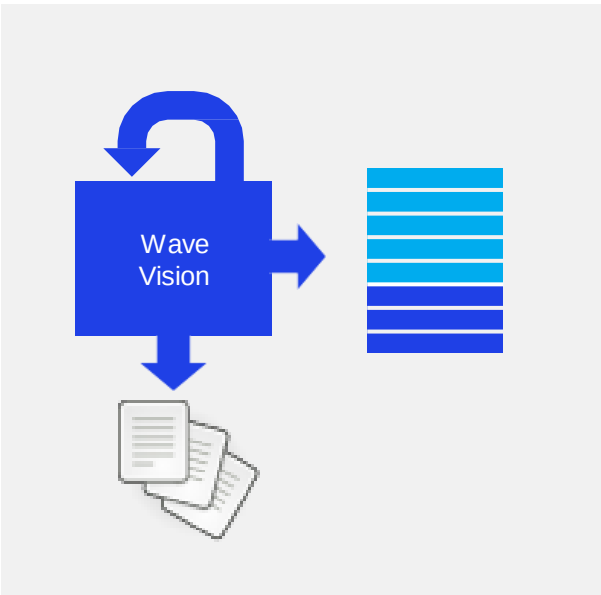

Process Summary

1. Review and refine high-level goals of current and future Waves, including on
   - Internal changes (Business and technical constraints/opportunities)
   - Changes from external influences)
   - Discovery from delivery (including user feedback, analysis and technical input)
2. Update Vision documents to reflect reassessment
3. Analysts create/update any impacted Jira epics/user-stories in current Wave

SOURCE: McKinsey

Last Modified 11/27/2019 5:46 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

What this module covers

To be developed

What are the outputs for each journey during Waves Phase? How should each journey operationalize itself?

- Recap: Phases that each Journey Team undergoes
- C1. Implementation and test
- **C2. Deployment of the solution in the IT infrastructure**
- C3. Roll out of solution to business

Last Modified 11/27/2019 5:46 PM Malay Peninsula Standard Time

Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

IT industrialization team from CIMB is required to support migration of solution to production environment

What is IT industrialization?

- Integration of TCJ solution with CIMB architecture
- Release management
- Infrastructure provisioning
- Service management (e.g., improve performance, increase speed)
- Application support (e.g., fix bugs, handle incidents)

Guiding principles:

30-50% of capacity from CIMB IT subject matter experts dedicated to support TCJ Journey Teams on the IT industrialization activities

Resource requirements may scale up as more features are released into production

Service management and L1-L2 application support for all TCJ solutions should be transitioned to CIMB IT at a defined point

These subject matter experts are **co-located with TCJ Journey Team** to support rapid and frequent releases

Last Modified 11/27/2019 5:46 PM Malay Peninsula Standard Time
Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time

What this module covers

To be developed

What are the outputs for each journey during Waves Phase? How should each journey operationalize itself?

- Recap: Phases that each Journey Team undergoes
- C1. Implementation and test
- C2. Deployment of the solution in the IT infrastructure
- **C3. Roll out of solution to business**

Last Modified 11/27/2019 5:46 PM Malay Peninsula Standard Time

Printed 3/20/2019 2:25 PM Malay Peninsula Standard Time
