About TCJ

Governance

This playbook contains all the pieces and parts that make up our approach to transforming customer journeys. This is a living document and the latest version can be found on TCJ's Confluence site.

Last updated in May 2019

CIMB

How this module fits into overall TCJ Playbook

Guiding principles to TCJ governance

Delivery empowerment at the Squad level:
TCJ Leadership is responsible for defining target (the “what”) while squad has full autonomy to realize said target (the “how”)

Shared outcomes between TCJ and bank:

No overlaps in efforts and decision rights

Simple governance structure with clear guidance from TCJ and bank:
Establish formal governance channels to ensure collaboration and provide mechanisms to raise and resolve issues swiftly. Regular cadence for each forum.

All units work towards same delivery targets:
Squads (delivery units) will deliverables every 12 weeks

Table of Contents

How do we make decisions with the bank?

- **Decision-making bodies**
- Key decision-making processes
- Appendix: CIMB governance committees

TCJ governance bodies

With wider Bank | Within TCJ

Scope	Committee	Purpose	Attendees	Frequency
Program-level	**TCJ Business Review**	▪ Budget allocation based on drawdown approved by DEXCO ▪ Drawdown for all OPEX and CAPEX expenditures below RM1m (within budget) ▪ Overall TCJ program delivery plan (Benefits and timeline by Journey) ▪ Target tech architecture (where applicable across journeys; incl. DevOps, infrastructure, security, test environment) ▪ Vendor assessment ▪ Manage risks and issues at programme level	▪ **Chief Strategy and Design (Chair)** ▪ Group Chief Technology Officer ▪ Group Technology Leads (e.g. EAS, IT Security, App) ▪ Head of TCJ ▪ TCJ Program Director ▪ TCJ Head of Tech Solution Delivery ▪ TCJ Head of Design ▪ TCJ Journey Lead (of Journey in discussion) ▪ Compliance ▪ Audit ▪ Risk ▪ Legal	Monthly
	TCJ Leadership	▪ Resolution of interdependencies and allocation of resources between Journey Teams ▪ TCJ-wide standards (e.g., Tech architecture, industrialization approach, UI/UX guidelines) ▪ Review of benefit delivery and cost for all journeys ▪ Run Quarterly Business Review	▪ **Head of TCJ (Chair)** ▪ TCJ Program Director ▪ TCJ Head of Tech Solution Delivery ▪ TCJ Head of Design ▪ TCJ Journey Team (of Journey in discussion)	Weekly

Journey-level	**Journey Council**	Review:
		▪ Journey-level business case and OKRs
		▪ Benefit delivery and cost for journey
		▪ Key design and delivery decisions
		  ▫ Sub-journeys to be prioritized
		  ▫ Target customer journey
		  ▫ Target technology architecture
		  ▫ Target operational processes
		  ▫ Org transformation
		Resolve:
		▪ Interdependencies with non-TCJ units (e.g. API Dev, Resources from BAU,
		▪ Conflicts between TCJ vs BAU initiatives
		  ▫ Risks and mitigation requirements (incl. security sign-off)
			▪ **Chief Strategy and Design (Chair)**
			▪ **Business Division Head (Chair)**
			▪ Group Chief Technology Officer
			▪ Group Technology Leads (e.g. EAS, IT Security, App)
			▪ Head of TCJ
			▪ Business Department Heads
			▪ TCJ Program Director
			▪ TCJ Head of Tech Solution Delivery
			▪ TCJ Head of Design
			▪ TCJ Journey Team (of Journey in discussion)
			▪ Compliance
			▪ Audit
			▪ Risk
			▪ Legal
				Monthly

	Journey Team Scrums	▪ Detailed design and delivery decision (e.g., release planning and features bundled into each release) ▪ Delivery plan by Wave	▪ **Journey Lead (Chair)** ▪ TCJ Journey Team Members	Daily

Terms of Reference for these bodies are currently being finalized

Table of Contents

How do we make decisions with the bank?

- Decision-making bodies
- **Key decision-making processes**
- Appendix: CIMB governance committees

Deliverables and whether TCJ governance required (1/5)

Current focus for TCJ governance

Phase	Deliverable	Activity	Is decision required outside TCJ?	Existing process that serves TCJ?	Urgency of decision?
0a. Transformation management	Overall TCJ 5-year roadmap	Overall TCJ 5-year roadmap	Y	Syndication with BUs	One-off
		Overall economics of TCJ and investment required			
	Governance	Programme charter	Y	SPM process	One-off
		Project charters	N	SPM process	
		Annual funding for overall TCJ programme	Y	Approved with SPM	Annual
		Funding allocation for Journey Team	N		
		Detailed budget for TCJ	Y	Ongoing effort	
		IT CAPEX and OPEX	Y		
		Non-IT	Y		
		Project	Y		
		Proposal on budget drawdown timing	Y	TBD with Finance	
		Annual hiring plan	Y	F23 People process	
0b. Tech enablement	DevOps	Procure:			
		Alibaba cloud infrastructure (Dev, Staging)	Y	Ongoing	By 1-May
		On premise infrastructure (Pre-prod, Prod)	Y	Ongoing	May-June
		DevOps tools and software	Y	Ongoing	Prioritized list by 1-May
		Vendor contracts	Y		
		Hardware for TCJ developers and designers (e.g., Macbooks)	Y		
	DevOps environment set-up	Set-up and link tools	N		By 1-July
		Penetration /security testing	Y		By 1-July
		Align access rights with CIMB IT policy	Y		By 1-July
		Document operation manuals, training guides	N		Aug onwards
Admin	Resource mobilization	Grant access rights required (e.g.,	Y	Ongoing effort	By 1-June
		VPN access			
		VPC access (* connection to Alibaba cloud and on-prem)			
		MobileIron mobile business email			
		DevOps tools			
		Hardware assignment	Y	Ongoing effort	By 1-June

Deliverables and TCJ governance required (2/5)

Current focus for TCJ governance

Phase	Deliverable	Activity	Is decision required outside TCJ?	Existing process that serves TCJ?	Urgency of decision?
1. Journey - Transformation Design / Pre-work	Final sub-journey roadmap with overall plan by waves	Map sub-journeys	N	Meeting with Group Head, Business Head and Heads of relevant departments	
		Map current IT architecture and existing API	N		
		High-level assessment of impact, feasibility and complexity	N		
		Prioritize sub-journeys with potential impact	Y		Ongoing
		Sign-off wave by wave roadmap	Y		Ongoing
	Cost, FTE, performance and CX baseline				
	Initial blueprint for prioritized sub-journeys	For prioritized sub-journey:	N		
		Map as-is journey, pain points and opportunities			
		Outline high-level implementation plan	N		
		Define KPIs and potential impact	Y		
	Target technology architecture for journey	Create target IT architecture	Y	Meeting with IT EAS and existing dev	
		Architecture implementation roadmap	Y		
	API development	Raise additional API request to CIMB			
		Identify APIs	N		
		Raise request and receive estimate on effort	Y	Challenges expected	May onwards
		Wait for procurement / internal build	Y	Challenges expected	May onwards
	Resource planning	Raise resource request			
		Business SMEs	Y		Ongoing
		CIMB IT	Y		Ongoing
0c. Design strategy		Design guides for channels, product, etc.	N		
		Ownership for each design guide	Y	Discussion needed	May-June

Deliverables and TCJ governance required (3/5)

Current focus for TCJ governance

Phase	Deliverable	Activity	Is decision required outside TCJ?	Existing process that serves TCJ?	Urgency of decision?
2. Journey - Incubate	Target customer journey design using ZBD	Storyboards for customer proposition vision	Y		
		Target customer journey map			
		Target policies and procedures; change from as-is	Y	GPOC committee	During Incubate
	MVP design for development	Product release plan for each wave	N		
		List of features to be developed	N		
		Create and test prototype	N		
		Create design briefs for developers	N		
		Create blueprint of future organization affected	Y	Meeting with BU Head and HODs	
	Refined target architecture	Map desired functionality in architecture	N		
		Identify additional APIs required	N		
		Raise request with CIMB IT	Y		
	Delivery plan	IT development timeline, dependencies/overlaps and critical path	Y	Not available	During Incubate
		Existing digital front-end channels	Y		
		Middleware	Y		
		Back-end systems	Y		
		Operational and org transformation roadmap	Y		
	OKRs and KPIs	Finalize journey-level business case and baseline	Y	Meeting with BU Head and HODs	
		Define squad objective, OKRs and target	N		
		Define KPI for Journey Team members	N		
		Submit project charter for Journey Team	Y	Forward 23 SPM	
	List of risks and mitigations				
	Resourcing for Waves	Outline resource request	N		
		TCJ and vendor	N		
		Business SMEs	Y	Meeting with BU Head and HODs	
		CIMB IT	Y		
	DevOps provisioning	Set up DevOps environment for sub-journey	N		
		Build APIs	N		
		Test and deploy	N		

Deliverables and TCJ governance required (4/5)

Current focus for TCJ governance

Phase	Deliverable	Activity	Is decision required outside TCJ?	Existing process that serves TCJ?	Urgency of decision?
3a. Journey - Waves - Build	Design	Iterate on prototypes			
		Finalize customer testing to validate and refine designs	N		
		Incorporate high-priority customer feedback into backlog	N		
		Finalize design	Y		
	Tech	Determine acceptance criteria	N		
		Build / develop solution	N		
		Ensure development meets teams agreement on DoD	N		
		Design test plan	N		
3b. Journey - Waves - Deploy Technology	Tech	Release management	Y	CIMB IT	
		Infrastructure provisioning	Y	CIMB IT	
		Set up test plan	Y	CIMB IT	
		Architecture review	Y	CIMB IT EAS	
		Staging deployment	Y	Not available	
		Security review / risk assessment	Y	CIMB IT	
		Performance test, i.e. QA Feature/smoke testing approval	N		
		Penetration test and compliance notification (by Deloitte)	Y	External	3 months
		UAT approval	N		
		Go / No-go approval for deployment	N		
	Plan for next Wave	Groom backlog	N		

Deliverables and TCJ governance required (5/5)

Current focus for TCJ governance

Phase	Deliverable	Activity	Is decision required outside TCJ?	Existing process that serves TCJ?	Urgency of decision?
3b. Journey - Wave - Deploy business	Preparation	Create Model Office approach / adoption of target policy and procedures	Y		
		Customer communications	Y		
		Training manual for operations	Y		
		Change in incentives	Y		
		Set up metrics and tracking mechanism during deployment	N		
		Outline risks and mitigations	Y		
	Pilot to validate learning on benefits	Review success metrics for pilot	N		
		Go / no-go decision for further roll-in	Y		
		Refine new processes	N		
	Scale-up of pilot	Finalize new process	Y		
		BNM compliance notification of new process	Y		
		Set up metrics and tracking mechanism after full deployment	N		

All of these topics are addressed in current GPOC Submission Form.

In summary, we identified six focus areas for TCJ governance

Decision-making process requiring intervention	Question to be solved	Next steps	Owner
a. Funding	▪ Does the process for ongoing approval of drawdown need to be simplified? ▪ If so, does the bank allow for separate, simplified process for TCJ?	▪ TBD	
b. Technology – API development	▪ How will TCJ resolve dependencies on CIMB IT for API development ▫ Development capacity constraints ▫ Budgetary support needed for API development	▪ Discussion with CTO ongoing	
c. Changes to policy and procedures	▪ At which stage of the Journey Lifecycle should TCJ interact with GPOC? ▪ Can GPOC processes support TCJ's test and learn approach (e.g., pilots and iterative process changes)?	▪ N/A – Dedicated Compliance resource being onboarded	TBD
d. Design	▪ What is the existing process to align on design standards? ▪ How will TCJ design standards be aligned with existing design governance?	As part of first journey Incubation: 1. Designers to establish 'Design System', incl. mapping the gaps in current style guide document and improvements needed 2. Align 'Design System' with existing bank stakeholders (incl. Customer Experience department, CIMB Clicks) 3. Cascade 'Design System' to from TCJ Head of Design to Journey Design Leads 4. Set up cadence within Design chapter to align on 'living document' additions and approvals during Delivery	Design stream (Led by Kim Mueller)
e. Technology – Digital front-end channels	▪ How should TCJ interact with existing digital front-end channels on: ▫ Backlog prioritization ▫ Provisioning of testing environment ▫ Coding standards ▫ Release management ▫ Service management and incident management ▫ Resourcing	▪ N/A – Scrum of Scrums cadence to be adopted	
f. Technology – Deployment	▪ What are the dependencies from bank during deployment process? ▪ What are the external dependencies (e.g. BNM) during deployment process? ▪ How will these dependencies be managed with frequent release cycles?	As part of first journey Incubation: ▪ Detail out "go-live" process during TCJ Waves ▪ Understand internal compliance requirements (incl. Risk Plan) ▪ Understand external compliance requirements (pending Scope of Work from Deloitte) and create plan for addressing	

a. Funding – as-is

Question for TCJ Governance:

Does the process for ongoing approval of drawdown need to be simplified?

If so, does the bank allow for separate, simplified process for TCJ?

As-is process

- Funding: Approved on an annual basis by Forward 23 SPM. In Oct of each year, TCJ must prepare the request form for SPM for funding of the next year.
- Detailed budgeting: After total fund is approved, TCJ allocates total fund by line item. The allocation then approved by respective BAU committees (e.g., IT by IT Strategic Committee (ITSC)
- Drawdown of budget for each purchase:
  - IT CAPEX and OPEX:
    - <RM100K is approved by Head of TCJ
    - <RM1 Mn is approved by Chief of Strategy and Design
    - RM1-3 Mn is approved by ITPC
    - >RM3 Mn is approved by ITSC
  - Non-IT CAPEX and OPEX:
    - A sum of OPEX per period of time is pre-approved with Finance
    - Drawdown from TCJ OPEX budget code does not require approvals per transaction.

Challenges for TCJ

- Lengthy process involving multiple approvals and touchpoints for each procurement. This raises challenges to meet TCJ delivery timeline
- TCJ Journey Teams may also have emerging procurement requirements arising during delivery, as new needs are identified during Planning and Incubation Phase

a. Funding – to-be

Question for TCJ Governance:

Does the process for ongoing approval of drawdown need to be simplified?

If so, does the bank allow for separate, simplified process for TCJ?

Process required by TCJ (as seen at other Digital Factories)

- Funding: Approved on an annual basis
- Detailed budgeting: After total fund is approved, TCJ allocates total fund by spend category.
  - Principle: only lock figures that are really needed (e.g. spend per vendor; profit forecast per quarter), leave rest flexible
- Drawdown of budget for each purchase:
  - "Charge-code" is approved quarterly, by spend category

Line item	TCJ_Q1	TCJ_Q2	TCJ_Q3	TCJ_Q4
IT CAPEX	$10	…	…	…
People	$20	…	…	…
Facilities	$5	…	…	…

- Budgeted amount is spent and managed by TCJ. Deep-dive in next page.

Next steps for TCJ:

1. **Discuss funding** and draw-down process with SPM, DEXCO and Finance
2. Identify dedicated Finance capacity (with CIMB context) to support TCJ to establish this new process

Deep-dive: Budgeting process as seen at other Digital Factories

TCJ org levels	Decisions	Example: How resources are allocated at each level		
		Description	**Accountability**	**Frequency**
TCJ Leadership	Strategic level	▪ **TCJ Leadership establishes budget** for following year (per Journey Team) based on macroeconomics forecasts as well as objectives from Group level ▪ Principle: only lock figures that are really needed (e.g. spend per vendor; profit forecast per quarter), leave rest flexible	Management team is the only one responsible for "full" P&L	Yearly
Journey Team Leadership	Tactical	▪ In each Quarterly Business Review, Journey Team updates strategic priorities for next 3 months, which are translated into Journey OKR ▪ **Resources (FTE + discretionary budget) are allocated to each Journey Team quarterly** based on the OKR they commit to ▪ If needed, resources are reallocated to other Journey Teams	Journey Leads (along with TCJ Central Team) refine resource allocation each quarter	Quarterly
Squad(s)	Operational	▪ **Journey Lead assigns resources** (FTE and discretionary budget) between squads, often in a dynamic / non-formal process ▪ If needed, resources can also be re-allocated to other squads	Journey Leads are responsible to reach their OKR and to assign/ redistribute resources accordingly	Continuous

b. Technology – API development

Question for TCJ Governance:

How will TCJ interact with CIMB IT to ensure that development capacity (either CIMB IT or third-party) is available to meet TCJ release plan?

How will the budgeting process support ongoing API development requests?

As-is process

Current API request process and activities

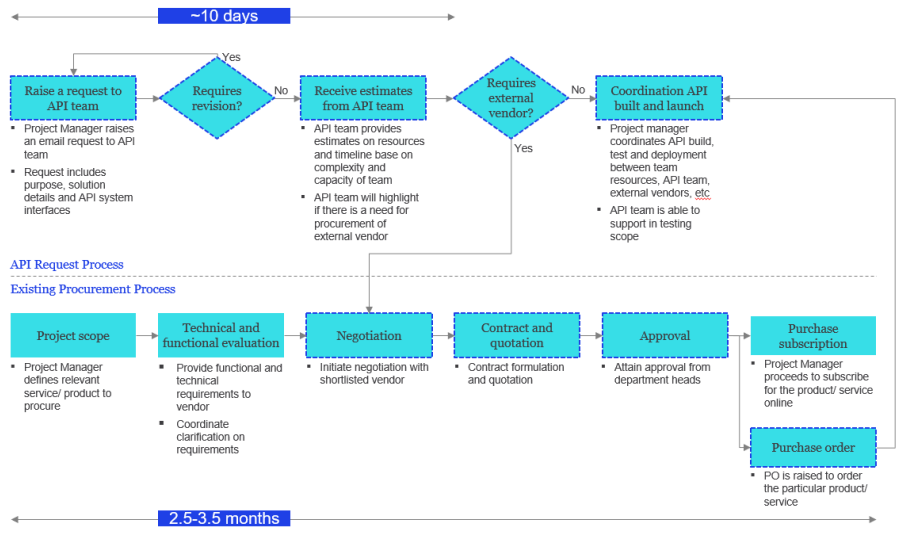

- TCJ API development will be dependent on CIMB IT capacity and procurement timelines

Process required by TCJ

TCJ Journey Team will provide requests to EAS in three key touchpoints:

- Design phase: Provide high-level API requirements to get estimate for budgeting purpose
- Incubate phase: Provide low-level design of APIs to begin development (either through CIMB IT or third-party vendor)
- Waves: Onboard APIs in development as scheduled; API development team joins 'Scrum of scrums' meeting to solve interdependencies

Next steps for TCJ

1. **Establish Operating Level Agreement** with CIMB IT Enterprise Architecture Solutioning team (for e.g., TAT for first response, response with plan, onboarding of development team after API list provided)
2. **Appoint dedicated SPOC** from EAS
3. (optional) **Dedicate CIMB IT resources** to TCJ to support
4. **Discuss financing of new API development:**
   - Leverage existing budgetary support with CIMB IT
   - TCJ to support and undertake expenditure

c. Changes to policy and procedures

Question for TCJ Governance:

At which stage of Journey Lifecycle should TCJ interact with GPOC?

Can GPOC committee processes support TCJ's test and learn approach (e.g., pilots and iterative process changes)

As-is process

- GPOC charter:
  - Review CIMB Group's new or changed policies; new or material changes to procedures; and new product/ material variation to/retirement of existing product proposals
  - Review and recommend to the Boards the framework within which the Group Policies and Procedures are approved and maintained.
- GPOC convenes fortnightly to table submissions across the Ban; approvals require multiple rounds of clarifications
- Members include: representatives of Group Compliance and Legal for each BU, Head of Operations, Head of CX, representative from Finance.
- Project team has to complete GPOC Submission Form or GPOC Notification Template including
  - Assessment of impact to staff
  - Channel operations or customer
  - Staff readiness and communication method
  - System readiness
  - Risk assessment.
- Scope of assessment depends on whether a change is considered material or non-material (guidelines for classification provided by Compliance)

Process required by TCJ

- Representative of all departments affected joins a monthly Journey Team working group to make any decisions that cannot be made by TCJ members.

Next steps for TCJ

Onboard dedicated Compliance Subject Matter Expert in May

Scope of work during Incubate phase:

- **Adapt assessment templates** for Journey Teams to use towards end of Incubate phase (after target journey is aligned upon)
- Support journey team in completion of documentation and procedural requirements from GPOC and/ or other compliance approval perspective
- **Evaluate and guide on developing a flexible sign-off process** which allows for rapid, iterative test, learn and deploy approach

d. Alignment on design standards

Question for TCJ Governance:

What is the existing process to align on design standards?

How will TCJ design standards be aligned with existing design governance?

As-is process

- Design changes are made and **approved within each Project Committees**
- **Bank Customer Experience department is consulted as needed**
- In addition, there is a **UI/UX Design Standards document for digital platforms** (e.g., CIMB Clicks) and is referred to by all project teams.

Process required by TCJ

- **'Design System' is set up as a single source of truth** for all Journey Teams, to ensure streamlined omnichannel experience from design point of view
- Design System consists of:
  - Reusable components that can be used for any number of applications
  - Clear standards and guiding elements, incl. Design Philosophy, language, grammar, personas

Next steps

1. Designers to **establish 'Design System',** incl. mapping the gaps in current style guide document and improvements needed
2. **Align** 'Design System' **with existing bank stakeholders** (incl. Customer Experience department, CIMB Clicks)
3. **Cascade 'Design System'** to from TCJ Head of Design to Journey Design Leads
4. **Set up cadence within Design chapter** to align on 'living document' additions and approvals during Delivery
5. Developers to **co-create code base** and agree on how and where to set-up

d. What is a Design System?

Advantages of a Design System [1]

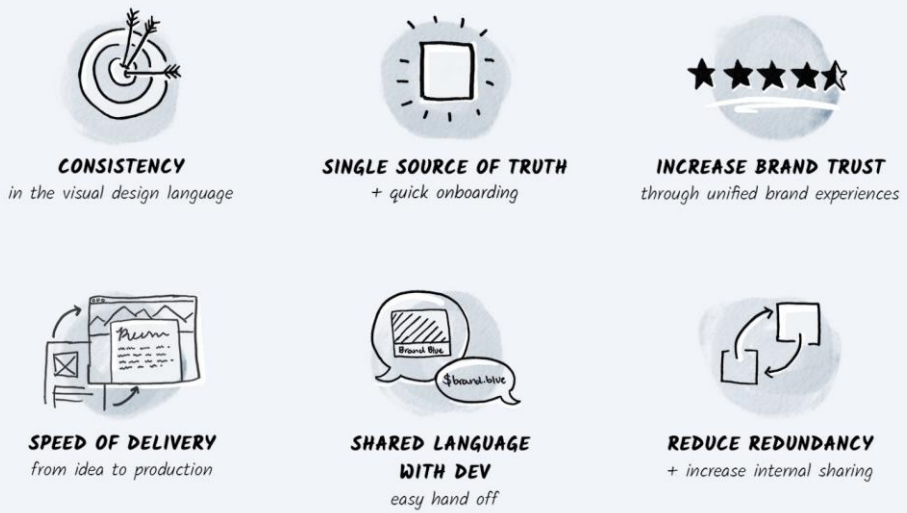

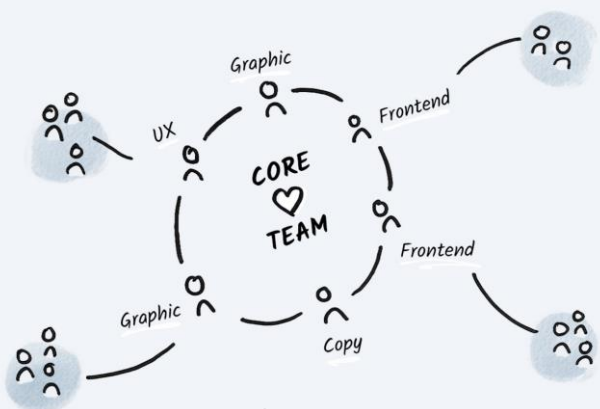

A Design system contains of reusable components, guided by clear standards, that can be assembled together to build any number of applications

- Reusable components to build pages
- Colors, typography, sizing, spacing (grids), Imagery, icons
- … can be extended to any other guiding elements, such as: Design Philosophy, language, grammar, personas….
- Visualized automatically components from production

"Completeness is not the goal"

- Will evolve over time
- Designers and developers alike should be able to update as much of the system as possible



IBM



Atlassian

1- source: medium.com

d. Typical design governance in Digital Factories

Journey Phase	Typical role of design governance	Description	Current responsibility	Proposed future responsibility
Incubate	Provide design guidance	▪ **Develop 'Design System'** to be used by all Journey teams ▪ Includes design philosophy, components and source code for all front-end channels as one single source of truth ▪ 'Living document' additions and approvals during Delivery	Within channel teams (e.g., CIMB Clicks)	TCJ Head of Design (after alignment with Bank CX team)
	Review and approve design	▪ Detailed **review of to-be journey design** during incubation phase (incl. visual assets, user flow); to ensure consistency and alignment with design principles ▪ Go/no-go recommendation for development	Project Steering Committee[1], Bank CX team may be consulted if needed	Journey Design Lead[2] (after consulting TCJ Head of Design)
Waves (Develop-ment)	Confirm alignment with Operating Model	▪ **Impact** assessment of design on divisional operating model ▪ Identification of potential dependencies with other BU-led initiatives	Project Steering Committee	Journey Design Lead to gather inputs; present to Journey Team Working Group[3]
	Resolve roadblocks and issues	▪ **Resolve key design issues** and address design roadblocks	Project Steering Committee	TCJ Head of Design to liaise with other stakeholders
Waves (Deploy-ment)	Control change	▪ Design audit to ensure **acceptable customer and colleague impact before implementation;** and fit with banks strategy	Project Steering Committee	Journey Design Lead to gather inputs; present to Journey Team Working Group

1 Committees formed for each project (e.g., Project to consolidate three apps into main Clicks app); composed of Business, IT and vendor
2 TCJ organization structure includes Journey Designers at Journey Team-level, all of which report to Head Design at TCJ program-level
3 Proposed governance committee for each Journey Team, to include Chief of BU Division, Chief of Compliance/Risk/Legal, Representative from IT

e. Technology – Digital front-end channels

Question for TCJ Governance:

How should TCJ interact with existing digital front-end channels on:

- Backlog prioritization
- Provisioning of technology environment for testing and development
- Coding standards
- Release management
- Service management and incident management
- Resourcing

As-is process

- Current channels are standalone with separate roadmap of improvements and resources. Meanwhile, TCJ will need to coordinate its release plans with these teams.
- The channels largely deploy using waterfall models, where releases are at end of the project and requirements are defined at the beginning. Meanwhile, TCJ has frequent releases and requirements are expected to change throughout lifecycle

Emerging hypothesis

- Three interaction models laid out:
  - 'Scrum of scrums'
  - Ring-fenced BAU capacity + dotted line from Channel PO to TCJ
  - Entire channel subsumed into TCJ
- Given CIMB context and learnings from other Digital Factories, TCJ would likely use the first option ('scrum of scrums').
  - This is mainly because BAU channel team covers many other elements that are out of scope for TCJ.
  - However, both teams are aligned by same unit and shared objective
- Hence, requirements from existing channel teams:
  - Each channel dedicates one PO to attend our Journey Team 'Scrum of scrums'
  - With each channel PO, upfront alignment needed on DevOps, codebase accountability, etc.

f. Technology Deployment

Question for TCJ Governance:

- What are the **dependencies from bank** during deployment process?
- What are the **external dependencies** (e.g. BNM) during deployment process?
- How will these dependencies be **managed with frequent release cycles?**

Pre-requisites to tackle:

- TCJ test environment

Steps:

1. Detail out go-live process for TCJ Waves
2. Compare with CIMB as-is and identify dependencies between TCJ and CIMB IT environment during development, test and deployment, incl.
   - Risk plan
3. Understand external compliance requirements (pending Scope of Work from Deloitte) and create plan for addressing

Week

- TBD

Output

- List of sign-offs required from CIMB IT and Business, incl.
  - Stage of deployment
  - Person-in-charge
  - Format (form vs. email vs. DevOps tool)
- Attendees and cadence for Scrum of Scrum meetings
  - Appointed representative of each System involved

As-is CIMB software development lifecycle

3.1 Requirement analysis (REQ)	3.2 Design (DES)	3.3 Build & unit test (BUT)	3.4 System test (ST)	3.5 System & integration Test (SIT)	3.6 User acceptance test (UAT)	3.7 Deploy (DPY)
▪ FSD ▪ RTM ▪ IMAC pack ▪ EUC pack	▪ ADD ▪ DR pack	▪ Test plan ▪ Test sign-off	▪ Code review	▪ Test sign-off	▪ Test sign-off	▪ Set-up production environment ▪ Change management for production deployment ▪ OAT, VA, PT and ORT

Table of Contents

How do we make decisions with the bank?

- Decision-making bodies
- Key decision-making processes
- **Appendix: CIMB governance committees**

“As-is” landscape of key governance bodies that TCJ will interact with (1/2)

Scope	Governance bodies	Description	Cadence	Participants	Level
Forward 23 program	**Transformation Council (TC)**	Steer Forward23 programmes and set goals; ensure continued alignment to strategy	1x monthly	CEO, COO, Group People, Group Strategy, Group Risk	GMC
	Project Steering Committee	Track progress and advise on resolution of risks, issues, inter-dependencies	1x monthly	Head of TCJ	GMC, GMC-1
	Strategic Program Management		…	…	…
IT	**Group IT Strategy Committee (GITSC)**	Approve IT CAPEX and OPEX >3Mn; Changes to CIMB IT architecture; Ensure IT is aligned with strategic plans.	Monthly	COO, Chief Tech, Chief of BUs, Compliance, Strategy	GMC, GMC-1
	Group IT Strategy Committee (GITPC)	Approve IT CAPEX and OPEX <RM1-3Mn	Monthly	CFO, Tech, BUs, Compliance, Strategy; Procurement	GMC-2
	Group Solution Review Council (GSRC)	…	…	…	…
Risk & Compliance	**Group Policy and Procedure Oversight Committee (GPOC)**	Changes of product, policy and frameworks	Fortnightly	Representative of Group Compliance for each Business Unit, Operations, CX, Finance	Working level
	Group Operational and Resiliency Risk Committee (GORRC)	…	…	…	GMC
Business Unit	**Business Unit Management Committee** (e.g. Commercial Banking Malaysia Management Committee, Consumer, Wealth Management)	Strategy and direction, budgets, product offerings	…	Heads of Departments	GMC-2
	Consumer Banking Incentive & Rewards Committee	Sales incentives	…	…	

“As-is” landscape of key governance bodies that TCJ will interact with (2/2)

Scope	Governance bodies	Description	Cadence	Participants	Level
Design	**Group Customer Experience Council**	Assist	…	Group-wide (incl. outside Malaysia)	GMC, GMC-1
	Group Brand Strategy and Alignment Council	…	…	…	…
	…		…	…	…
Procurement	**Group Vendor Outsourcing Committee (GVOC)**	Oversee outsourcing risks (incl. people, licenses)	Monthly	Corporate Development, OSP Governance, Risk, Legal, T&O Governance, CFO	GMC-2
People	**Manpower Planning**	Hiring budgets	…	…	…
	Group Human Resource Committee	…	…	…	GMC-1
